


PROJECT BRIEF

PROJECT TITLE	:	CONSTRUCTION OF PORT OPERATIONS BUILDING
LOCATION	:	PORT OF ORMOC, ORMOC CITY, LEYTE
CONTRACTOR	:	DAKAY CONSTRUCTION & DEVELOPMENT CORPORATION
SCOPE OF WORK	:	A. PORT OPERATION BUILDING (AREA = 1,975.92 SQ.M.)
DATE OF BIDDING	:	15 December 2015
DATE OF AWARD	:	17 February 2016
DATE OF NOTICE TO PROCEED	:	12 May 2016
CONTRACT DURATION	:	390 <i>calendar days</i>
APPROVED BUDGET AMOUNT	:	₱49,163,562.80
SOURCE OF FUNDS	:	PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	:	PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	:	₱47,845,978.90
RECAPITULATION	:	₱1,867,879.54 Covering the variance of the pre-determined quantities indicated in the Bill of Quantities (BOQ) as bid as against the actual quantities measured after the completion of the project.
REVISED CONTRACT AMOUNT (Final Revision)	:	₱49,713,858.44
EFFECTIVITY DATE	:	19 May 2016
ORIGINAL EXPIRY DATE	:	12 June 2017
TIME EXTENSION NO. 1 / TIME ADJUSTMENT NO. 1	:	360 <i>calendar days</i> Covering the delays brought about by the issued on suspension/ resumption orders and late removal of existing structures located within the new location of the POB.
REVISED EXPIRY DATE (First Revision)	:	08 March 2019
TIME EXTENSION NO. 2	:	61 <i>calendar days</i> Covering the unworkable days caused by bad weather condition for the period from 14 March 2018 to 25 February 2019.
LATEST REVISED EXPIRY DATE (Second Revision)	:	08 May 2019
PROJECT STATUS	:	- Completed on 20 November 2020.
REMARKS:	:	- As-built plans was approved on 26 February 2021 - Recapitulation was approved on 18 March 2021.

CONSTRUCTION OF PORT OPERATIONS BUILDING PORT OF ORMOC, ORMOC CITY, LEYTE

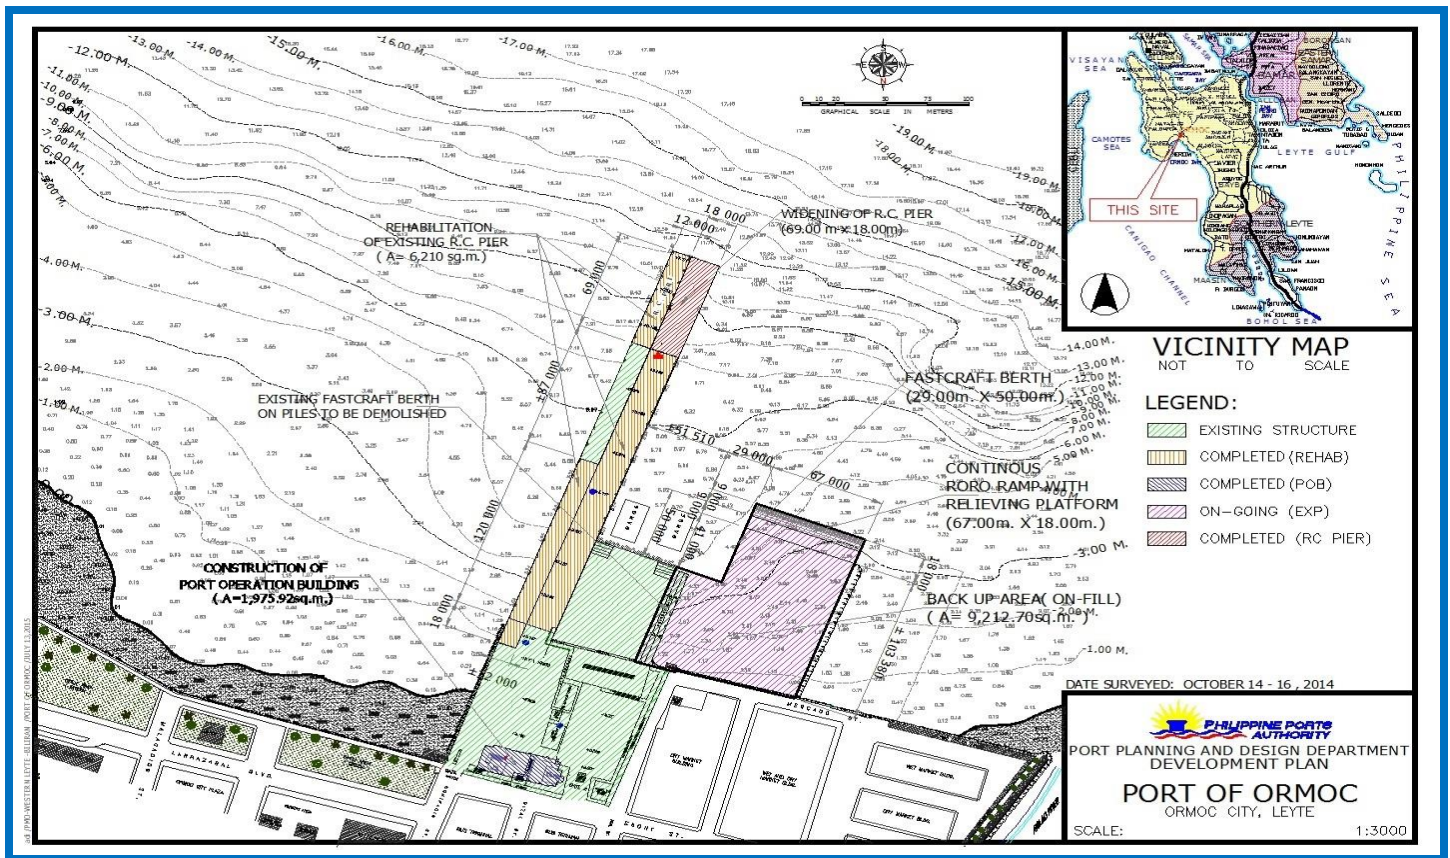

DEVELOPMENT PLAN




AFTER CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	: EXTENSION OF RC WHARF
LOCATION	: PORT OF GUIUAN, EASTERN SAMAR
CONTRACTOR	: JSP BUILDER'S AND GENERAL MERCHANDISE
SCOPE OF WORK	: A. EXTENSION OF RC WHARF B. MOORING AND FENDERING SYSTEM
DATE OF BIDDING	: 07 September 2017
DATE OF AWARD	: 28 September 2017
DATE OF NOTICE TO PROCEED	: 10 November 2017
CONTRACT DURATION	: 270 <i>calendar days</i>
APPROVED BUDGET AMOUNT	: ₱24,524,056.36
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱23,871,127.50
EFFECTIVITY DATE	: 20 November 2017
ORIGINAL EXPIRY DATE	: 16 August 2018
TIME EXTENSION NO. 1	: 190 <i>calendar days</i> Covering the time elapsed of the suspended period caused by issues and concerns relative to the issuance of ECC.
LATEST REVISED EXPIRY DATE (First Revision)	: 15 August 2019
PROJECT STATUS (As of 25 January 2023)	: - Completed on 15 July 2022.
REMARKS:	: - Liquidated damages will be imposed and to be deducted from the final billing claim. - As-built plans and recapitulation are under preparation.

EXTENSION OF RC WHARF PORT OF GUIUAN, EASTERN SAMAR

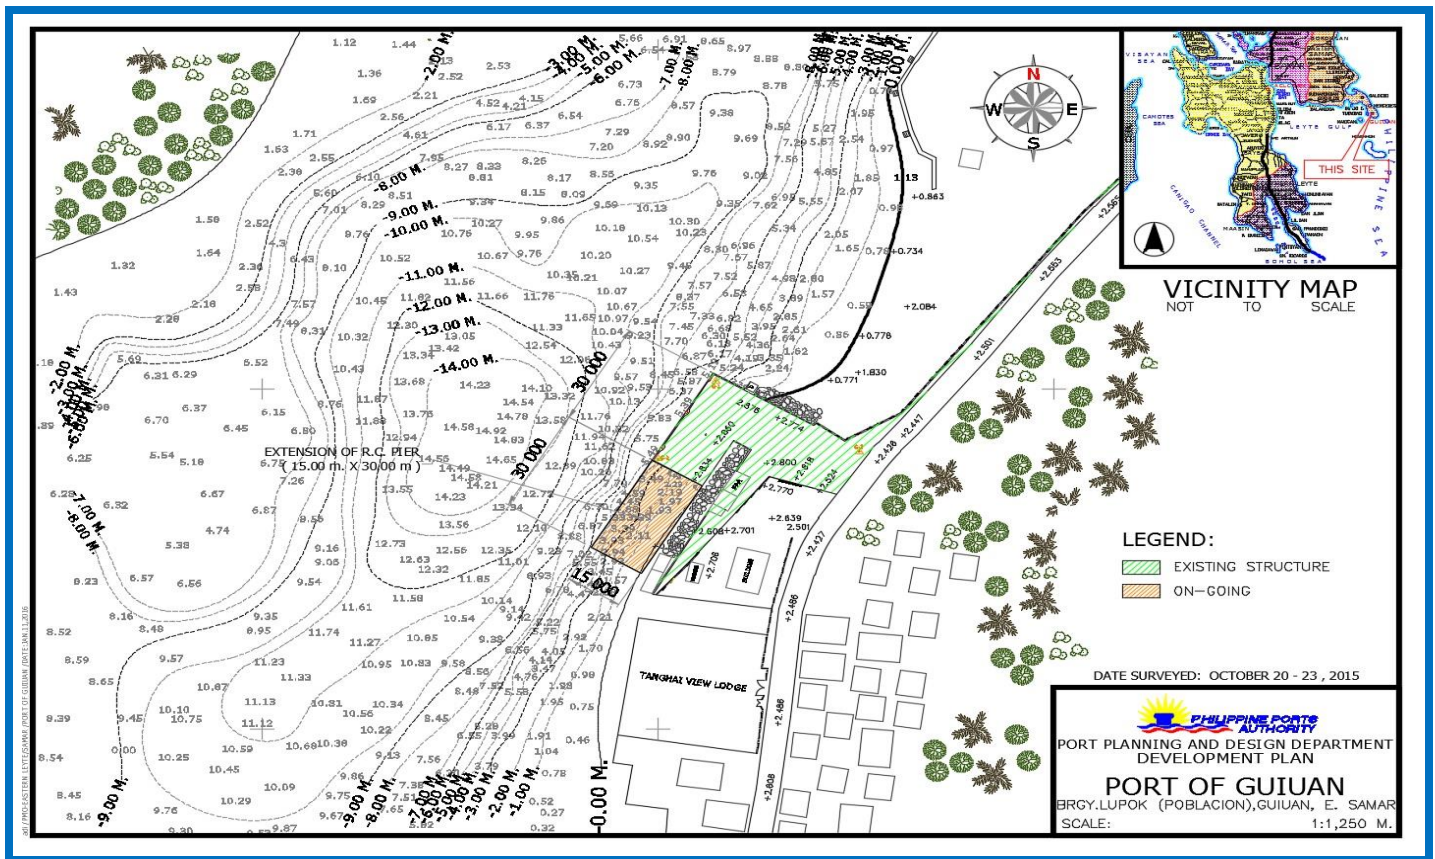

DEVELOPMENT PLAN




AFTER CONSTRUCTION


PROJECT BRIEF

PROJECT TITLE	:	MARIBOJOC PORT IMPROVEMENT PROJECT
LOCATION	:	PORT OF MARIBOJOC, MARIBOJOC, BOHOL
CONTRACTOR	:	PREMIUM MEGASTRUCTURE, INC./ ULTICON BUILDERS, INC. - J.V.
SCOPE OF WORK	:	A. IMPROVEMENT OF EXISTING ROCK CAUSEWAY (AREA = 1,823.96 SQ.M) B. CONSTRUCTION OF BACK UP AREA WITH RORO RAMP ON FILL (AREA = 6,304.98 SQ.M) C. CONSTRUCTION OF BREASTING DOLPHIN D. PORT LIGHTING SYSTEM
DATE OF BIDDING	:	21 November 2017
DATE OF NOTICE TO PROCEED	:	04 March 2018
CONTRACT DURATION	:	690 <i>calendar days</i>
APPROVED BUDGET AMOUNT	:	₱485,806,838.39
SOURCE OF FUNDS	:	PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	:	PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	:	₱480,948,770.01
RECAPITULATION	:	-₱9,322,301.39 Covering the variance of the pre-determined quantities indicated in the Bill of Quantities (BOQ) as bid as against the actual quantities measured after the completion of the project.
REVISED CONTRACT AMOUNT (Final Revision)	:	₱471,626,468.62
EFFECTIVITY DATE	:	12 March 2018
ORIGINAL EXPIRY DATE	:	30 January 2020
TIME EXTENSION NO. 1	:	113 <i>calendar days</i> Covering the delays incurred by the project brought about by the unworkable bad weather/rough sea condition for the period 12 March 2018 to 31 January 2019.
REVISED EXPIRY DATE (First Revision)	:	22 May 2020
TIME EXTENSION NO. 2/ TIME ADJUSTMENT NO. 2	:	272 <i>calendar days</i> - Covering the delays brought about by suspension of reclamation activities due to issues and concerns with Philippine Reclamation Activities (PRA) was approved on 16 October 2020.
REVISED EXPIRY DATE (Second Revision)	:	18 February 2021
LATEST TIME EXTENSION NO. 3	:	41 <i>calendar days</i> - Covering the time elapsed due to unworkable bad weather conditions.
REVISED EXPIRY DATE (Third Revision)	:	31 March 2021
PROJECT STATUS (As of 25 December 2021)	:	- Completed as of 25 June 2021.
REMARKS:	:	- Recapitulation was approved on 07 December 2021.

MARIBOJOC PORT IMPROVEMENT PROJECT PORT OF MARIBOJOC, MARIBOJOC, BOHOL

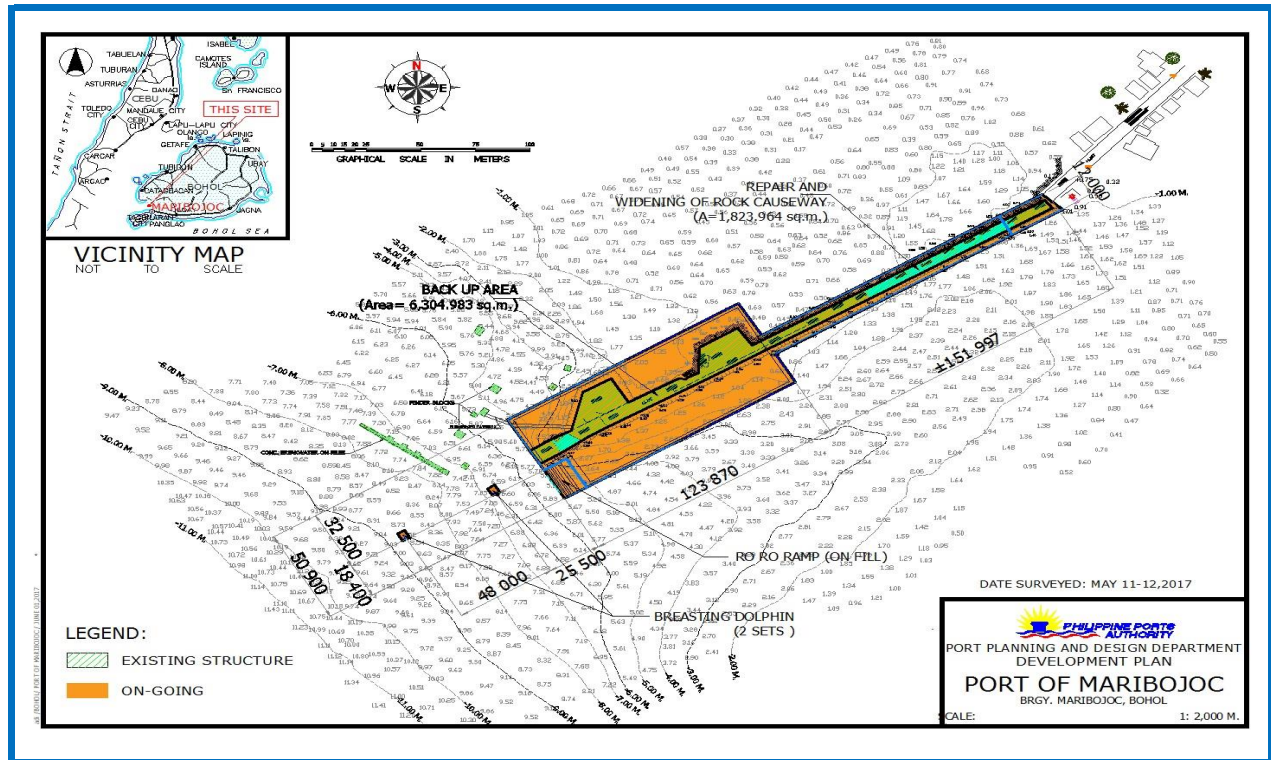

DEVELOPMENT PLAN

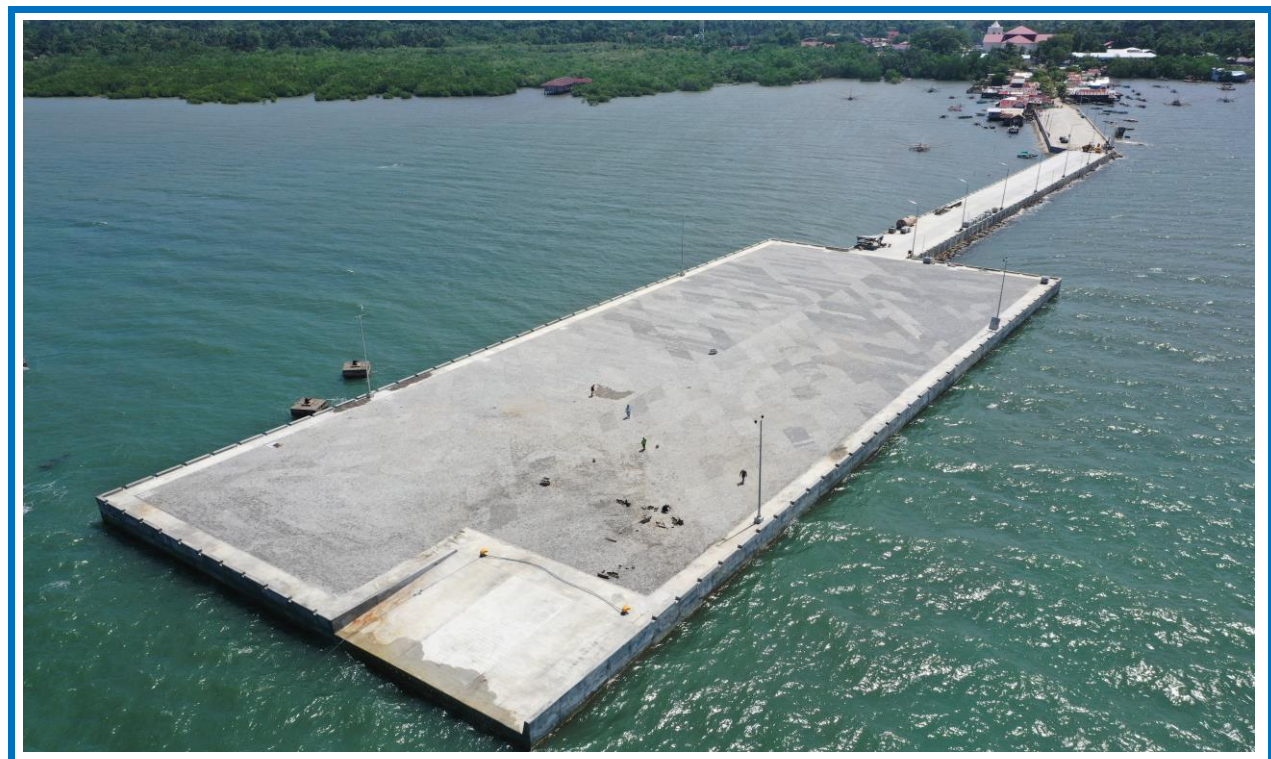


AFTER CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	:	CONSTRUCTION OF PORT OPERATIONS BUILDING
LOCATION	:	PORT OF DUMAGUETE, DUMAGUETE CITY NEGROS ORIENTAL
CONTRACTOR	:	A5R DYNAMICS CONSTRUCTION CORPORATION
SCOPE OF WORK	:	A. CHB FENCE, DEMOLITION & REMOVAL B. PORT OPERATIONS BUILDING
DATE OF BIDDING	:	17 April 2018
DATE OF AWARD	:	23 May 2018
DATE OF NOTICE TO PROCEED	:	21 June 2018
CONTRACT DURATION	:	420 calendar days
APPROVED BUDGET AMOUNT	:	₱112,670,064.39
SOURCE OF FUNDS	:	PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	:	PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	:	₱110,545,812.42
EFFECTIVITY DATE	:	28 June 2018
ORIGINAL EXPIRY DATE	:	21 August 2019
VARIATION ORDER NO. 1 (Change Order No.1/Extra Work Order No.1)	:	₱4,388,510.68 Covering the quantity adjustments of some of the original items of work and additional work as called for by the approved revised/modified interior partitions wall and relocation of existing power transformers affected by sites development.
REVISED CONTRACT AMOUNT (First Revision)	:	₱114,934,323.10
TIME EXTENSION NO. 1	:	98 calendar days Covering the delays brought about by late removal/transfer of office equipment/personnel from the existing building to be demolished to the new temporary office and unworkable bad weather condition for the period June 28, 2018 to March 25, 2019.
REVISED EXPIRY DATE (First Revision)	:	27 November 2019
TIME EXTENSION NO. 2	:	30 calendar days Due to Variation Order No. 1
REVISED EXPIRY DATE (Second Revision)	:	27 December 2019
PROJECT STATUS	:	- Completed on 15 October 2020.
REMARKS	:	- As-built plans was approved on 24 May 2021 and recapitulation was approved on 02 June 2021.

CONSTRUCTION OF PORT OPERATIONS BUILDING PORT OF DUMAGUETE, DUMAGUETE CITY, NEGROS ORIENTAL

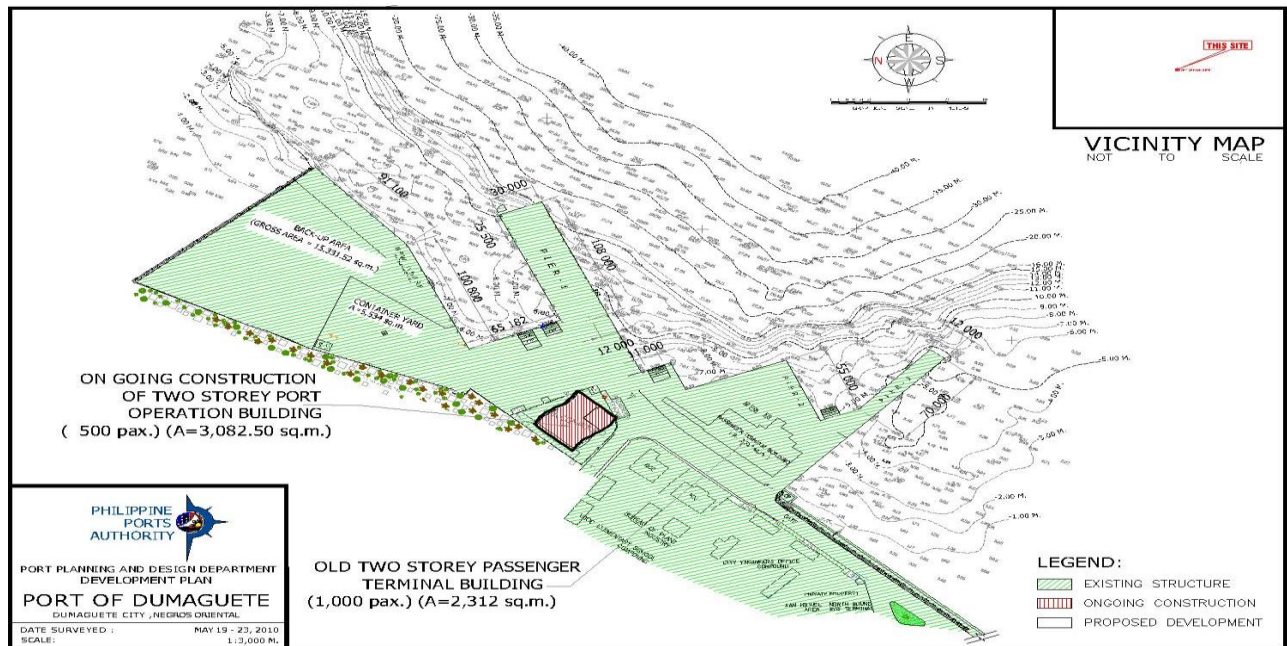

DEVELOPMENT PLAN



AFTER CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	:	CONSTRUCTION OF PASSENGER TERMINAL BUILDING (PTB)
LOCATION	:	PORT OF TAGBILARAN, BOHOL
CONTRACTOR	:	REX E. MORALES CONSTRUCTION
SCOPE OF WORK	:	A. DEMOLITION AND REMOVAL WORK B. PASSENGER TERMINAL BUILDING
DATE OF BIDDING	:	10 January 2018
DATE OF AWARD	:	30 January 2018
DATE OF NOTICE TO PROCEED	:	12 April 2018
CONTRACT DURATION	:	420 calendar days
APPROVED BUDGET AMOUNT	:	₱70,414,112.12
SOURCE OF FUNDS	:	PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	:	PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	:	₱68,988,264.86
EFFECTIVITY DATE	:	24 April 2018
ORIGINAL EXPIRY DATE	:	17 June 2019
VARIATION ORDER NO. 1 (Change Order No.1/Extra Work Order No.1)	:	₱6,714,857.60 Covering the quantity adjustment of some of the original item of works and additional works for the proposed expansion of the on-going passenger terminal building, demolition of existing structure and removal of existing water tank.
REVISED CONTRACT AMOUNT (First Revision)	:	₱75,703,122.46
RECAPITULATION	:	(2,844,136.64) Covering the variance of the pre-determined quantities indicated in the Bill of Quantities (BOQ) as bid as against the actual quantities measured after the completion of the project.
REVISED CONTRACT AMOUNT (Final Revision)	:	₱72,858,985.82
TIME EXTENSION NO. 1	:	76 calendar days Covering the unworkable days caused by bad weather condition and busy port operations for the period from 24 April 2018 to 25 February 2019.
REVISED EXPIRY DATE (First Revision)	:	01 September 2019
TIME EXTENSION NO. 2	:	123 calendar days Covering the delays brought about by unworkable days caused by bad weather condition and port operation for the period 26 Feb to 25 August 2019.
REVISED EXPIRY DATE (Second Revision)	:	02 January 2020

TIME EXTENSION NO. 3

: **69 *calendar days***

Covering the delays brought about by unworkable days caused by bad weather condition and port operation for the period 26 August 2019 to 02 January 2020.

REVISED EXPIRY DATE

(Third Revision)

: **11 March 2020**

TIME EXTENSION NO. 4

: **72 *calendar days***

Covering the delays caused by the unworkable weather condition and time elapsed of the suspended period caused by the imposition of Enhanced Community Quarantine (ECQ) brought by COVID-19 crisis.

REVISED EXPIRY DATE

(Fourth Revision)

: **22 May 2020**


PROJECT STATUS

: - Completed on 31 October 2020

REMARKS:

: - As-built plans was approved on 08 April 2021 and Recapitulation with Time Extension No. 4 was approved on 27 May 2021.

CONSTRUCTION OF PASSENGER TERMINAL BUILDING (PTB) PORT OF TAGBILARAN, BOHOL

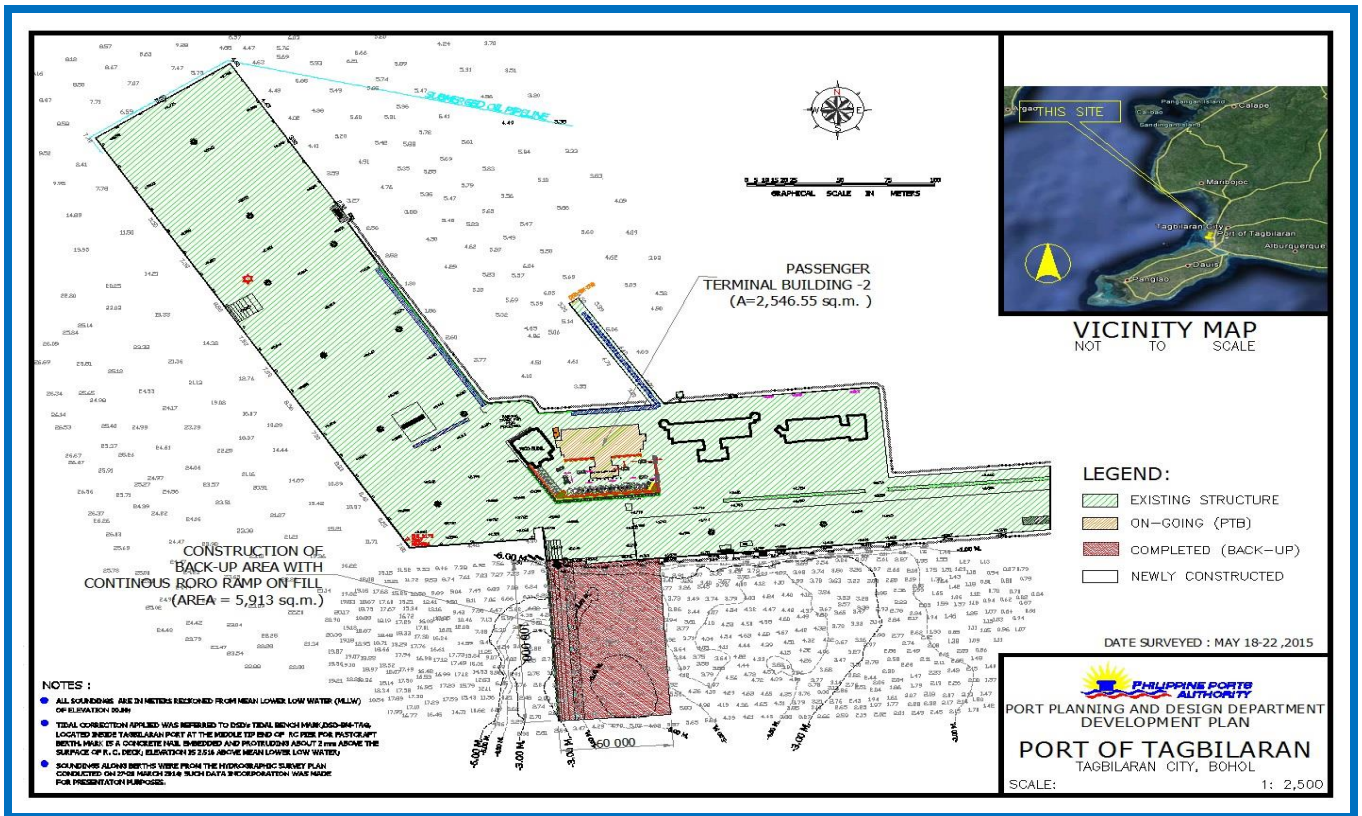

DEVELOPMENT PLAN



AFTER CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	: SIQUIJOR PORT EXPANSION PROJECT
LOCATION	: PORT OF SIQUIJOR, MUNICIPALITY OF SIQUIJOR, PROVINCE OF SIQUIJOR
CONTRACTOR	: WTG CONSTRUCTION & DEV'T. CORPORATION
SCOPE OF WORK	: A. CONSTRUCTION OF RC WHARF WITH RORO ROMP (AREA = 1,395.00 SQ.M.) B. CONSTRUCTION OF BACK-UP AREA (AREA = 4,735.71 SQ.M.) C. PORT LIGHTING SYSTEM
DATE OF BIDDING	: 27 July 2018
DATE OF AWARD	: 16 August 2018
DATE OF NOTICE TO PROCEED	: 10 December 2018
CONTRACT DURATION	: <i>450 calendar days</i>
APPROVED BUDGET AMOUNT	: <i>₱168,021,729.01</i>
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: <i>₱167,092,960.79</i>
RECAPITULATION	: <i>1,405,644.02</i> Covering the variance of the pre-determined quantities indicated in the Bill of Quantities (BOQ) as bid as against the actual quantities measured after the completion of the project.
REVISED CONTRACT AMOUNT (Final Revision)	: <i>₱168,498,604.81</i>
EFFECTIVITY DATE	: 10 December 2018
ORIGINAL EXPIRY DATE	: 03 March 2020
TIME EXTENSION NO. 1 / TIME ADJUSTMENT NO. 1	: <i>207 calendar days</i> Covering the delays brought about by unworkable bad weather/rough sea conditions for the period 1 January 2019 to 25 January 2020; busy port operations for the period 01 June 2019 to 25 January 2020 and time elapsed for the suspended period caused by the imposition of Enhanced Community Quarantine (ECQ) due to COVID-19 crisis.
REVISED EXPIRY DATE (First Revision)	: 26 September 2020

**TIME EXTENSION NO. 2 /
TIME ADJUSTMENT NO. 2**

- : 174 calendar days**
- Covering the delays caused by the issued suspension order on reclamation activities brought about by the issues and concerns raised by the Philippine Reclamation Authority (PRA).

REVISED EXPIRY DATE
(Second Revision)

: 23 March 2021

TIME EXTENSION NO. 3

- : 96 calendar days**
- Covering the delays brought about by unworkable bad weather / rough sea conditions for the period May 16, 2020 to February 25, 2021.

REVISED EXPIRY DATE
(Third Revision)

: 27 June 2021

PROJECT STATUS


- : - Completed as of 25 June 2021.**

REMARKS

:

SIQUIJOR PORT EXPANSION PROJECT

PORT OF SIQUIJOR, MUNICIPALITY OF SIQUIJOR, PROVINCE OF SIQUIJOR

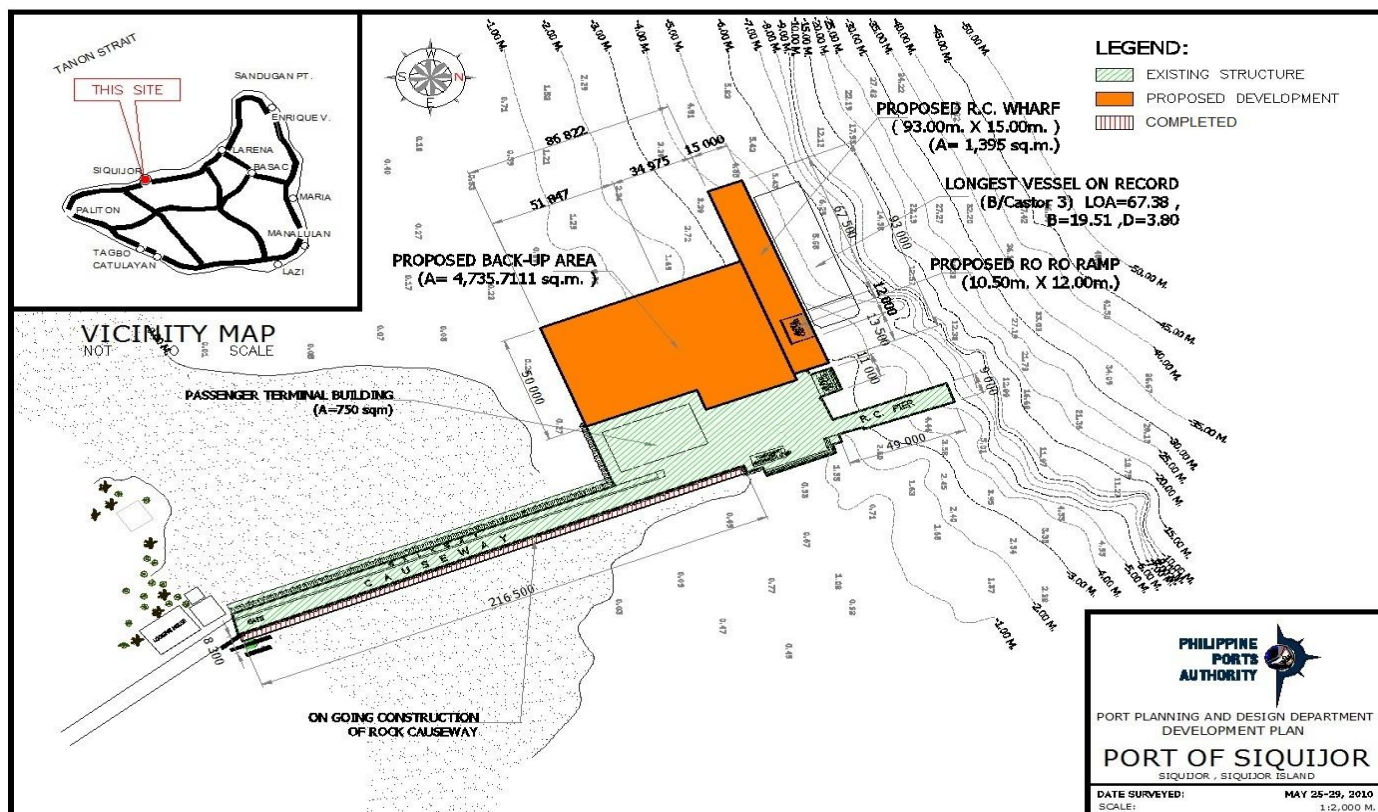

DEVELOPMENT PLAN




AFTER CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	:	CONSTRUCTION OF R.C. DECK APRON
LOCATION	:	PORT OF JAGNA, BOHOL
CONTRACTOR	:	JFAP CONST./RT CRISMAN BUILDER'S AND CONSTRUCTION SUPPLY - JV
SCOPE OF WORK	:	A. CONSTRUCTION OF R.C. PLATFORM
DATE OF BIDDING	:	17 July 2018
DATE OF AWARD	:	08 August 2018
DATE OF NOTICE TO PROCEED	:	30 October 2018
CONTRACT DURATION	:	360 <i>calendar days</i>
APPROVED BUDGET AMOUNT	:	P57,436,493.99
SOURCE OF FUNDS	:	PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	:	PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	:	P56,740,016.16
RECAPITULATION	:	P497,239.75 Covering the variance of the pre-determined quantities indicated in the Bill of Quantities (BOQ) as bid as against the actual quantities measured after the completion of the project.
REVISED CONTRACT AMOUNT	:	P57,237,255.91
EFFECTIVITY DATE	:	07 November 2018
ORIGINAL EXPIRY DATE	:	01 November 2019
TIME EXTENSION NO. 1	:	67 <i>calendar days</i> Covering the unworkable days caused by bad weather condition and busy port operations for the period from 01 January to 31 August 2019.
LATEST REVISED EXPIRY DATE (First Revision)	:	07 January 2020
PROJECT STATUS	:	- Completed on 07 January 2020
REMARKS	:	

CONSTRUCTION OF R.C. DECK APRON PORT OF JAGNA, BOHOL

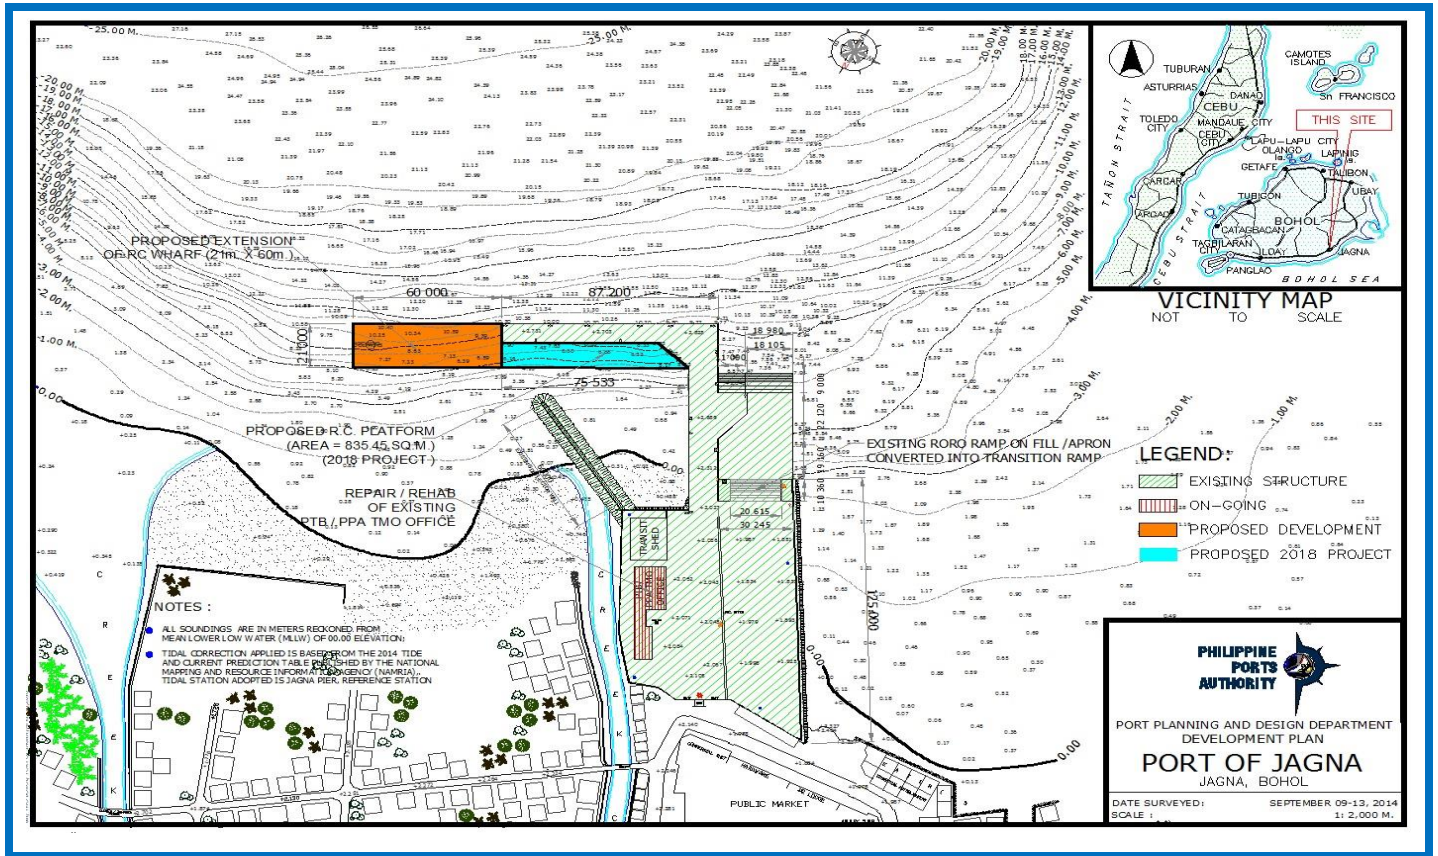

DEVELOPMENT PLAN



AFTER CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	: PALOMPON PORT IMPROVEMENT PROJECT
LOCATION	: PORT OF PALOMPON, LEYTE
CONTRACTOR	: FIAT CONSTRUCTION SERVICES
SCOPE OF WORK	: A. DEMOLITION & REMOVAL WORKS B. CONSTRUCTION OF BACK-UP AREA WITH RORO RAMP (ON-FILL). C. CONSTRUCTION OF PORT OPERATIONS BUILDING (POB) D. CONSTRUCTION OF TRANSIT SHED
DATE OF BIDDING	: 16 April 2018
DATE OF AWARD	: 23 May 2018
DATE OF NOTICE TO PROCEED	: 13 August 2018
CONTRACT DURATION	: 540 calendar days
APPROVED BUDGET AMOUNT	: ₱124,476,174.60
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱122,188,000.00
RECAPITULATION	: ₱2,342,318.68 Covering the variance of the pre-determined quantities indicated in the Bill of Quantities (BOQ) as bid as against the actual quantities measured after the completion of the project.
REVISED CONTRACT AMOUNT (Final Revision)	: ₱124,530,318.68
EFFECTIVITY DATE	: 20 August 2018
ORIGINAL EXPIRY DATE	: 10 February 2020
TIME EXTENSION NO. 1 / TIME ADJUSTMENT NO. 1	: 264 calendar days - Covering the delays brought about by unworkable bad weather/rough sea conditions for the period 20 August 2018 to 25 December 2019; time elapsed for the suspended period caused by imposition of Enhanced Community Quarantine (ECQ) due to COVID-19 crisis; and pending inventory / audit by COA on the valuable items stored in the existing Passenger Terminal prior to its removal/transfer to a temporary shelter to facilitate the remaining demolition works and execute the construction of transit shed.
REVISED EXPIRY DATE (First Revision)	: 31 October 2020
TIME EXTENSION NO. 2 / TIME ADJUSTMENT NO. 2	: 194 calendar days Due to delays caused by (a) suspension order on reclamation activities brought by the issues and concerns raised by the Philippine Reclamation Authority (PRA, and (b) late execution of demolition of the existing passenger terminal building brought by pending audit/inventory made by the Commission on audit on the valuable assets stored therein.
REVISED EXPIRY DATE (Second Revision)	: 27 July 2021

TIME EXTENSION NO. 3

: **121 calendar days**

Covering the delays brought about by unworkable bad weather / rough sea conditions for the period 15 January to 25 June 2021 and time needed for the execution of the approved additional works.

REVISED EXPIRY DATE

(Third Revision)

: **25 November 2021**

PROJECT STATUS


(As of 25 January 2023)

: - Completed as of 22 November 2021.

REMARKS

: - As-built plan was approved on 04 October 2022 and Recapitulation with Time Extension covering the delays brought by unworkable weather / rough sea conditions and time needed for the execution of the approved additional works was approved on 19 January 2023.

PALOMPON PORT IMPROVEMENT PROJECT PORT OF PALOMPON, LEYTE

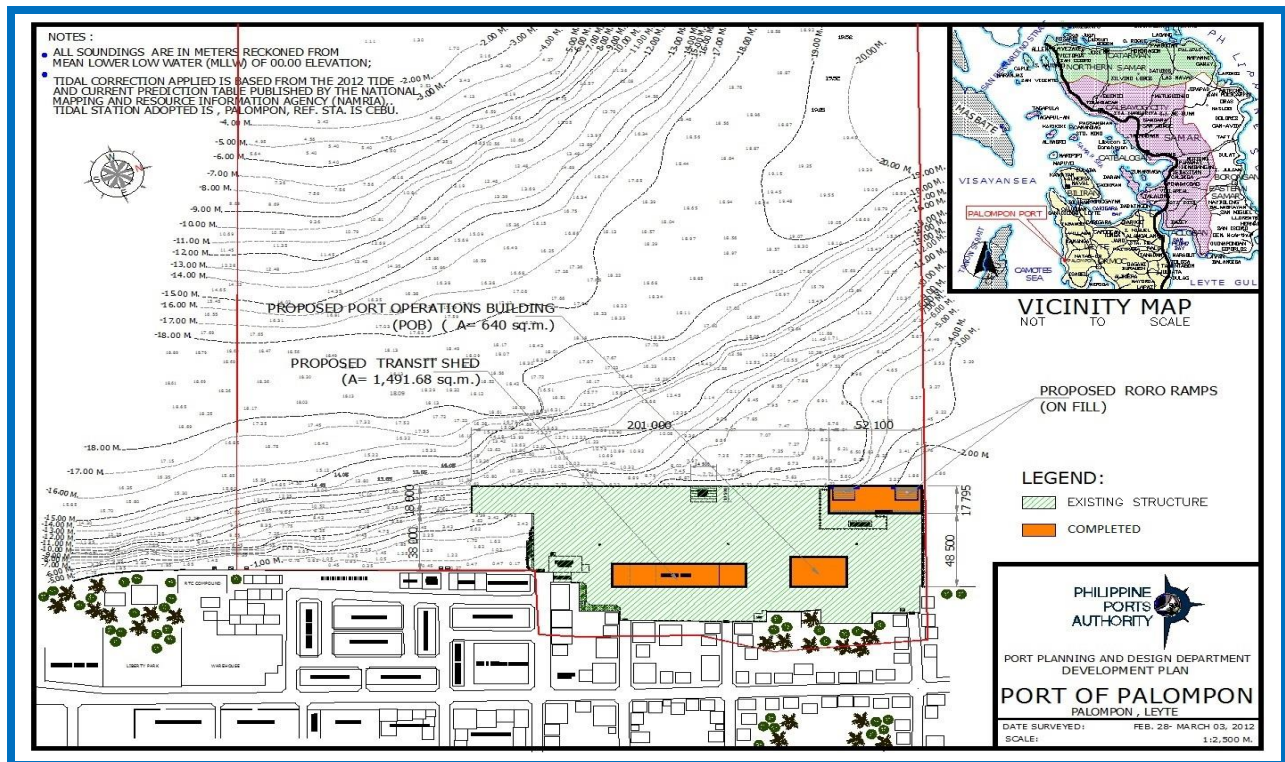

DEVELOPMENT PLAN




AFTER CONSTRUCTION


PROJECT BRIEF

PROJECT TITLE	: ORMOC PORT EXPANSION PROJECT
LOCATION	: PORT OF ORMOC, LEYTE
CONTRACTOR	: PREMIUM MEGASTRUCTURE, INC.
SCOPE OF WORK	: A. DEMOLITION, REMOVAL AND EXCAVATION WORKS B. BACK-UP AREA C. PLATFORM AND RORO RAMP
DATE OF BIDDING	: 14 December 2017
DATE OF AWARD	: 16 January 2018
DATE OF NOTICE TO PROCEED	: 07 March 2018
CONTRACT DURATION	: 540 calendar days
APPROVED BUDGET AMOUNT	: ₱262,809,794.53
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱260,181,700.00
RECAPITULATION	: ₱1,073,759.89 Covering the variance of the pre-determined quantities indicated in the Bill of Quantities (BOQ) as bid as against the actual quantities measured after the completion of the project.
REVISED CONTRACT AMOUNT (Final Revision)	: ₱261,255,459.89
EFFECTIVITY DATE	: 12 March 2018
ORIGINAL EXPIRY DATE	: 02 September 2019
TIME EXTENSION NO. 1	: 100 calendar days Covering the delays incurred by the project brought about by the unworkable bad weather/rough sea conditions for the period 12 March 2018 to 25 June 2019.
REVISED EXPIRY DATE (First Revision)	: 11 December 2019
TIME EXTENSION NO. 2 / TIME ADJUSTMENT NO. 2	: 344 calendar days Covering the delays brought by unworkable days caused by bad weather condition for the period of 26 June to 17 November 2019 and the time elapsed of the suspended period from 18 November 2019 to 29 September 2020 due to Philippine Reclamation Authority (PRA) issues on legality/ownership in the implementation of reclamation projects.
LATEST REVISED EXPIRY DATE (Second Revision)	: 19 November 2020
PROJECT STATUS	: - Completed on 26 October 2020.
REMARKS:	: - As-built plans was approved on 09 June 2021 and recapitulation was approved on 23 June 2021.

ORMOC PORT EXPANSION PROJECT PORT OF ORMOC, LEYTE

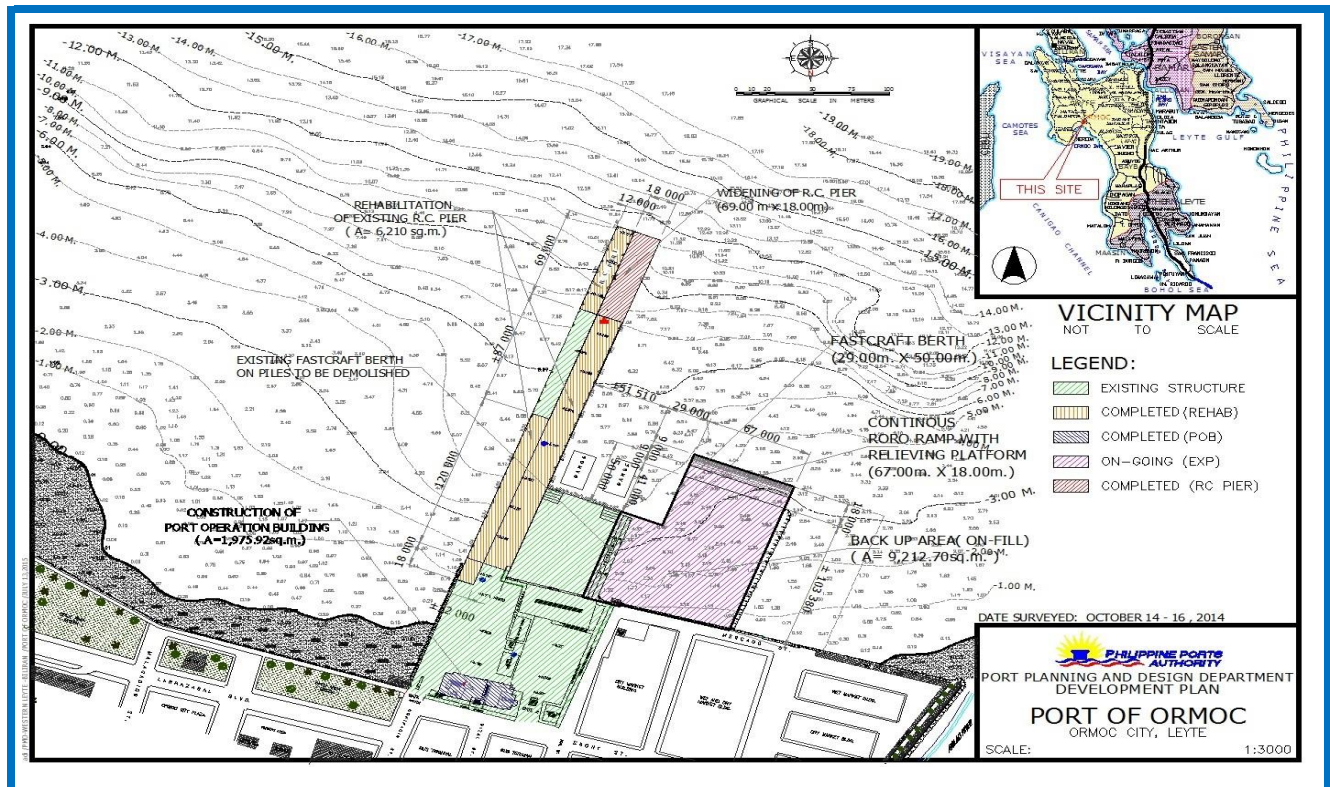

DEVELOPMENT PLAN

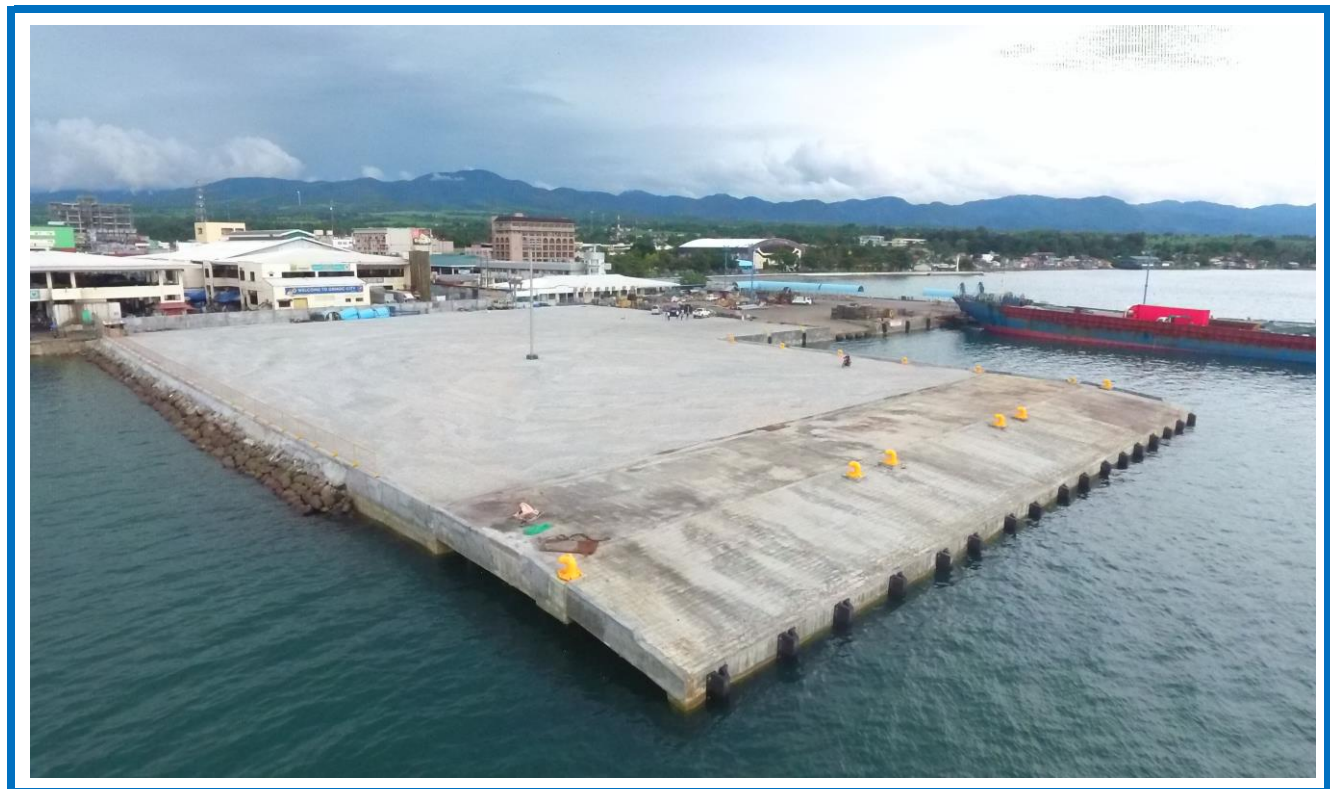


AFTER CONSTRUCTION


PROJECT BRIEF

PROJECT TITLE	: BANAGO PORT EXPANSION PROJECT
LOCATION	: PORT OF BANAGO, BACOLOD CITY, NEGROS OCCIDENTAL
CONTRACTOR	: MAMSAR CONSTRUCTION AND INDUSTRIAL CORPORATION/SILVER DRAGON CONSTRUCTION AND LUMBER AND GRASS SUPPLY, INC. JV
SCOPE OF WORK	: A. CONSTRUCTION OF BACK-UP AREA WITH RORO RAMP ON PILES B. MOORING AND FENDERING SYSTEM C. PORT LIGHTING SYSTEM
DATE OF BIDDING	: 03 October 2018
DATE OF AWARD	: 16 October 2018
DATE OF NOTICE TO PROCEED	: 24 January 2019
CONTRACT DURATION	: 660 <i>calendar days</i>
APPROVED BUDGET AMOUNT	: ₱363,575,987.67
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱362,698,606.45
RECAPITULATION	: 766,297.87 Covering the variance of the pre-determined quantities indicated in the Bill of Quantities (BOQ) as bid as against the actual quantities measured after the completion of the project.
REVISED CONTRACT AMOUNT (Final Revision)	: ₱363,464,904.32
EFFECTIVITY DATE	: 28 January 2019
ORIGINAL EXPIRY DATE	: 17 November 2020
TIME EXTENSION NO. 1 / TIME ADJUSTMENT NO. 1	: 194 <i>calendar days</i> - Covering the delays caused by the unworkable weather condition, busy port operation and issues suspension order due to COVID-19 pandemic and imposition of Enhance Community Quarantine (ECQ) throughout the island of Luzon and other parts of the Philippines.
REVISED EXPIRY DATE	: 30 May 2021
PROJECT STATUS	: - Completed as of 25 June 2021.

BANAGO PORT EXPANSION PROJECT PORT OF BANAGO, BACOLOD CITY, NEGROS OCCIDENTAL

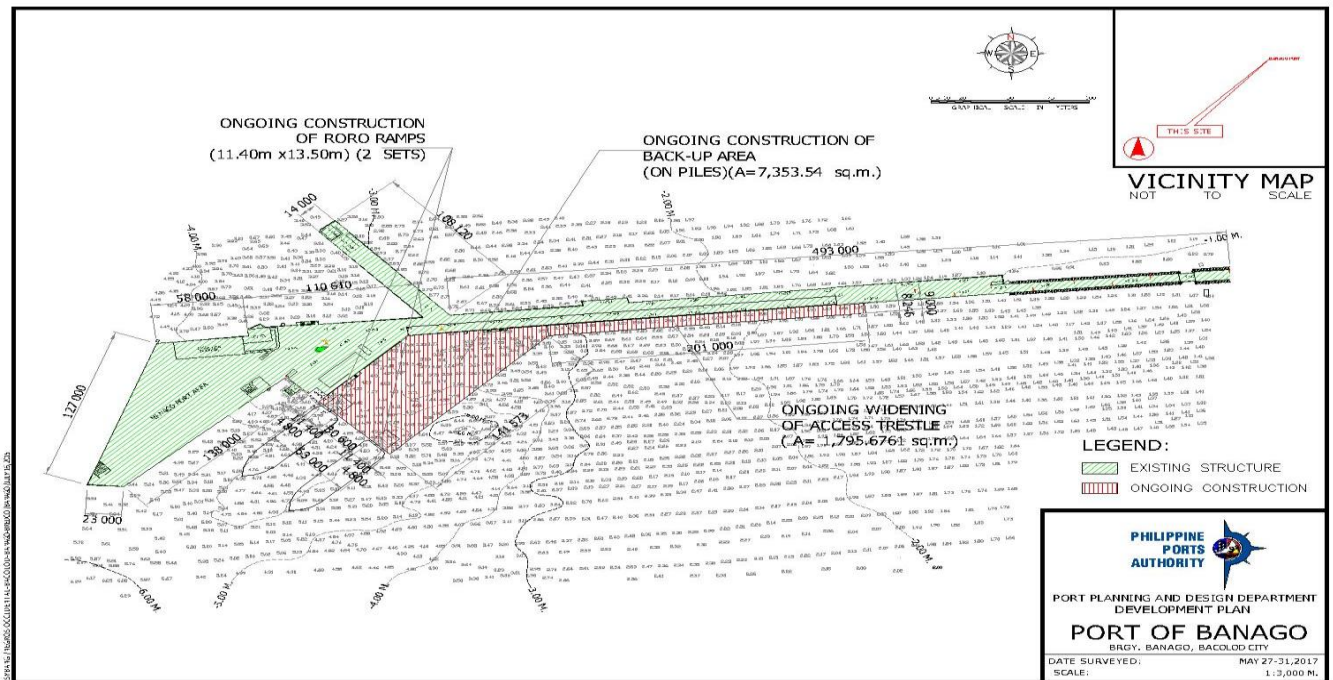

DEVELOPMENT PLAN

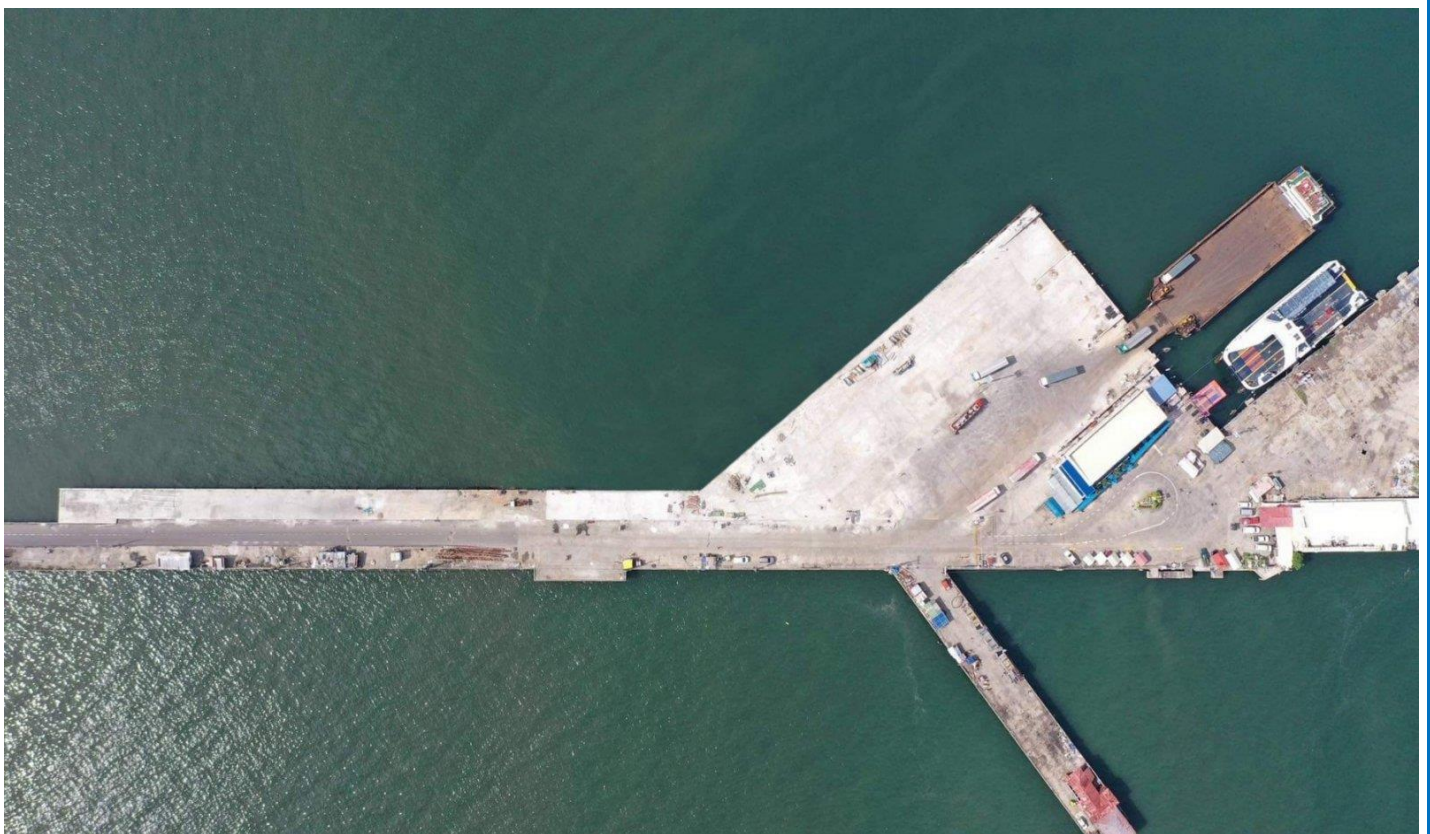


AFTER CONSTRUCTION


PROJECT BRIEF

PROJECT TITLE	:	MANOC MANOC CARGO PORT PROJECT
LOCATION	:	PORT OF MANOC MANOC, MALAY, AKLAN
CONTRACTOR	:	KHAN KON CHI CONSTRUCTION AND DEV'T CORPORATION
SCOPE OF WORK	:	A. CONSTRUCTION OF BACK-UP AREA (AREA = 4,571.00 SQ.M.) B. CONSTRUCTION OF ACCESS ROAD (AREA = 337.56 SQ.M.) C. PORT LIGHTING SYSTEM
DATE OF BIDDING	:	23 May 2019
DATE OF AWARD	:	26 June 2019
DATE OF NOTICE TO PROCEED	:	28 August 2019
CONTRACT DURATION	:	420 calendar days
APPROVED BUDGET AMOUNT	:	₱134,170,466.65
SOURCE OF FUNDS	:	PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	:	PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	:	₱132,828,205.91
VARIATION ORDER NO. 1 (Change Order No.1/Extra Work Order No.1)	:	₱11,334,902.57 Covering the quantity adjustments (overrun/underruns/deletion) of some of the original items of work and inclusion of additional works as called for by the results of the approved revised plans / drawings incorporating the final location of the project including the substitution / extension of the designed concrete sheet piles in lieu of the rock bulkhead to conform to the actual seabed elevation based on the conducted pre-construction survey.
REVISED CONTRACT AMOUNT (First Revision)	:	₱144,163,108.48
EFFECTIVITY DATE	:	30 August 2019
ORIGINAL EXPIRY DATE	:	22 October 2020
TIME EXTENSION NO. 1 / TIME ADJUSTMENT NO. 1	:	420 calendar days Covering the original project duration being affected by the issued Suspension Order.
REVISED EXPIRY DATE (First Revision)	:	02 November 2023
PROJECT STATUS (As of 25 January 2023)	:	- The project is 46.452% complete and progressing ahead of 19.227%.
REMARKS	:	- On-going.

MANOC MANOC CARGO PORT PROJECT PORT OF MANOC MANOC, MALAY, AKLAN

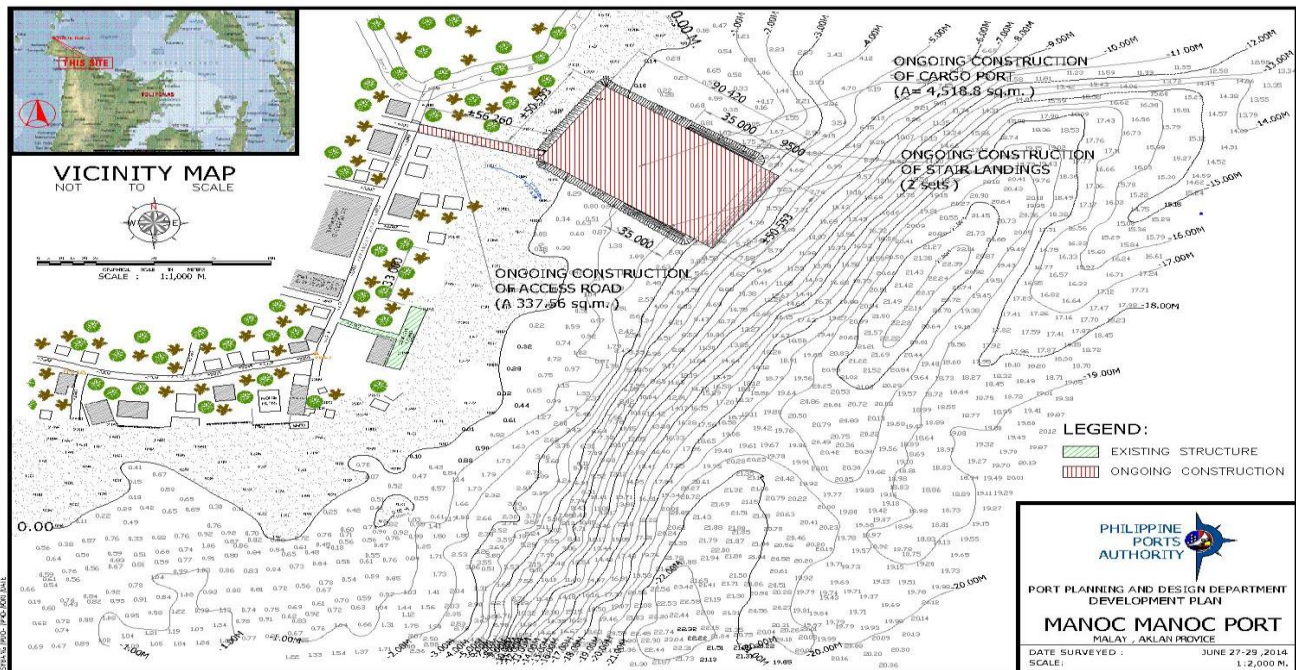

DEVELOPMENT PLAN

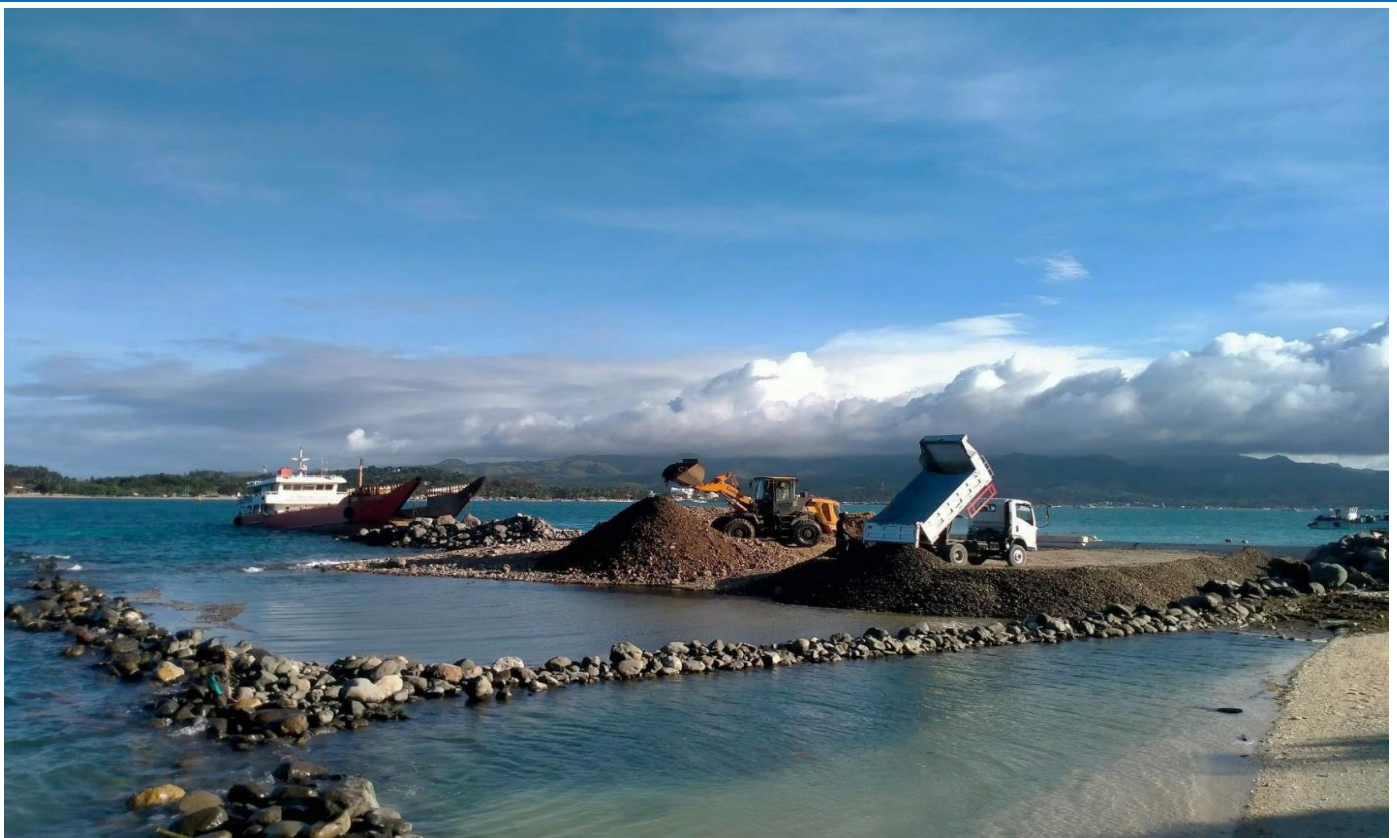


ONGOING CONSTRUCTION


PROJECT BRIEF

PROJECT TITLE	:	WIDENING OF ACCESS TRESTLE AND CONSTRUCTION OF RORO RAMP WITH PLATFORM
LOCATION	:	PORT OF ESTANCIA, ILOILO
CONTRACTOR	:	J.S. LAYSON AND CO. INC.
SCOPE OF WORK	:	A. CONSTRUCTION OF CAUSEWAY(5.135m x 6.00m) B. CONSTRUCTION OF ACCESS TRESTLE AND RORO RAMP WITH PLATFORM
DATE OF BIDDING	:	14 September 2018
DATE OF AWARD	:	4 October 2018
DATE OF NOTICE TO PROCEED	:	20 February 2019
CONTRACT DURATION	:	360 <i>calendar days</i>
APPROVED BUDGET AMOUNT	:	₱36,357,823.04
SOURCE OF FUNDS	:	PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	:	PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	:	₱35,900,947.00
RECAPITULATION	:	(104,058.80) Covering the variance of the pre-determined quantities indicated in the Bill of Quantities (BOQ) as bid as against the actual quantities measured after the completion of the project.
REVISED CONTRACT AMOUNT	:	₱35,796,888.20
EFFECTIVITY DATE	:	4 March 2019
ORIGINAL EXPIRY DATE	:	26 February 2020
PROJECT STATUS	:	- Completed on 15 February 2020
REMARKS	:	

WIDENING OF ACCESS TRESTLE AND CONSTRUCTION OF RORO RAMP WITH PLATFORM PORT OF ESTANCIA, ILOILO

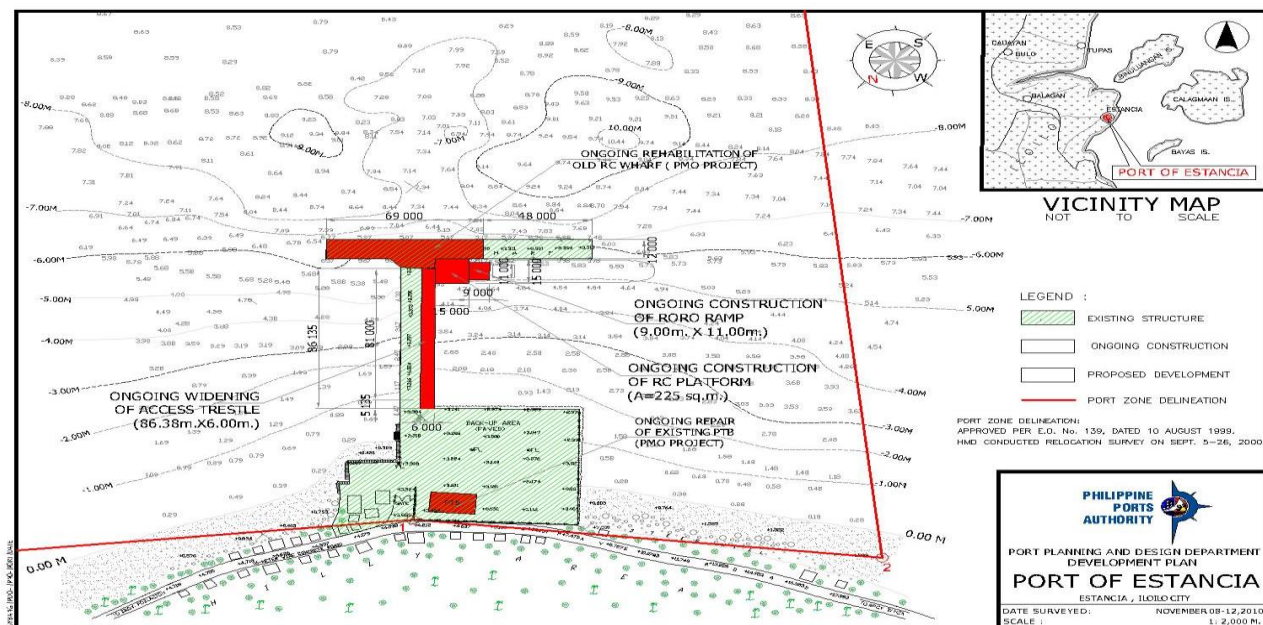

DEVELOPMENT PLAN

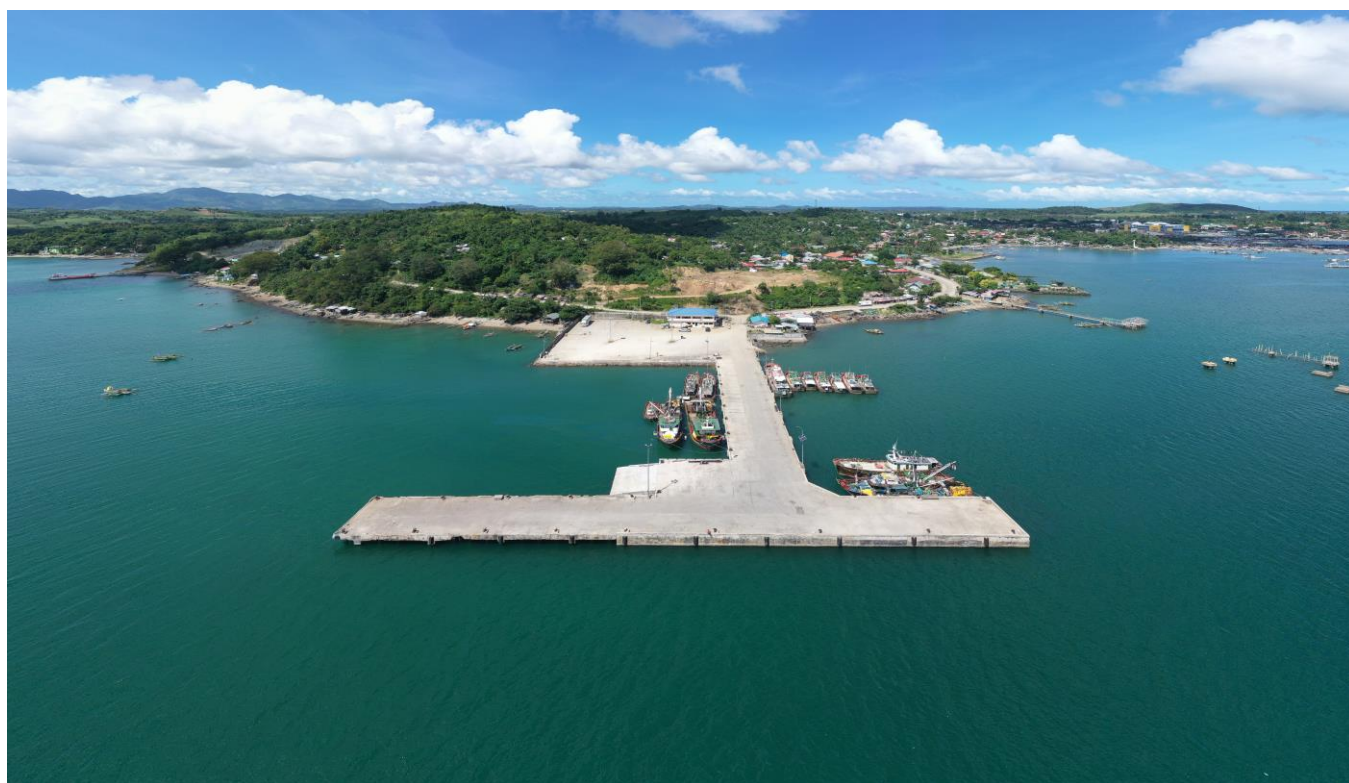

AFTER CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	:	CONSTRUCTION OF BACK-UP AREA PROJECT
LOCATION	:	PORT OF GETAFE, BOHOL
CONTRACTOR	:	MAMSAR CONSTRUCTION & INDUSTRIAL CORPORATION/JFAP CONSTRUCTION - JV
SCOPE OF WORK	:	A. BACK-UP AREA
DATE OF BIDDING	:	03 December 2019
DATE OF AWARD	:	24 January 2020
DATE OF NOTICE TO PROCEED	:	02 March 2020
CONTRACT DURATION	:	360 <i>calendar days</i>
APPROVED BUDGET AMOUNT	:	₱163,296,490.50
SOURCE OF FUNDS	:	PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	:	PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	:	₱161,899,074.84
RECAPITULATION	:	(36,135.82) Covering the quantity adjustment brought by the actual adjustment of work which are necessary to suit actual field condition and in conformity with the duly approved as-built/drawings and project specifications.
REVISED CONTRACT AMOUNT	:	₱161,862,939.02
EFFECTIVITY DATE	:	09 March 2020
ORIGINAL EXPIRY DATE	:	03 March 2021
TIME EXTENSION NO. 1	:	199 <i>calendar days</i> Covering the delays caused by issued suspension order by the Provincial Government of Bohol to all quarry permits/operations and implementation of Legal Compliance Audit to all quarry permit holders time elapsed for the suspended period caused by the imposition of Enhanced Community Quarantine (ECQ) due to COVID-19 Pandemic.
REVISED EXPIRY DATE (First Revision)	:	18 September 2021
TIME EXTENSION NO. 2	:	40 <i>calendar days</i> Covering the delays brought about by unworkable bad weather condition for the period March 2020 to June 2021.
REVISED EXPIRY DATE (Second Revision)	:	28 October 2021
TIME EXTENSION NO. 3	:	42 <i>calendar days</i> Covering the delays caused by the unworkable weather condition for the period June 2021 to October 2021.
REVISED EXPIRY DATE	:	09 December 2021

(Third Revision)

TIME EXTENSION NO. 4

: ***112 calendar days***

Covering the quantity adjustment brought by the actual adjustment of work which are necessary to suit actual field condition and in conformity with the duly approved as-built/drawings and project specifications.

LATEST REVISED EXPIRY DATE

: **31 March 2022**

(Fourth Revision)


PROJECT STATUS

: - Completed as of 22 March 2022.


REMARKS

: - As-built plans was approved on 29 April 2022 and Recapitulation was approved on 15 September 2022.

CONSTRUCTION OF BACK-UP AREA PROJECT PORT OF GETAFE, BOHOL

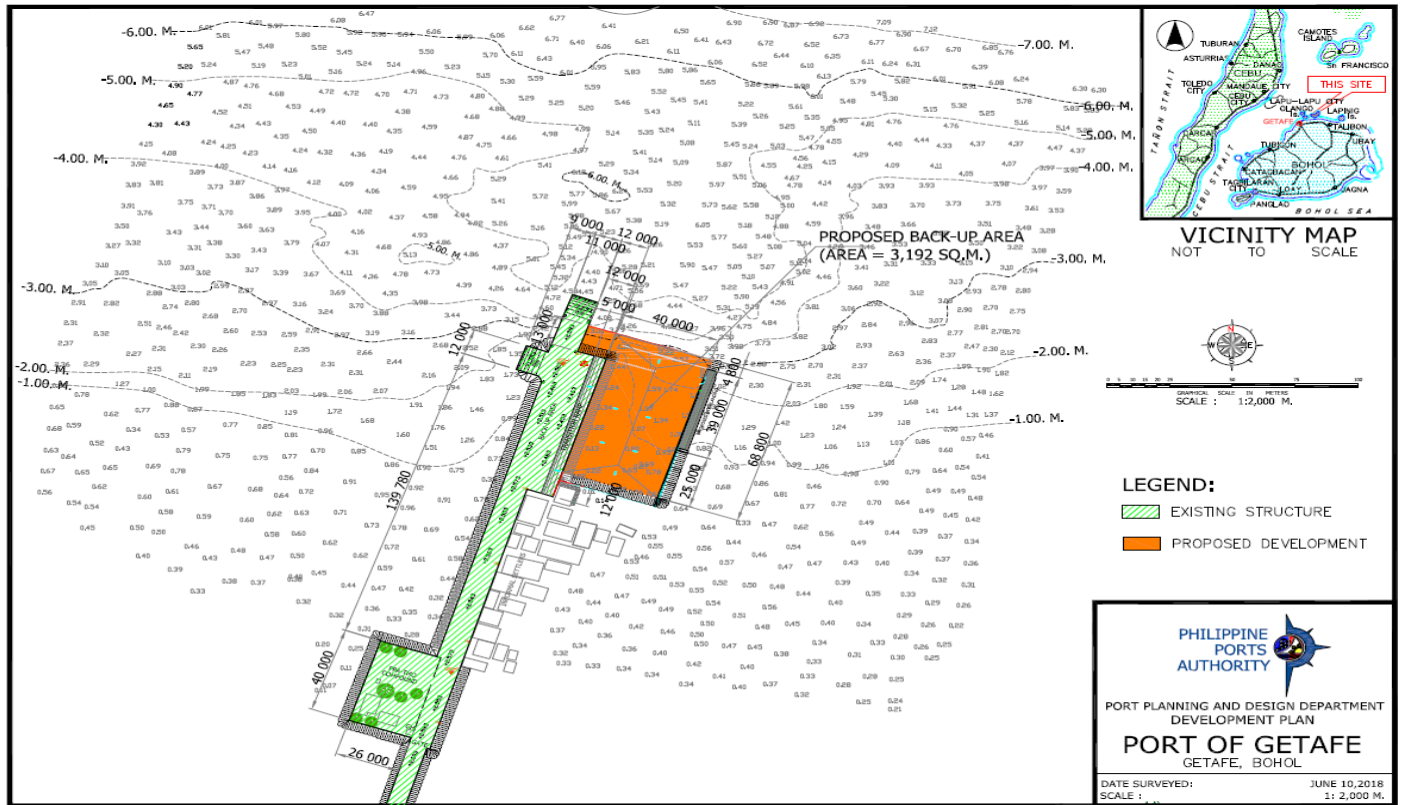

DEVELOPMENT PLAN

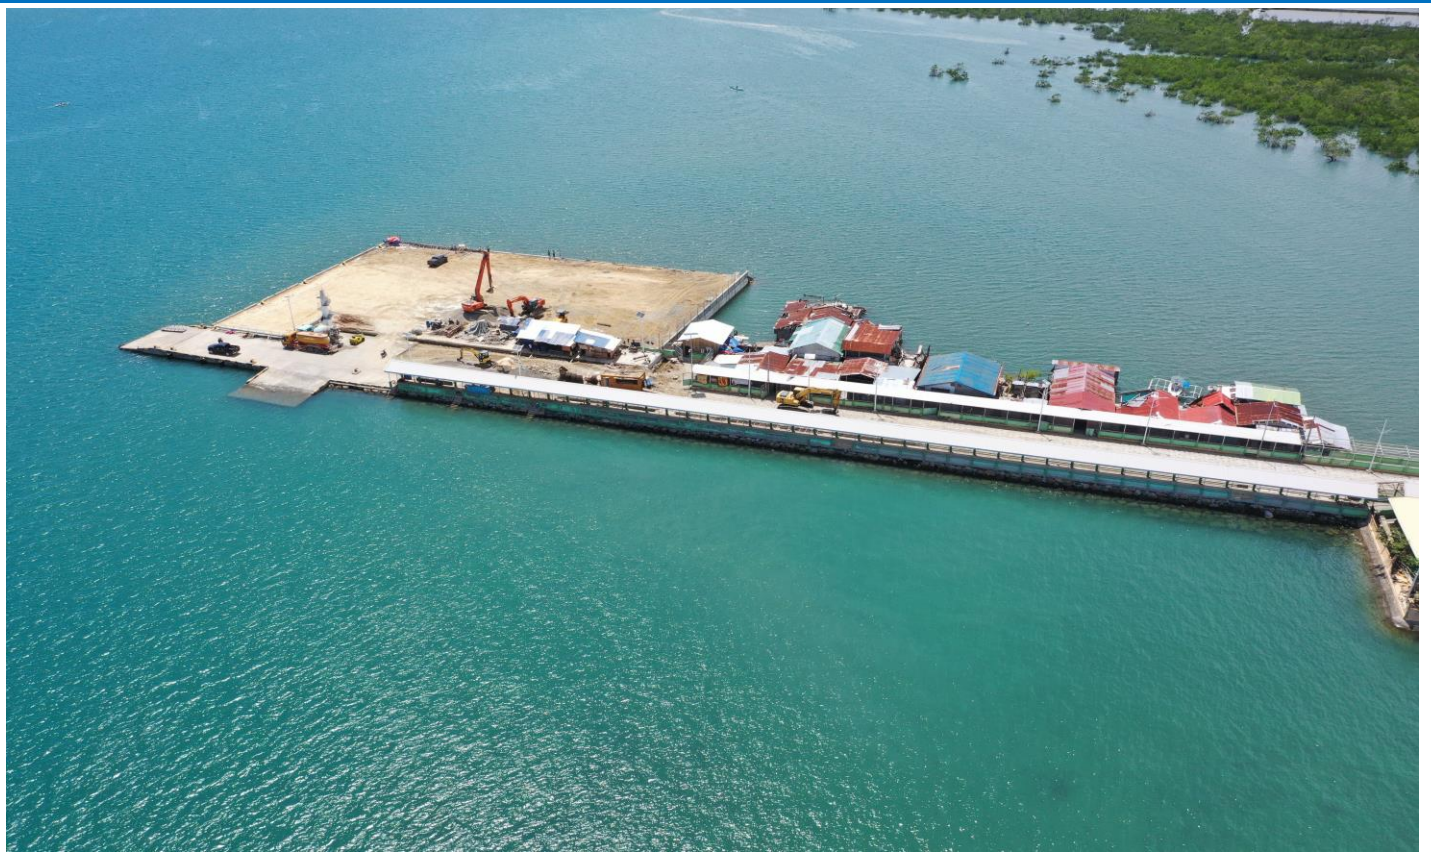


AFTER CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	: REHABILITATION OF EXISTING R.C. PIER
LOCATION	: PORT OF BAYBAY, LEYTE
CONTRACTOR	: A.T. TAN CONSTRUCTION CORPORATION
SCOPE OF WORK	: A. DEMOLITION, REMOVAL & EXCAVATION WORKS B. TRANSITION RAMP & EXTENSION OF RORO RAMP ON FILL C. REHABILITATION OF EXISTING OF R.C. PIER
DATE OF BIDDING	: 01 October 2019
DATE OF AWARD	: 24 October 2019
DATE OF NOTICE TO PROCEED	: 20 December 2019
CONTRACT DURATION	: 420 calendar days
APPROVED BUDGET AMOUNT	: ₱126,092,268.37
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱120,851,884.27
RECAPITULATION	: -₱2,525,183.76 Covering the variance of the pre-determined quantities indicated in the Bill of Quantities (BOQ) as bid as against the actual quantities measured after the completion of the project.
REVISED CONTRACT AMOUNT (Final Revision)	: ₱118,326,700.51
EFFECTIVITY DATE	: 08 January 2020
ORIGINAL EXPIRY DATE	: 02 March 2021
PROJECT STATUS	: - Completed on 02 March 2021.
REMARKS:	:

REHABILITATION OF EXISTING R.C. PIER PORT OF BAYBAY, LEYTE

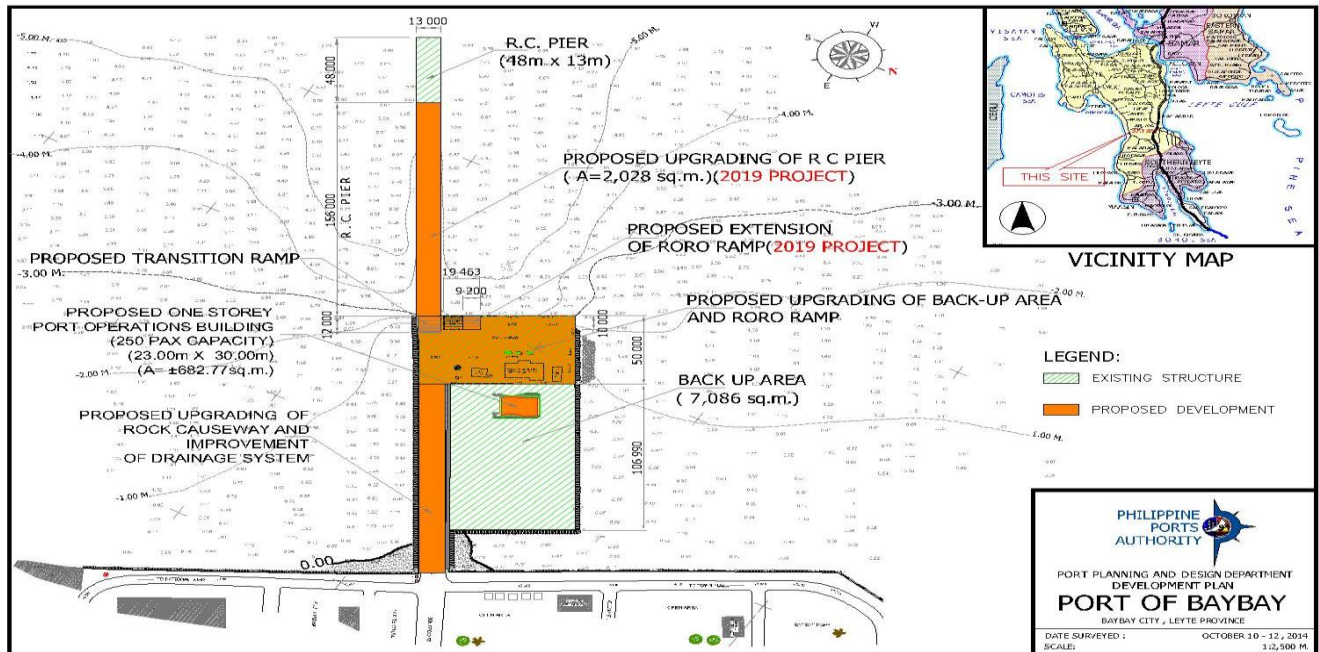

DEVELOPMENT PLAN




AFTER CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	: CONSTRUCTION OF BACK-UP AREA AND RORO RAMP
LOCATION	: PORT OF TAPAL, BOHOL
CONTRACTOR	: MAMSAR CONST. AND INDUSTRIAL CORP. / JFAP CONSTRUCTION. - JV
SCOPE OF WORK	: A. DEMOLITION, REMOVAL AND EXCAVATION WORKS B. BACK-UP AREA AND RORO RAMP (ON-FILL)
DATE OF BIDDING	: 23 May 2019
DATE OF AWARD	: 19 June 2019
DATE OF NOTICE TO PROCEED	: 19 August 2019
CONTRACT DURATION	: 300 <i>calendar days</i>
APPROVED BUDGET AMOUNT	: ₱56,559,225.82
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱56,285,488.85
RECAPITULATION	: (559,268.56) Covering the variance of the pre-determined quantities indicated in the Bill of Quantities (BOQ) as bid as against the actual quantities measured after the completion of the project.
REVISED CONTRACT AMOUNT	: ₱55,726,220.29
EFFECTIVITY DATE	: 28 August 2019
ORIGINAL EXPIRY DATE	: 22 June 2020
TIME EXTENSION NO. 1 / TIME ADJUSTMENT NO. 1	: 189 <i>calendar days</i> Covering the time elapsed due to suspended period from 18 November 2019 to 29 September 2020.
LATEST REVISED EXPIRY DATE (First Revision)	: 27 November 2020.
PROJECT STATUS	: - Completed on 31 October 2020. - Recapitulation was approved on 08 April 2021.

CONSTRUCTION OF BACK-UP AREA AND RORO RAMP PORT OF TAPA, BOHOL

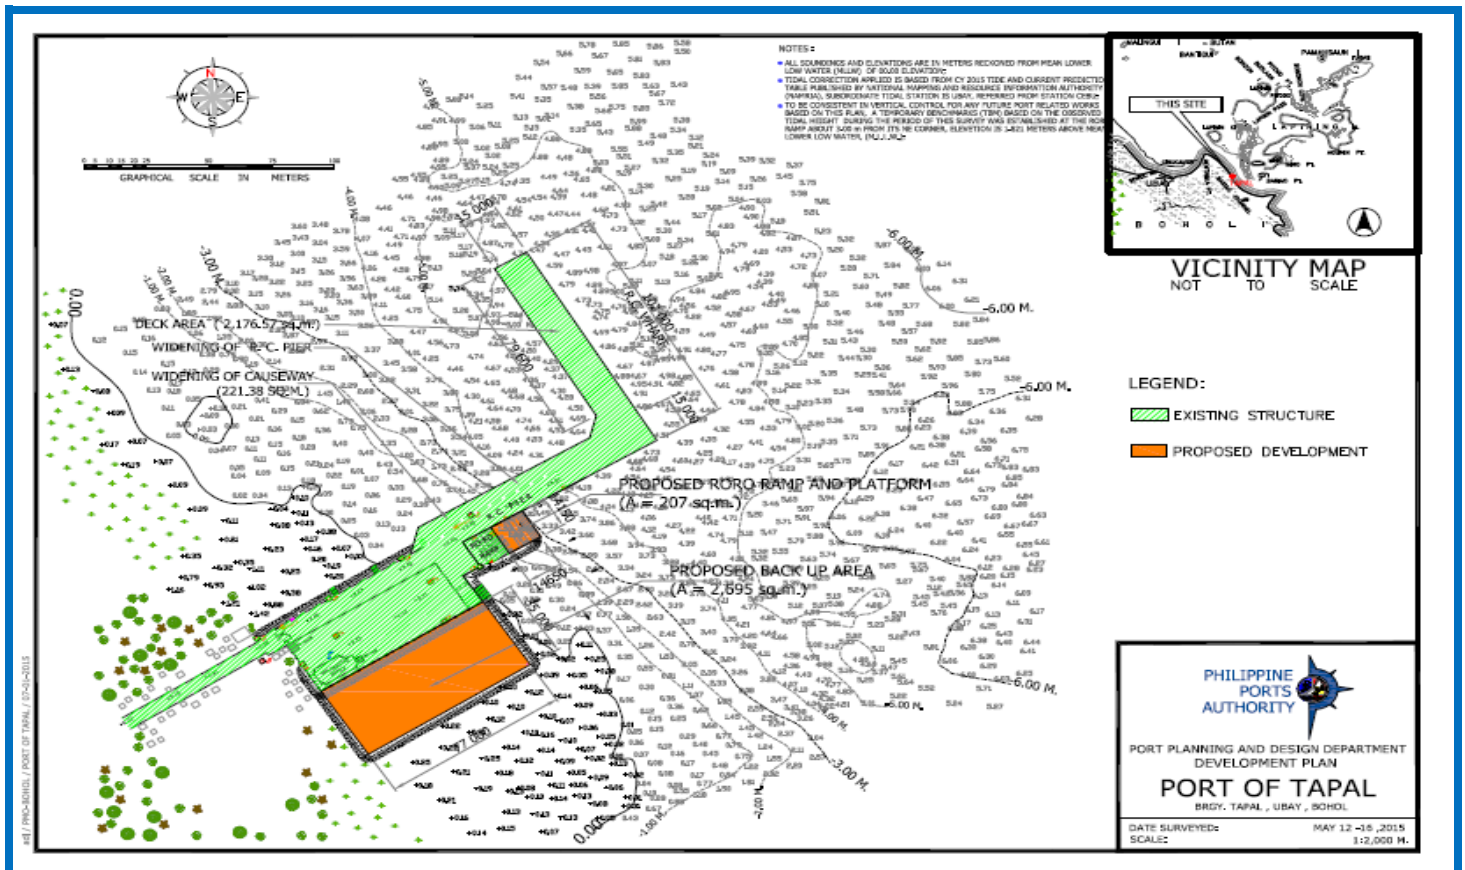


AFTER CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	: CONSTRUCTION OF RC PIER
LOCATION	: PORT OF UBAY, BOHOL
CONTRACTOR	: JFAP CONST./RT CRISMAN BUILDER'S AND CONST. SUPPLY - JV
SCOPE OF WORK	: A. DEMOLITION AND REMOVAL WORKS B. CONSTRUCTION OF PIER APPROACH C. CONSTRUCTION OF RC PIER
DATE OF BIDDING	: 30 October 2018
DATE OF AWARD	: 19 November 2018
DATE OF NOTICE TO PROCEED	: 20 February 2019
CONTRACT DURATION	: <i>420 calendar days</i>
APPROVED BUDGET AMOUNT	: <i>₱97,084,311.28</i>
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: <i>₱95,897,552.51</i>
RECAPITULATION (Final Revision)	: <i>-₱12,042,751.64</i> Covering the variance of the pre-determined quantities indicated in the Bill of Quantities (BOQ) as bid as against the actual quantities measured after the completion of the project.
REVISED CONTRACT AMOUNT	: <i>₱83,854,800.87</i>
EFFECTIVITY DATE	: 28 February 2019
ORIGINAL EXPIRY DATE	: 22 April 2020
TIME EXTENSION NO. 1	: <i>236 calendar days</i>
LATEST REVISED EXPIRY DATE (First Revision)	: 14 December 2020
PROJECT STATUS	: - Completed as of 12 December 2020.
REMARKS:	: - Recapitulation was approved on 08 April 2021.

CONSTRUCTION OF R.C. PIER PORT OF UBAY, BOHOL

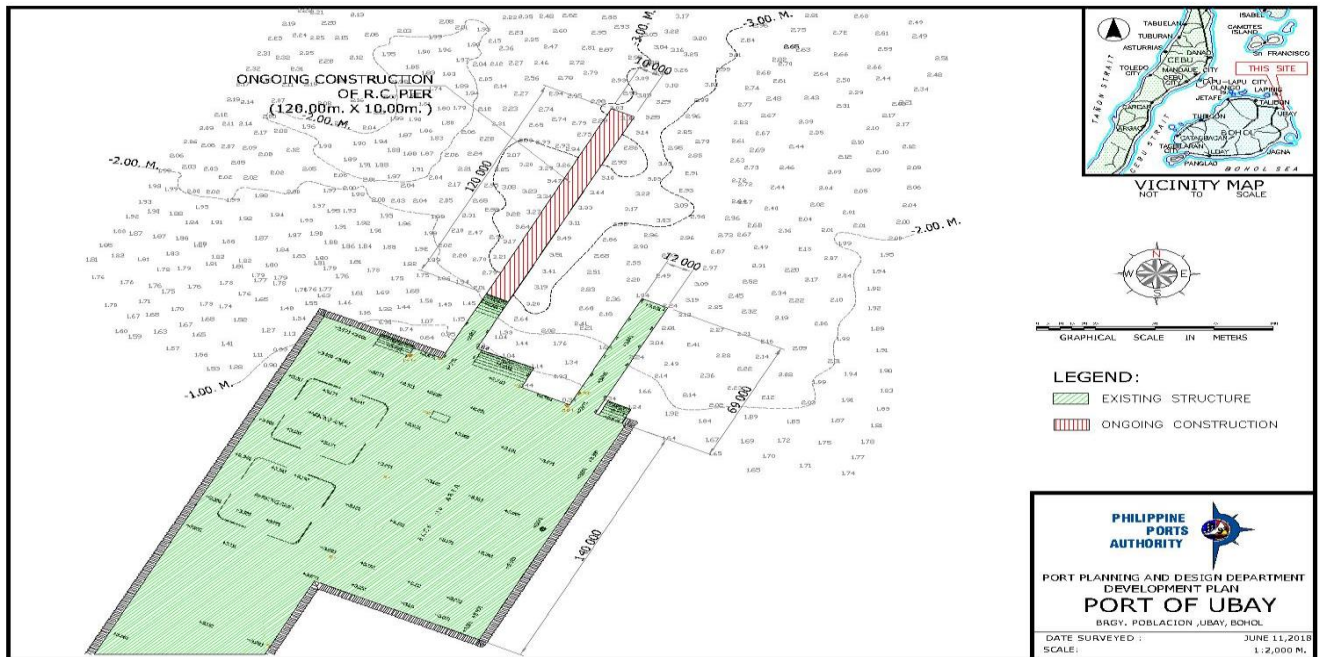

DEVELOPMENT PLAN




AFTER CONSTRUCTION

PROJECT BRIEF


PROJECT TITLE	:	CONSTRUCTION OF BACK-UP AREA
LOCATION	:	PORT OF DUMANGAS, BRGY. SAPAO, DUMANGAS, ILOILO
CONTRACTOR	:	IBC INTERNATIONAL BUILDERS CORPORATION/ DYNAMIC BUILDERS & CONSTRUCTION COMPANY (PHIL.), INC. / JV
SCOPE OF WORK	:	A. CONSTRUCTION OF BACK-UP AREA (AREA = 15,427.37 SQ.M.) B. PORT LIGHTING SYSTEM
DATE OF BIDDING	:	28 January 2019
DATE OF AWARD	:	14 February 2019
DATE OF NOTICE TO PROCEED	:	28 May 2019
CONTRACT DURATION	:	600 <i>calendar days</i>
APPROVED BUDGET AMOUNT	:	₱239,074,188.73
SOURCE OF FUNDS	:	PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	:	PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	:	₱237,931,283.84
VARIATION ORDER NO. 1 (Change Order No.1/Extra Work Order No.1)	:	₱2,961,848.46 Covering the additional works and quantity adjustment of some of the original items of work as called for by the approval of issuance the revised plans/drawing incorporating changes in existing back-up area.
REVISED CONTRACT AMOUNT (First Revision)	:	₱240,893,132.30
RECAPITULATION	:	9,421,823.68 Covering the variance of the pre-determined quantities indicated in the Bill of Quantities (BOQ) as bid as against the actual quantities measured after the completion of the project.
REVISED CONTRACT AMOUNT (Final Revision)	:	₱250,314,955.98
EFFECTIVITY DATE	:	04 June 2019
ORIGINAL EXPIRY DATE	:	23 January 2021
TIME ADJUSTMENT NO. 1	:	222 <i>calendar days</i> Covering the time elapsed of the suspended period from 18 November 2019 to 29 November 2020 due to Philippine Reclamation Authority (PRA) issues on legality/ownership in the implementation of reclamation projects. Evaluation of time adjustment focuses on the remaining duration of supply and place of rockworks and embankment.
REVISED EXPIRY DATE (First Revision)	:	02 September 2021

TIME EXTENSION NO. 1	: <i>90 calendar days</i> Covering the delays caused by the unworkable weather condition and time elapsed of the suspended period caused by the imposition of Modified Enhanced Community Quarantine (MECQ) and Enhanced Community Quarantine (ECQ) brought by the COVID-19 in the Province of Iloilo.
REVISED EXPIRY DATE (Second Revision)	: 01 December 2021
TIME EXTENSION NO. 2	: <i>49 calendar days</i> Covering the delays caused by the unworkable weather condition.
REVISED EXPIRY DATE (Third Revision)	: 19 January 2022
TIME EXTENSION NO. 3	: <i>45 calendar days</i> To facilitate the execution/completion of the approved changes/ additional works for the above-captioned project.
LATEST REVISED EXPIRY DATE (Fourth Revision)	: 05 March 2022
PROJECT STATUS	: - Completed on 17 February 2022
REMARKS	: - As-built plans was approved on 28 July 2022 and Recapitulation was approved on 07 October 2022.

CONSTRUCTION OF BACK-UP AREA PORT OF DUMANGAS, BRGY. SAPAO, DUMANGAS, ILOILO

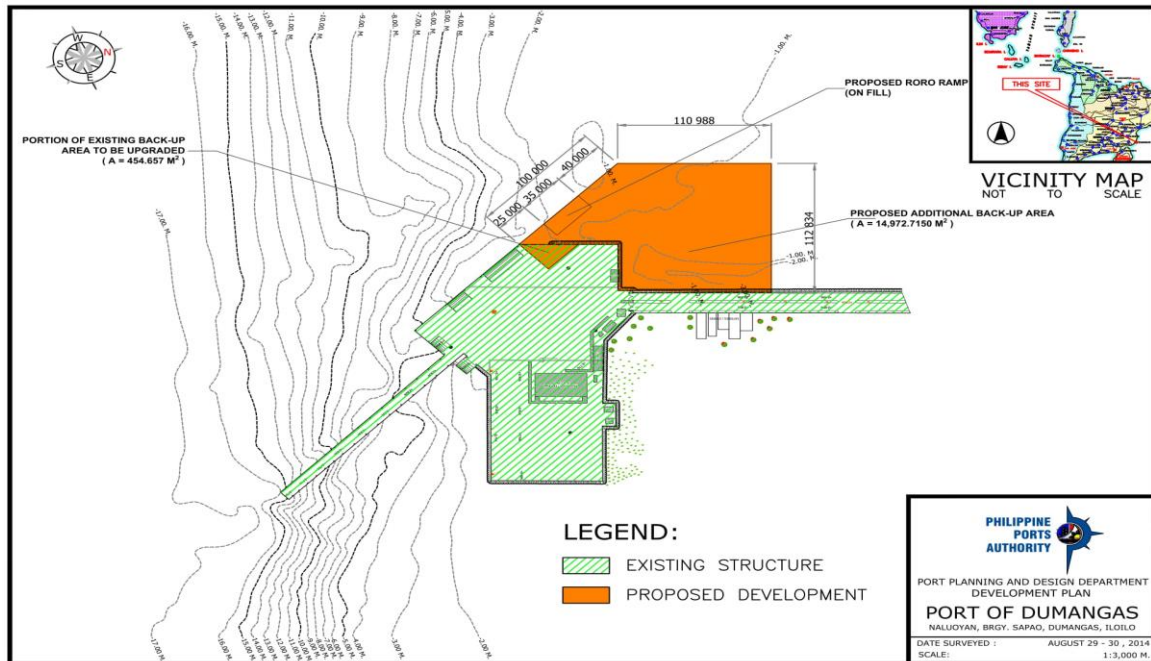

DEVELOPMENT PLAN

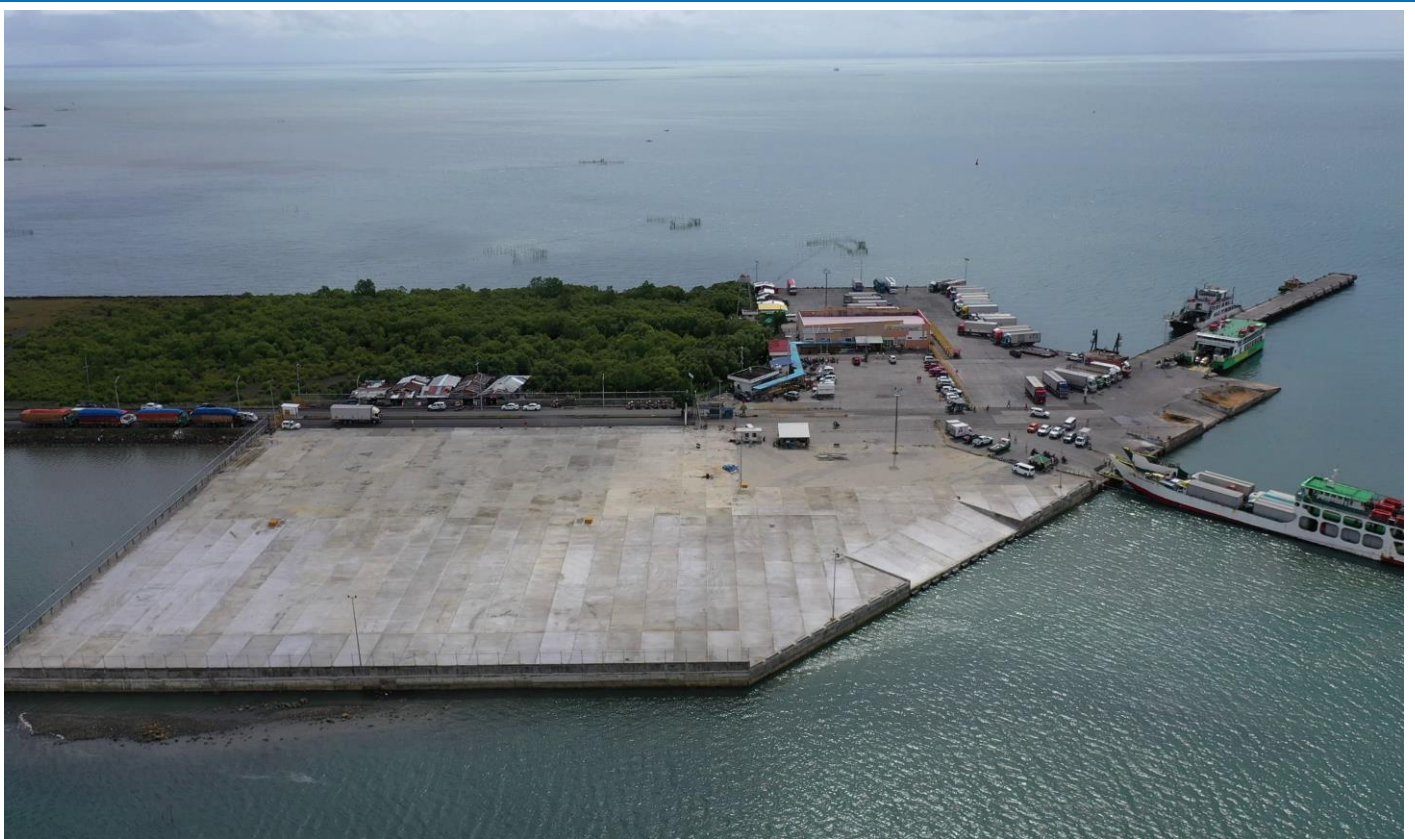

AFTER CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	:	CONSTRUCTION OF PORT OPERATIONS BUILDING AND RORO RAMP
LOCATION	:	PORT OF MAASIN, SOUTHERN LEYTE
CONTRACTOR	:	E.U. JINGCO CONSTRUCTION CORP.
SCOPE OF WORK	:	A. DEMOLITION AND REMOVAL WORKS B. CONSTRUCTION OF PORT OPERATIONS BUILDING
DATE OF BIDDING	:	16 January 2019
DATE OF AWARD	:	07 February 2019
DATE OF NOTICE TO PROCEED	:	02 May 2019
CONTRACT DURATION	:	420 calendar days
APPROVED BUDGET AMOUNT	:	₱48,544,352.27
SOURCE OF FUNDS	:	PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	:	PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	:	₱48,287,883.74
VARIATION ORDER NO. 1 (Change Order No. 1/ Extra Work Order No. 1)	:	₱4,003,725.83 - Covering the quantity adjustment of some of the original items of work and inclusion of additional works which are necessary for the protection, improvement and completion of the project and to suit actual field condition.
REVISED CONTRACT AMOUNT (First Revision)	:	₱52,291,609.57
RECAPITULATION	:	₱129,435.21 Covering the variance of the pre-determined quantities indicated in the BOQ as bid as against the actual quantities measured after the completion of the project.
REVISED CONTRACT AMOUNT (Final Revision)	:	₱52,421,044.78
EFFECTIVITY DATE	:	02 May 2019
ORIGINAL EXPIRY DATE	:	24 June 2020
TIME EXTENSION NO. 1/ TIME ADJUSTMENT NO. 1	:	270 calendar days - Covering the time needed for the demolition of the existing passenger terminal building and affected period for the construction of the proposed POB caused by pending completion of the necessary audit/inventory by COA to the materials stored in the existing PTB.
REVISED EXPIRY DATE (First Revision)	:	11 June 2021

**TIME EXTENSION NO. 2/
TIME ADJUSTMENT NO. 2**

122 calendar days

- Covering the delays caused by the unworkable weather condition and time elapsed brought by issued community quarantine restrictions by the Office of the Governor, Province of Southern Leyte due to continued surge of Covid-19 pandemic.

REVISED EXPIRY DATE

(Second Revision)

: 11 October 2021

**TIME EXTENSION NO. 3/
TIME ADJUSTMENT NO. 3**

52 calendar days

- Covering the delays caused by the unworkable weather condition

REVISED EXPIRY DATE

(Third Revision)

: 02 December 2021

TIME EXTENSION NO. 4

112 calendar days

- Covering the delays caused by (a) unworkable bad weather condition for the period October 10 to November 30, 2021, and (b) necessary restoration works on the damaged structures brought by super Typhoon "Odette" including cleaning/clearing of the entire construction area, delivery of new materials and finishing works.

REVISED EXPIRY DATE

(Fourth Revision)

: 24 March 2022

PROJECT STATUS


(As of 25 December 2022)

: - Completed as of 02 March 2022.

REMARKS:

: - As-built plans was approved on 16 May 2022 and Recapitulation was approved on 03 June 2022.

CONSTRUCTION OF PORT OPERATIONS BUILDING AND RORO RAMP PORT OF MAASIN, SOUTHERN LEYTE

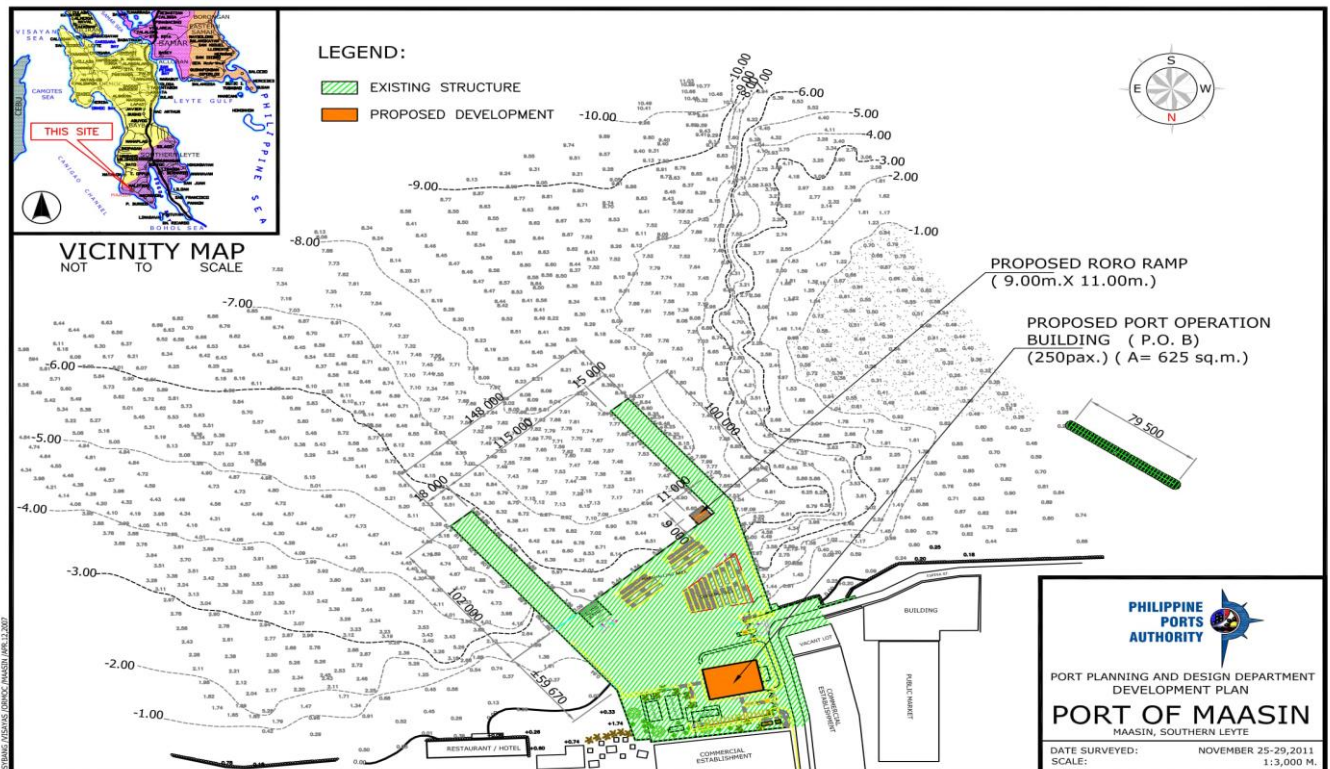

DEVELOPMENT PLAN




AFTER CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	: BASIAO PORT DEVELOPMENT PROJECT
LOCATION	: PORT OF BASIAO, IVISAN, CAPIZ
CONTRACTOR	: J.S. LAYSON & COMPANY, INC.
SCOPE OF WORK	: A. BACK-UP AREA AND CAUSEWAY B. RORO RAMP
DATE OF BIDDING	: 19 December 2019
DATE OF AWARD	: 24 January 2020
DATE OF NOTICE TO PROCEED	: 26 May 2020
CONTRACT DURATION	: 300 <i>calendar days</i>
APPROVED BUDGET AMOUNT	: ₱61,647,135.01
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱60,400,000.00
RECAPITULATION	: ₱281,781.77 Covering the variance of the pre-determined quantities indicated in the BOQ as bid as against the actual quantities measured after the completion of the project.
REVISED CONTRACT AMOUNT (Final Revision)	: ₱60,681,781.77
EFFECTIVITY DATE	: 08 June 2020
ORIGINAL EXPIRY DATE	: 03 April 2021
TIME EXTENSION NO. 1 / TIME ADJUSTMENT NO. 1	: 100 <i>calendar days</i> Covering the delays caused by the unworkable weather condition and time elapsed due to travel restriction implemented by the Municipality of Ivisan brought by the extreme quarantine protocols to prevent the spread of COVID-19 virus.
LATEST REVISED EXPIRY DATE (First Revision)	: 12 July 2021
PROJECT STATUS	: - Completed as of 30 June 2021.
REMARKS	: - Recapitulation was approved on 20 January 2022.

BASIAO PORT DEVELOPMENT PROJECT PORT OF BASIAO, IVISAN, CAPIZ

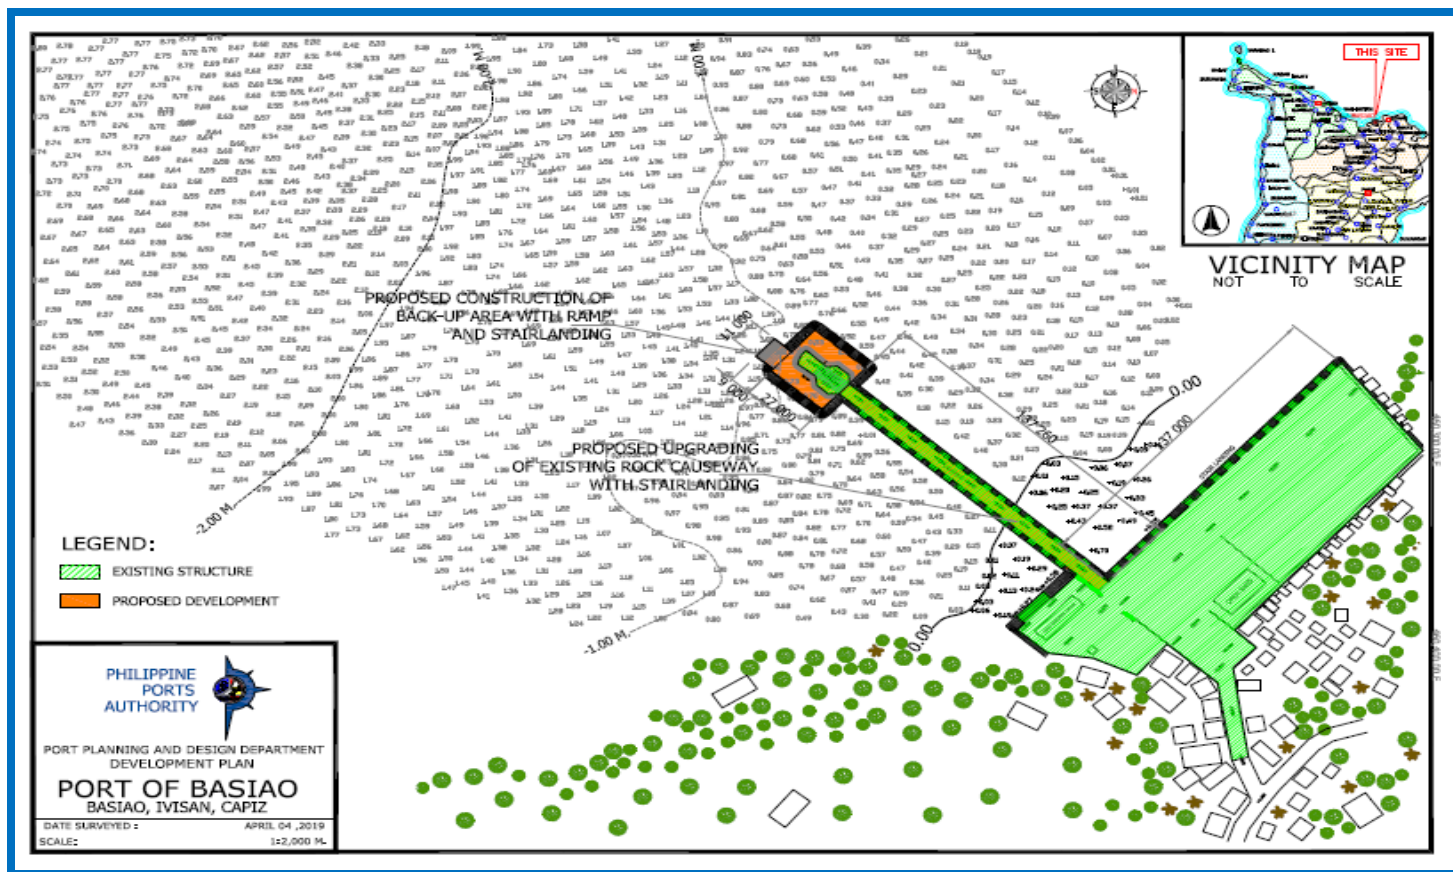

DEVELOPMENT PLAN



AFTER CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	: ALEGRIA PORT DEVELOPMENT PROJECT
LOCATION	: PORT OF ALEGRIA, BURUANGA, AKLAN
CONTRACTOR	: IBC INTERNATIONAL BUILDERS CORPORATION
SCOPE OF WORK	: <ul style="list-style-type: none">A. CONSTRUCTION OF BACK-UP AREA (Area = 3,073 sq.m.)B. RC PLATFORM 1 (Area = 1,308 sq.m.)C. RC PLATFORM 2 (Area = 1,224 sq.m.)D. RC PIER (Area = 1,344 sq.m.)E. RORO RAMP, 2 UNITS (Area = 198 sq.m.)F. BREASTING DOLPHING. PORT LIGHTING SYSTEM
DATE OF BIDDING	: 10 December 2019
DATE OF AWARD	: 24 January 2020
DATE OF NOTICE TO PROCEED	: 23 June 2020
CONTRACT DURATION	: <i>540 calendar days</i>
APPROVED BUDGET AMOUNT	: ₱217,619,862.09
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱214,850,000.00
EFFECTIVITY DATE	: 31 July 2020
ORIGINAL EXPIRY DATE	: 21 January 2022
TIME EXTENSION NO. 1 / TIME ADJUSTMENT NO. 1	: 177 calendar days Covering the delays caused by the unworkable days brought by bad weather / rough sea conditions for the period July 31, 2020 to October 25, 2021.
REVISED EXPIRY DATE (First Revision)	: 17 July 2022
TIME ADJUSTMENT NO. 2	: 120 calendar days - Covering the delays caused by the unworkable days brought by bad weather / rough sea conditions for the period 26 October 2021 to 25 April 2022.
REVISED EXPIRY DATE (Second Revision)	: 17 July 2022

TIME EXTENSION NO. 2**: 111 *calendar days***

Covering the delays caused by the unworkable days brought by bad weather / rough sea conditions for the period 26 October 2021 to 25 April 2022.

LATEST REVISED EXPIRY DATE**: 05 November 2022**

(Third Revision)

PROJECT STATUS


(As of 25 January 2023)

: - The project is 64.587% complete with a negative slippage of 35.413%.

REMARKS:

- : - On-going.
- Negative slippage was due to unworkable weather condition and slow pacing of work by the contractor.
 - Warning letters were sent to the contractor to undertake measures to cope with the project's delay.
 - Contractor's request for time extension is under evaluation.

ALEGRIA PORT DEVELOPMENT PROJECT PORT OF ALEGRIA, BURUANGA, AKLAN

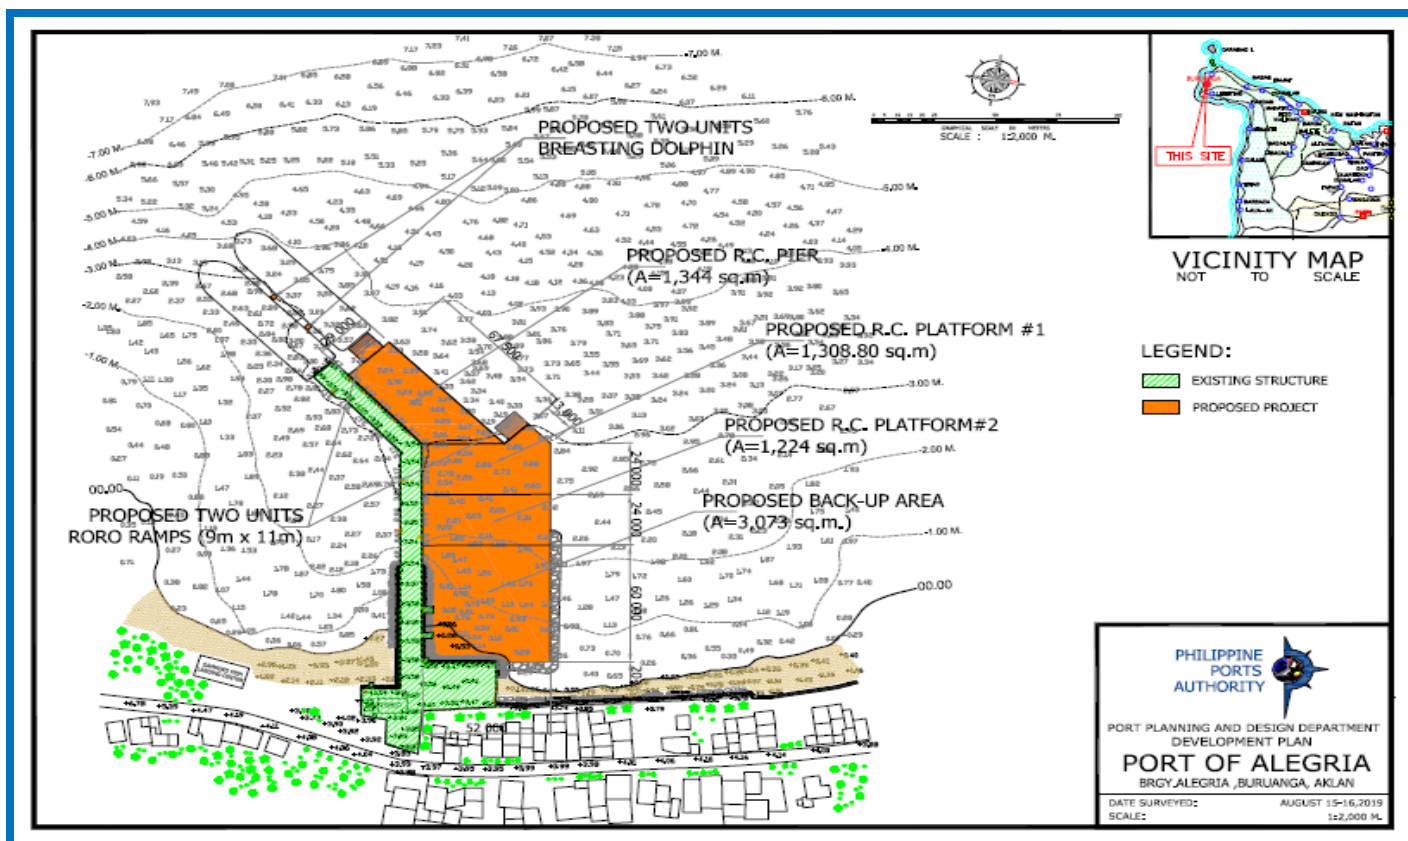

DEVELOPMENT PLAN



ONGOING CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	: CONSTRUCTION OF ADDITIONAL FASTCRAFT BERTH, PORT OF TAGBILARAN, BOHOL
LOCATION	: PORT OF TAGBILARAN, BOHOL
CONTRACTOR	: E.U. JINGCO CONSTRUCTION CORPORATION
SCOPE OF WORK	: A. FASTCRAFT BERTH B. COVERED WALKWAY
DATE OF BIDDING	: 30 October 2019
DATE OF AWARD	: 27 November 2019
DATE OF NOTICE TO PROCEED	: 26 February 2020
CONTRACT DURATION	: 360 <i>calendar days</i>
APPROVED BUDGET AMOUNT	: ₱88,486,427.13
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)

ORIGINAL CONTRACT AMOUNT : **₱88,032,936.61**

RECAPITULATION : **(37,040.46)**
Covering the variance of the pre-determined quantities indicated in the Bill of Quantities (BOQ) as bid as against the actual quantities measured after the completion of the project.

REVISED CONTRACT AMOUNT : **₱87,995,896.15**

EFFECTIVITY DATE : **26 February 2020**

ORIGINAL EXPIRY DATE : **19 February 2021**


TIME EXTENSION NO. 1 : **87 calendar days**
- Covering the delays caused by the unworkable weather condition and time elapsed of the suspended period caused by the imposition of Enhanced Community Quarantine (ECQ) brought by COVID-19 crisis throughout the island of Luzon and in other parts of the Philippines.

LATEST (1) REVISED EXPIRY DATE : **17 May 2021**

PROJECT STATUS : - Completed as of 25 June 2021.

REMARKS: :

CONSTRUCTION OF ADDITIONAL FASTCRAFT BERTH, PORT OF TAGBILARAN, BOHOL

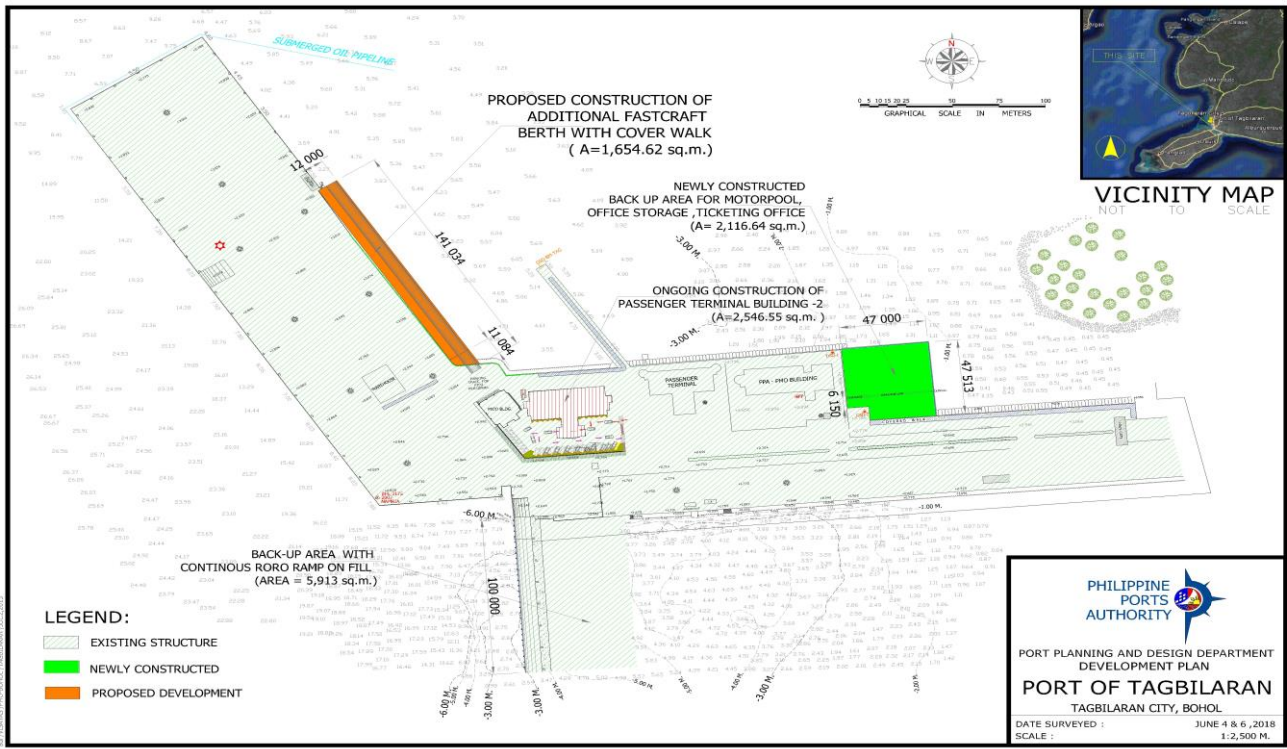

DEVELOPMENT PLAN



AFTER CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	:	CONSTRUCTION OF BACK-UP AREA WITH CONTINUOUS RORO RAMP & POB
LOCATION	:	PORT OF TUBIGON, BOHOL
CONTRACTOR	:	MAMSAR CONSTRUCTION & INDUSTRIAL CORPORATION/JFAP CONSTRUCTION -JV
SCOPE OF WORK	:	A. BACK-UP AREA WITH CONTINUOUS RORO RAMP ON-FILL B. PORT OPERATIONS BUILDING
DATE OF BIDDING	:	03 January 2020
DATE OF AWARD	:	24 January 2020
DATE OF NOTICE TO PROCEED	:	02 March 2020
CONTRACT DURATION	:	660 <i>calendar days</i>
APPROVED BUDGET AMOUNT	:	₱448,813,753.33
SOURCE OF FUNDS	:	PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	:	PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	:	₱445,388,282.65
VARIATION ORDER NO. 1 (Change Order No. 1/ Extra Work Order No. 1)	:	₱40,930,802.02 - Covering the quantity adjustments brought by the additional quantities due to the presence of upheaved unsuitable materials and overrun/underrun of some of the items of works as per approved BOQ.
REVISED CONTRACT AMOUNT (First Revision)	:	₱486,319,084.67
EFFECTIVITY DATE	:	16 March 2020
ORIGINAL EXPIRY DATE	:	04 January 2022
TIME EXTENSION NO. 1	:	195 <i>calendar days</i> Covering the delays caused by issued suspension order by the Provincial Government of Bohol to all quarry permits/operations and implementation of Legal Compliance Audit to all quarry permit holders and time elapsed for the suspended period caused by the imposition of Enhanced community Quarantine (ECQ) due to COVID-19 pandemic.
REVISED EXPIRY DATE (First Revision)	:	18 July 2022
TIME EXTENSION NO. 2	:	135 <i>calendar days</i> Due to Variation Order No. 1
REVISED EXPIRY DATE (Second Revision)	:	30 November 2022

TIME EXTENSION NO. 3**: 124 calendar days**

Covering the delays caused by the unworkable weather condition for the period 20 March to August 2022 and the necessary time of the restoration works on the damaged structures brought by Typhoon Odette including cleaning/clearing of the project site and delivery of new materials.

LATEST REVISED EXPIRY DATE**: 03 April 2023**

(Third Revision)

PROJECT STATUS


(As of 25 January 2023)

: - The project is 80.168% complete with a negative slippage of 11.268%.

REMARKS:

- : - On-going.
- Negative slippage was due to unworkable weather condition.
- Warning letters were sent to the contractor to undertake measures to cope with the project's delay

CONSTRUCTION OF BACK-UP AREA WITH CONTINUOUS RORO RAMP & POB PORT OF TUBIGON, BOHOL

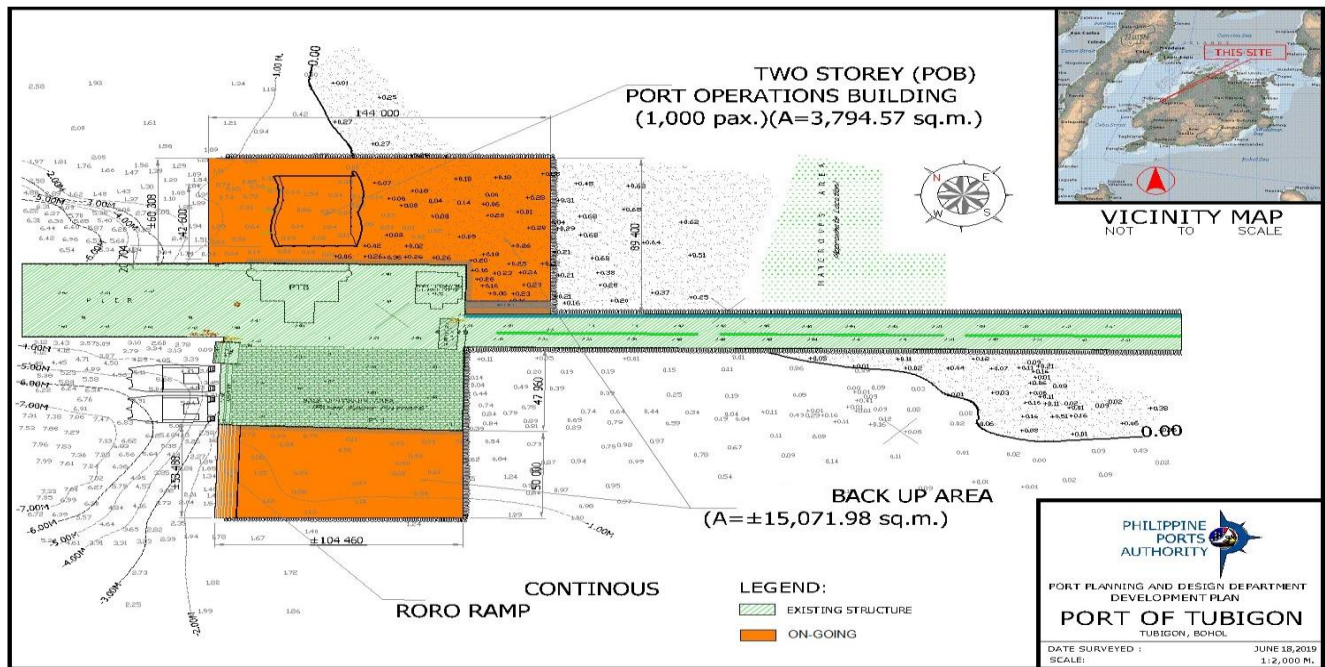

DEVELOPMENT PLAN




ONGOING CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	: REHABILITATION/UPGRADING OF EXISTING BACK-UP AREA AND CONSTRUCTION OF PORT OPERATIONS BUILDING (POB)
LOCATION	: PORT OF MAGUINO-O, CALBAYOG, SAMAR
CONTRACTOR	: BEMKAR CONSTRUCTION
SCOPE OF WORK	: A. REHABILITATION / UPGRADING OF EXISTING BACK-UP AREA A= 3,033.63 SQ.M. B. PORT OPERATIONS BUILDING
DATE OF BIDDING	: 15 December 2020
DATE OF AWARD	: 21 January 2021
DATE OF NOTICE TO PROCEED	: 10 March 2021
CONTRACT DURATION	: <i>450 calendar days</i>
APPROVED BUDGET AMOUNT	: <i>₱184,417,467.46</i>
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: <i>₱183,467,708.62</i>
EFFECTIVITY DATE	: 18 March 2021
ORIGINAL EXPIRY DATE	: 10 June 2022
TIME EXTENSION NO. 1	: <i>102 calendar days</i> Covering the delays caused by unworkable weather condition.
REVISED EXPIRY DATE	: 20 September 2022
LATEST TIME EXTENSION NO. 2	: <i>117 calendar days</i> Covering the delays caused by the unworkable weather condition for the period March 2022 to September 2022 and the delays incurred by the requested phasing of work for the construction of POB.
REVISED EXPIRY DATE	: 15 January 2023
PROJECT STATUS (As of 25 January 2023)	: - The project is 96.338% complete with a negative slippage of 3.662%.
REMARKS	: - On-going. - Negative slippage of the project was due to unworkable weather condition.

REHABILITATION/UPGRADING OF EXISTING BACK-UP AREA AND CONSTRUCTION OF PORT OPERATIONS BUILDING (POB)
PORT OF MAGUINO-O, CALBAYOG, SAMAR

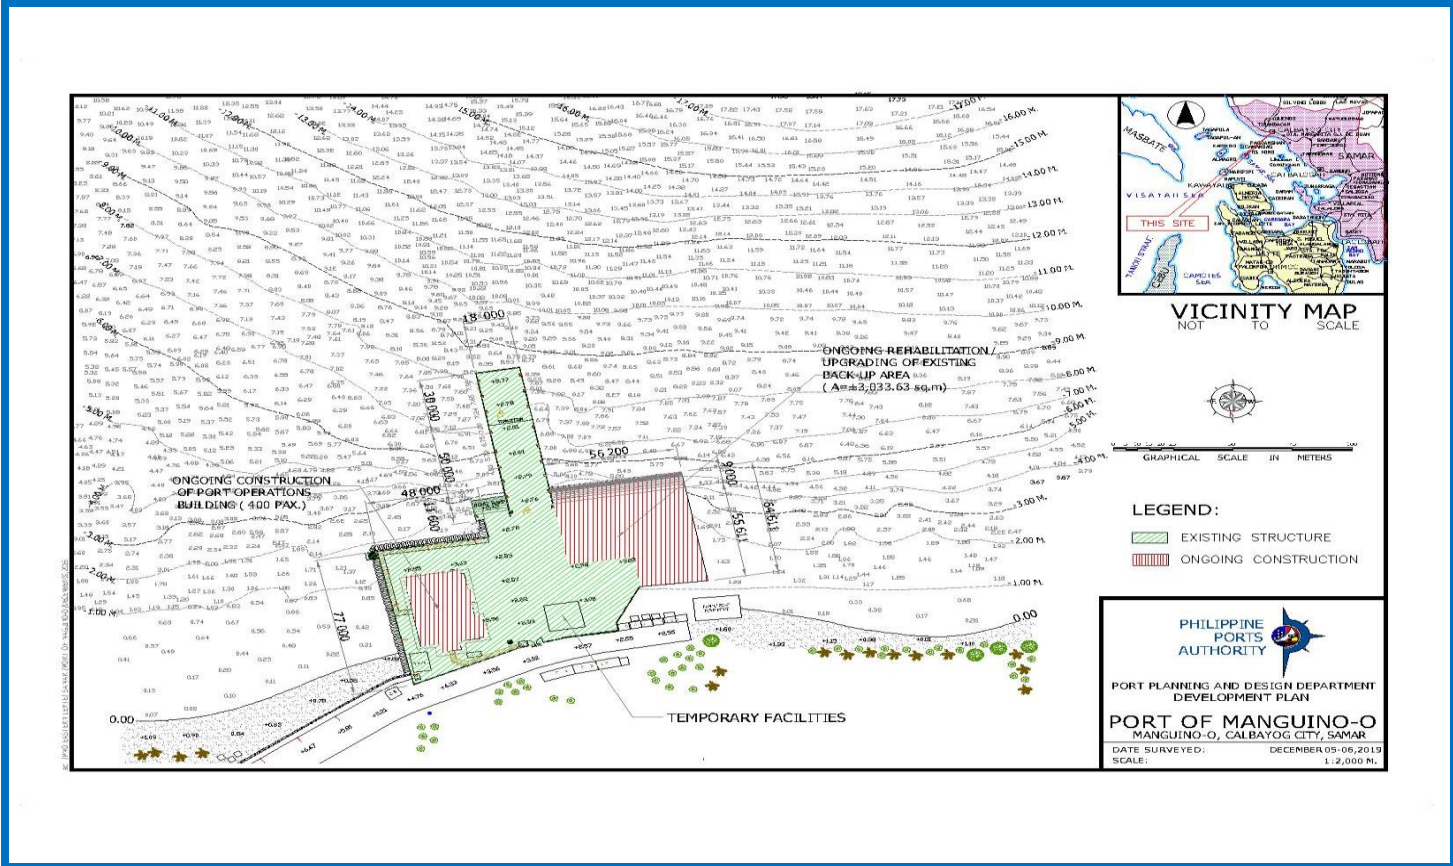

DEVELOPMENT PLAN




ONGOING CONSTRUCTION


PROJECT BRIEF

PROJECT TITLE	: CONSTRUCTION OF WHARF AND PORT OPERATIONAL AREA WITH CONTINUOUS RORO RAMP
LOCATION	: PORT OF CATAGBACAN, LOON, BOHOL
CONTRACTOR	: MAMSAR CONST. & INDUSTRIAL CORP.
SCOPE OF WORK	: A. CONSTRUCTION OF PORT OPERATIONAL AREA B. CONSTRUCTION OF RC WHARF
DATE OF BIDDING	: 21 October 2021
DATE OF AWARD	: 11 November 2021
DATE OF NOTICE TO PROCEED	: 06 December 2021
CONTRACT DURATION	: 720 calendar days
APPROVED BUDGET AMOUNT	: ₱669,307,773.87
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱666,988,000.00
VARIATION ORDER NO. 1 (Change Order No. 1/ Extra Work Order No. 1)	: ₱26,571,868.01 - Covering the additional works brought by the inclusions of dredging and disposal of existing seabed materials up to the designed elevation necessary for the safety of the calling vessels and to optimize the efficiency of the Port of Catagbacan.
REVISED CONTRACT AMOUNT (First Revision)	: ₱693,559,868.01
EFFECTIVITY DATE	: 17 December 2021
ORIGINAL EXPIRY DATE	: 06 December 2023
PROJECT STATUS (As of 25 January 2023)	: - The project is 60.322% complete and progressing ahead by 0.052%.
REMARKS	: - On-going. - Variation Order covering the additional works brought by inclusion of dredging and disposal of existing seabed materials necessary for the safety of the calling vessels and to optimize the efficiency of port was approved on 20 January 2023.

CONSTRUCTION OF WHARF AND PORT OPERATIONAL AREA WITH CONTINUOUS RORO RAMP PORT OF CATAGBACAN, LOON, BOHOL

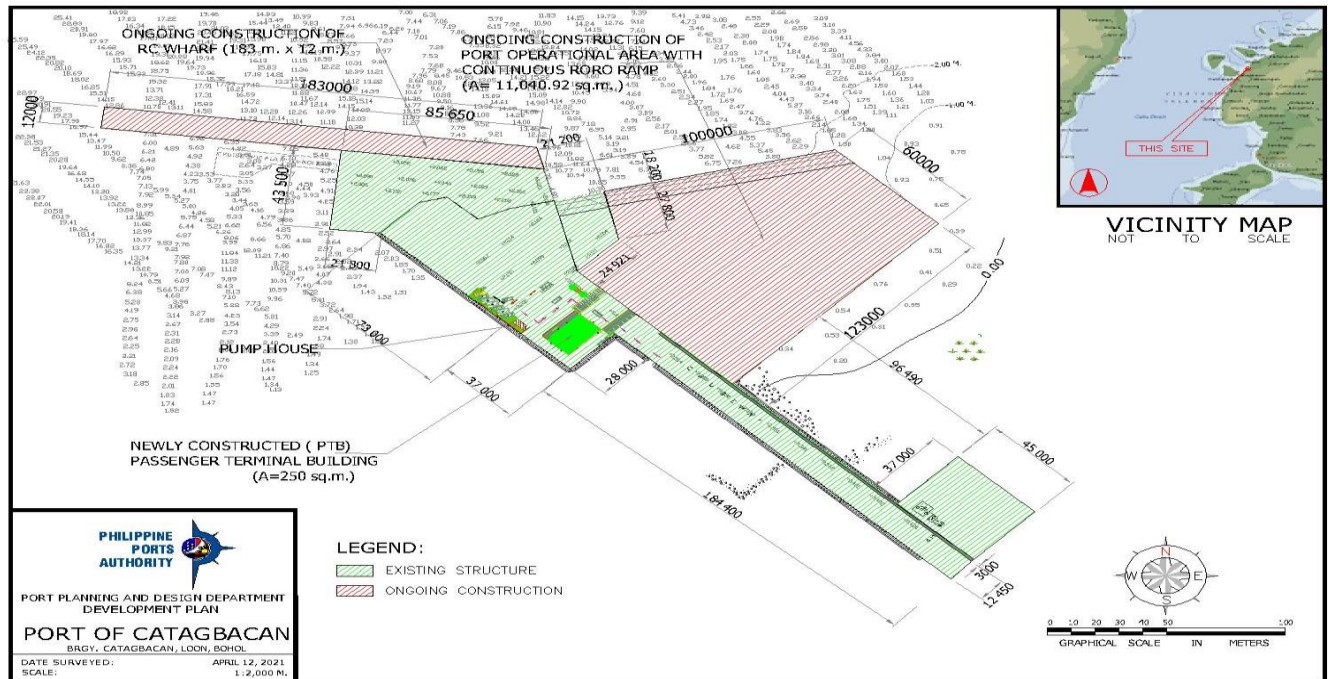

DEVELOPMENT PLAN

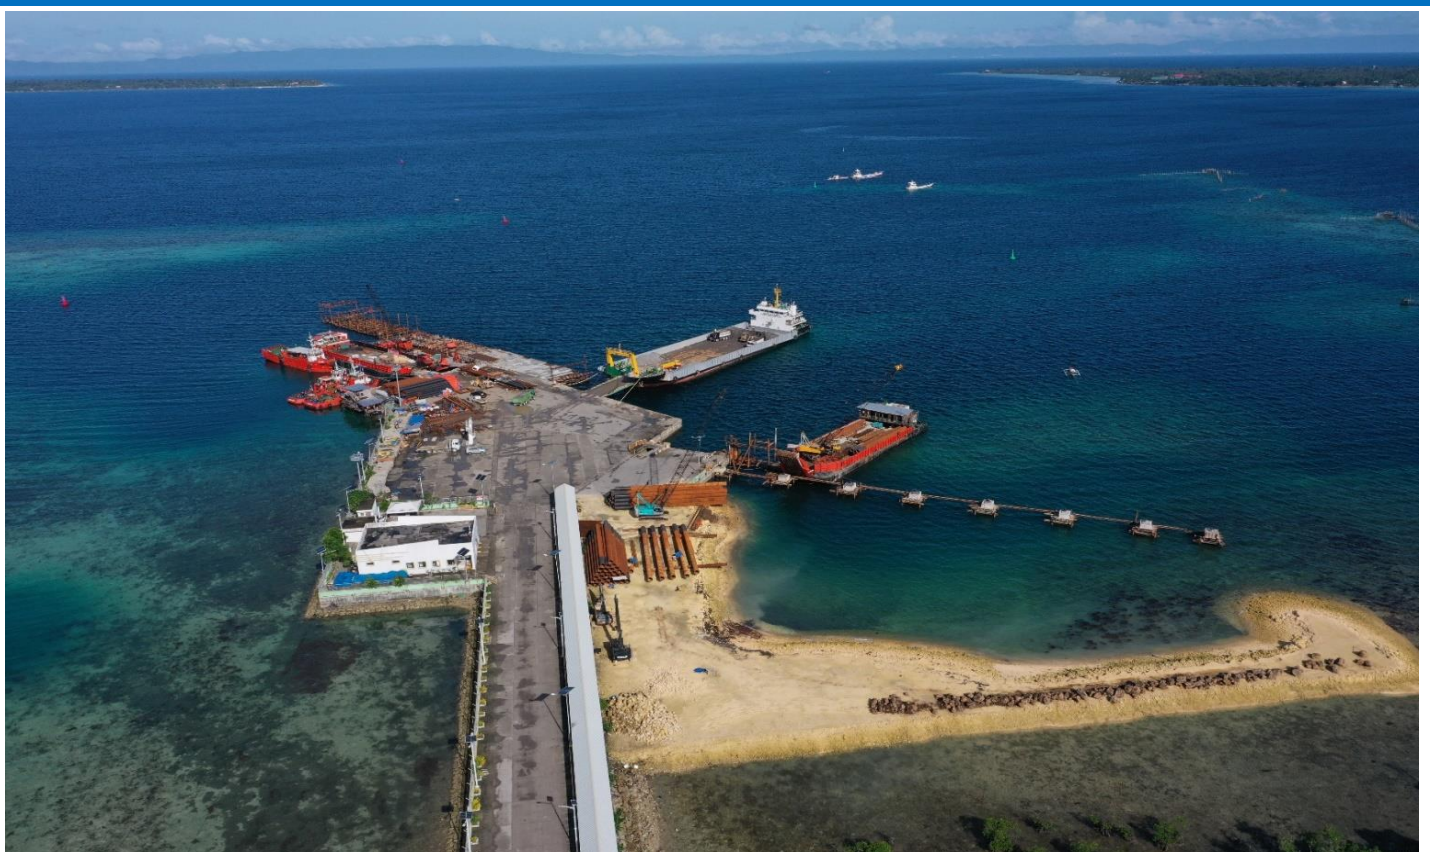


ONGOING CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	: FORT SAN PEDRO PORT EXPANSION PROJECT
LOCATION	: PORT OF SAN PEDRO, ILOILO CITY
CONTRACTOR	: IBC INTERNATIONAL BUILDERS CORP.
SCOPE OF WORK	: A. BACK-UP AREA B. RC WHARF
DATE OF BIDDING	: 06 July 2021
DATE OF AWARD	: 29 July 2021
DATE OF NOTICE TO PROCEED	: 15 September 2021
CONTRACT DURATION	: 660 <i>calendar days</i>
APPROVED BUDGET AMOUNT	: ₱305,306,259.48
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱302,887,999.91
EFFECTIVITY DATE	: 16 September 2021
ORIGINAL EXPIRY DATE	: 07 July 2023
PROJECT STATUS	: - The project is 7.692% completed
(As of 25 January 2023)	
REMARKS	: - Suspended due to pending issuance of Environmental Compliance Certificate (ECC).

FORT OF SAN PEDRO PORT EXPANSION PROJECT

PORT OF SAN PEDRO, ILOILO CITY

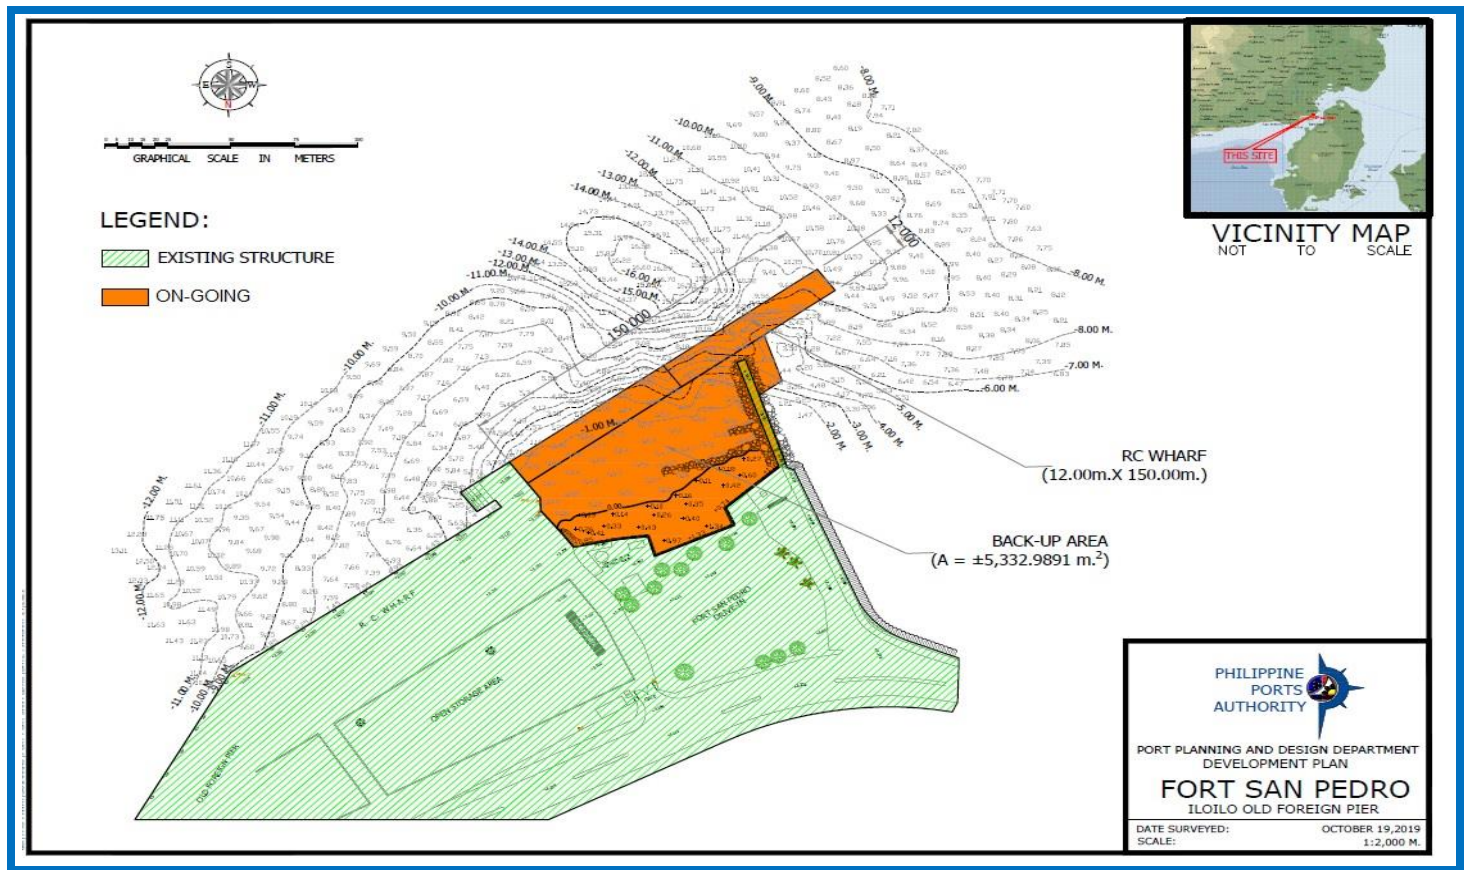

DEVELOPMENT PLAN




ONGOING CONSTRUCTION


PROJECT BRIEF

PROJECT TITLE	: EXTENSION OF ROCK CAUSEWAY AND CONSTRUCTION RC PIER
LOCATION	: PORT OF BASIAO, IVISAN, CAPIZ
CONTRACTOR	: IBC INTERNATIONAL BUILDERS CORP.
SCOPE OF WORK	: A. EXTENSION OF ROCK CAUSEWAY B. CONSTRUCTION OF RC PIER
DATE OF BIDDING	: 30 September 2021
DATE OF AWARD	: 26 October 2021
DATE OF NOTICE TO PROCEED	: 13 December 2021
CONTRACT DURATION	: 480 calendar days
APPROVED BUDGET AMOUNT	: ₱169,711,663.70
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱167,799,952.60
EFFECTIVITY DATE	: 15 December 2021
ORIGINAL EXPIRY DATE	: 08 April 2023
PROJECT STATUS (As of 25 January 2023)	: - Suspended due to pending issuance of Environmental Compliance Certificate (ECC) and request for revision of plans / re-orientation of causeway.

EXTENSION OF ROCK CAUSEWAY AND CONSTRUCTION RC PIER PORT OF BASIAO, IVISAN, CAPIZ

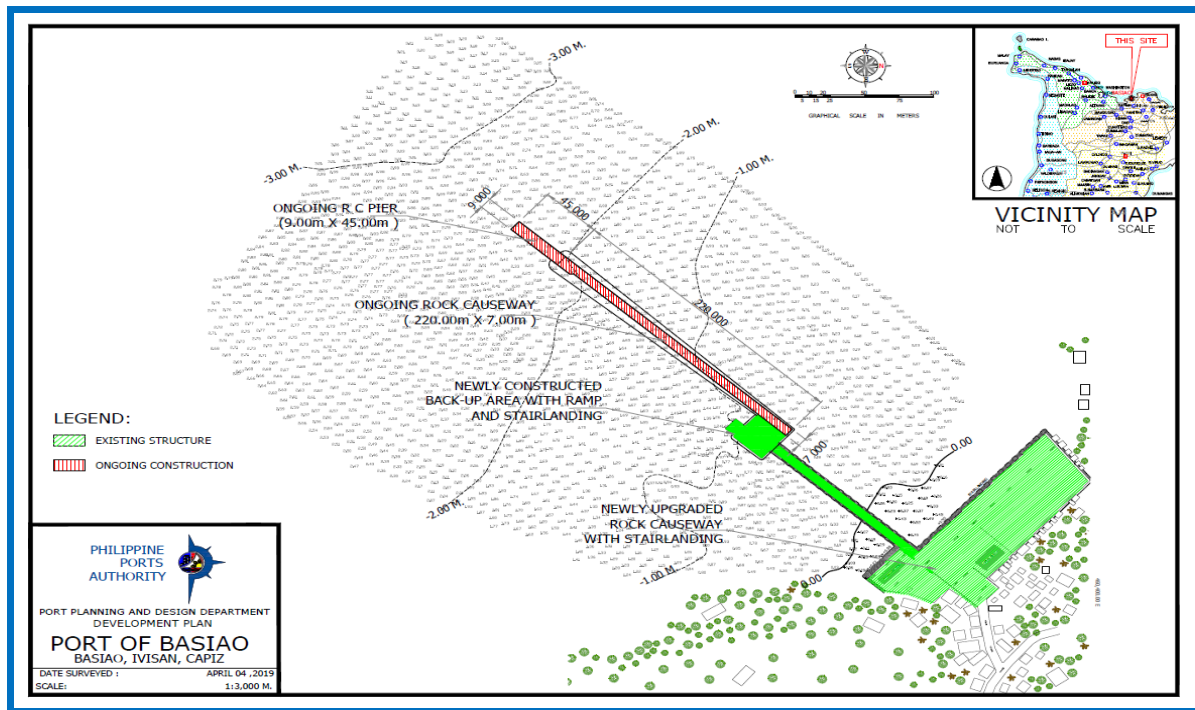

DEVELOPMENT PLAN

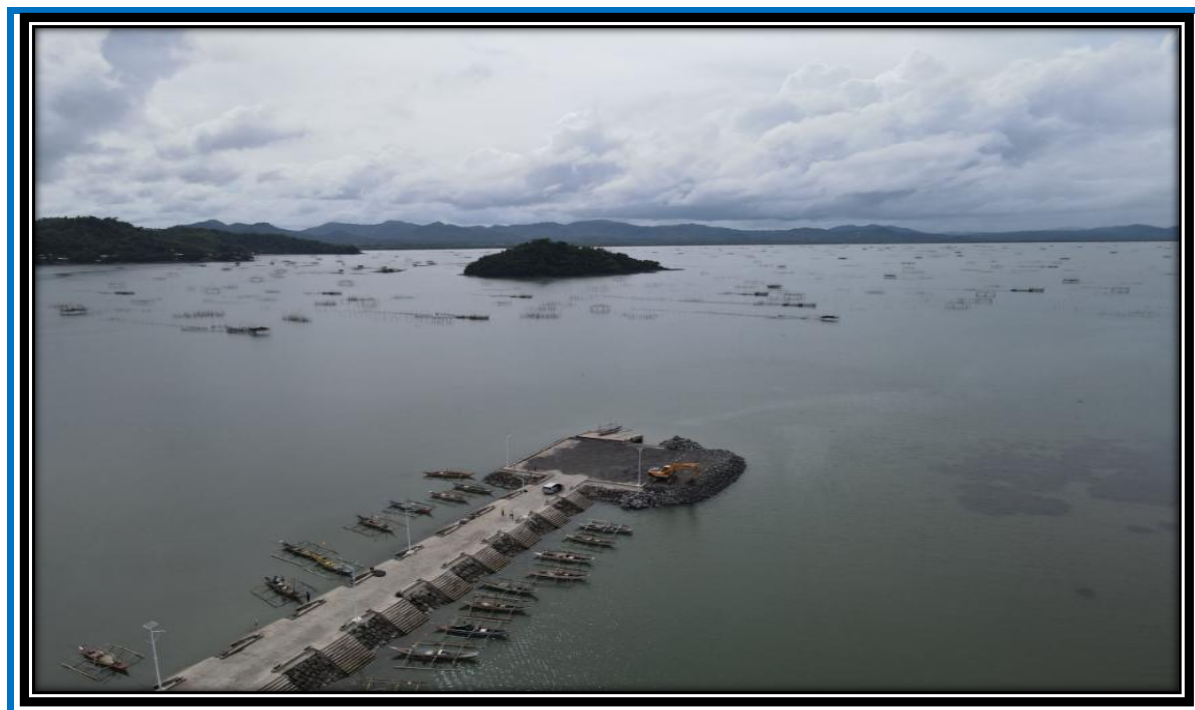


ONGOING CONSTRUCTION


PROJECT BRIEF

PROJECT TITLE	: EXTENSION OF R.C. WHARF
LOCATION	: PORT OF CULASI, ROXAS CITY, CAPIZ
CONTRACTOR	: J.S. LAYSON & CO., INC.
SCOPE OF WORK	: A. EXTENSION OF R.C. WHARF
DATE OF BIDDING	: 29 July 2021
DATE OF AWARD	: 07 September 2021
DATE OF NOTICE TO PROCEED	: 25 October 2021
CONTRACT DURATION	: 300 <i>calendar days</i>
APPROVED BUDGET AMOUNT	: ₱62,031,346.03
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱61,588,000.00
EFFECTIVITY DATE	: 27 October 2021
ORIGINAL EXPIRY DATE	: 22 August 2022
TIME EXTENSION NO. 1	: 100 <i>calendar days</i> - Covering the delays caused by unworkable bad weather / rough sea conditions for the period 27 October 2021 to 25 July 2022.
REVISED EXPIRY DATE (First Revision)	: 14 November 2022
TIME EXTENSION NO. 2	: 51 <i>calendar days</i> Covering the delays due to delays caused by unworkable bad weather / rough sea conditions for the period 26 July to 25 October 2022.
REVISED EXPIRY DATE (Second Revision)	: 04 January 2023
PROJECT STATUS (As of 25 January 2023)	: - The project is 98.502% complete with a negative slippage of 1.498%.
REMARKS	: - On-going.

EXTENSION OF R.C. WHARF PORT OF CULASI, ROXAS CITY, CAPIZ

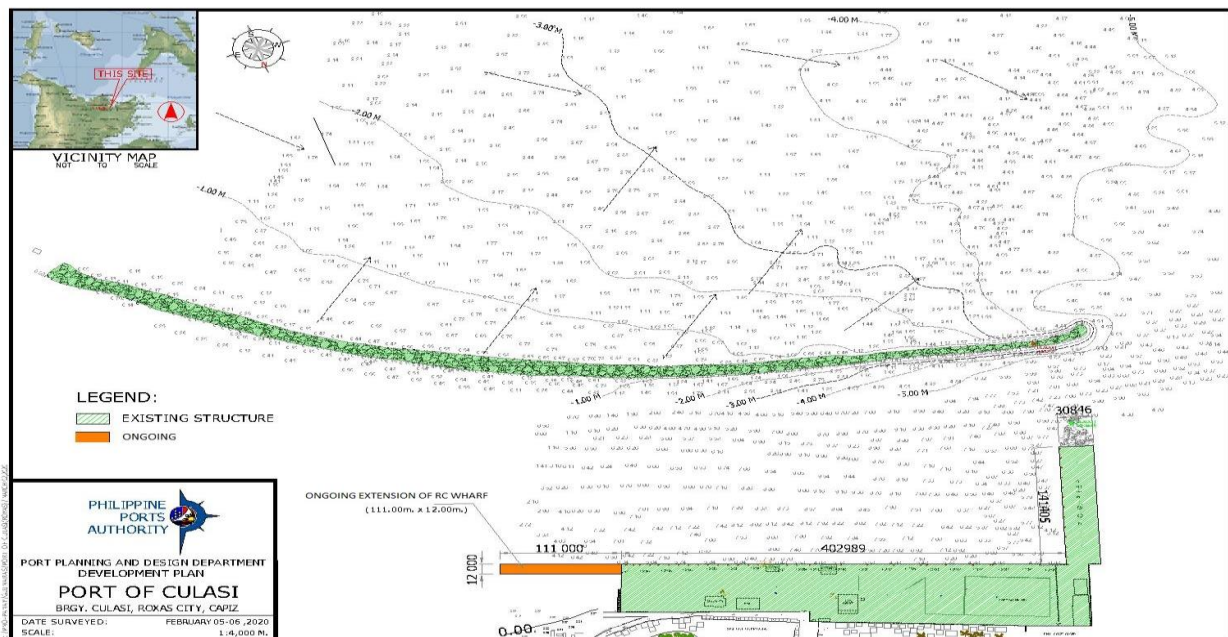

DEVELOPMENT PLAN

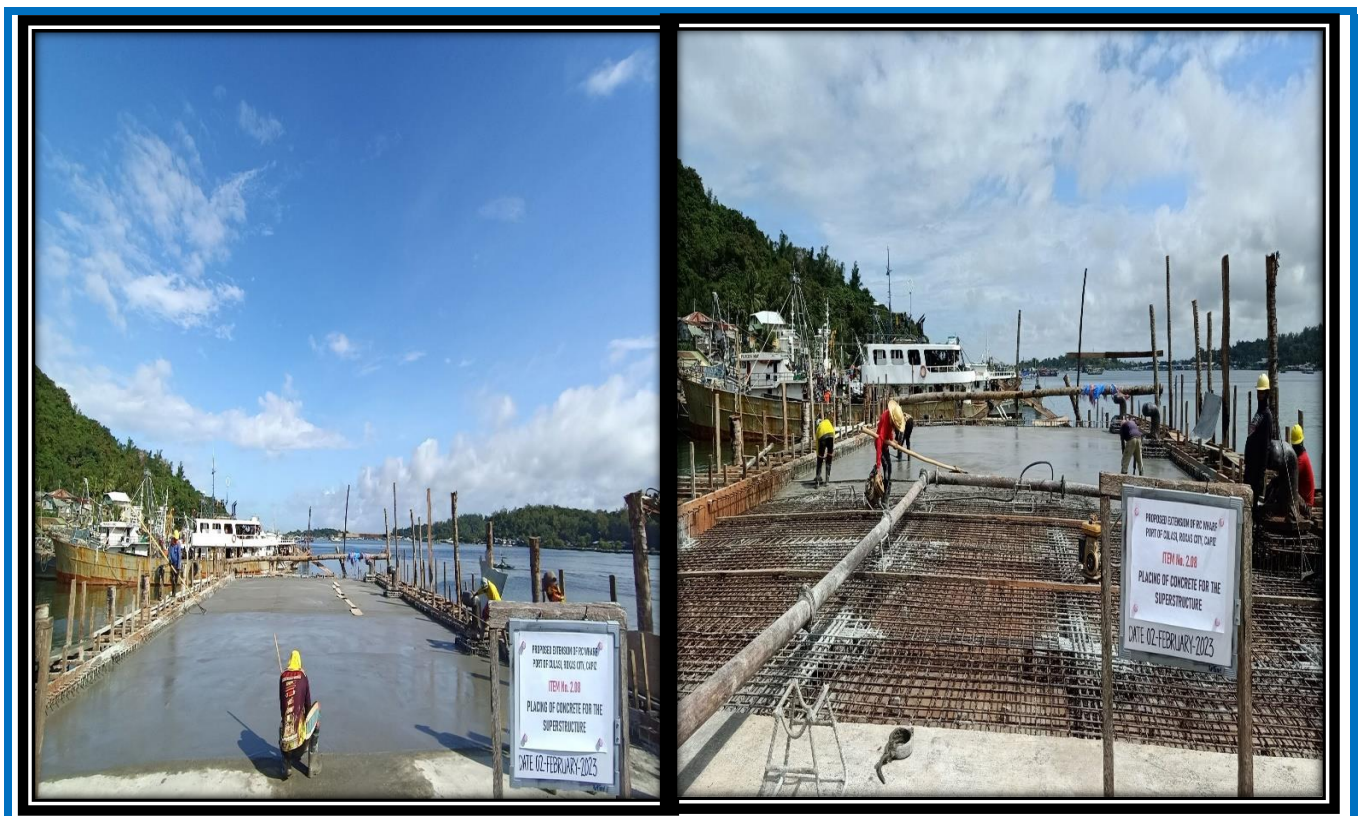


ONGOING CONSTRUCTION


PROJECT BRIEF

PROJECT TITLE	: CONSTRUCTION OF BACK-UP AREA AND RC PIER
LOCATION	: PORT OF TAGBILARAN, BOHOL
CONTRACTOR	: MAMSAR CONST. & INDUSTRIAL CORP./ JFAP CONSTRUCTION/JV
SCOPE OF WORK	: A. BACK-UP AREA (12,061.30 SQ.M.) B. RC PIER (15M X 150M)
DATE OF BIDDING	: 30 June 2021
DATE OF AWARD	: 27 July 2021
DATE OF NOTICE TO PROCEED	: 18 August 2021
CONTRACT DURATION	: 600 <i>calendar days</i>
APPROVED BUDGET AMOUNT	: ₱491,652,486.14
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱486,958,358.23
EFFECTIVITY DATE	: 23 August 2021
ORIGINAL EXPIRY DATE	: 14 April 2023
PROJECT STATUS (As of 25 January 2023)	: - The project is 73.855% complete with a negative slippage of 14.035%.
REMARKS:	: - On-going. - Negative slippage was due to unworkable weather condition. - Contractor's request for time extension is under evaluation.

CONSTRUCTION OF BACK-UP AREA AND RC PIER PORT OF TAGBILARAN, BOHOL

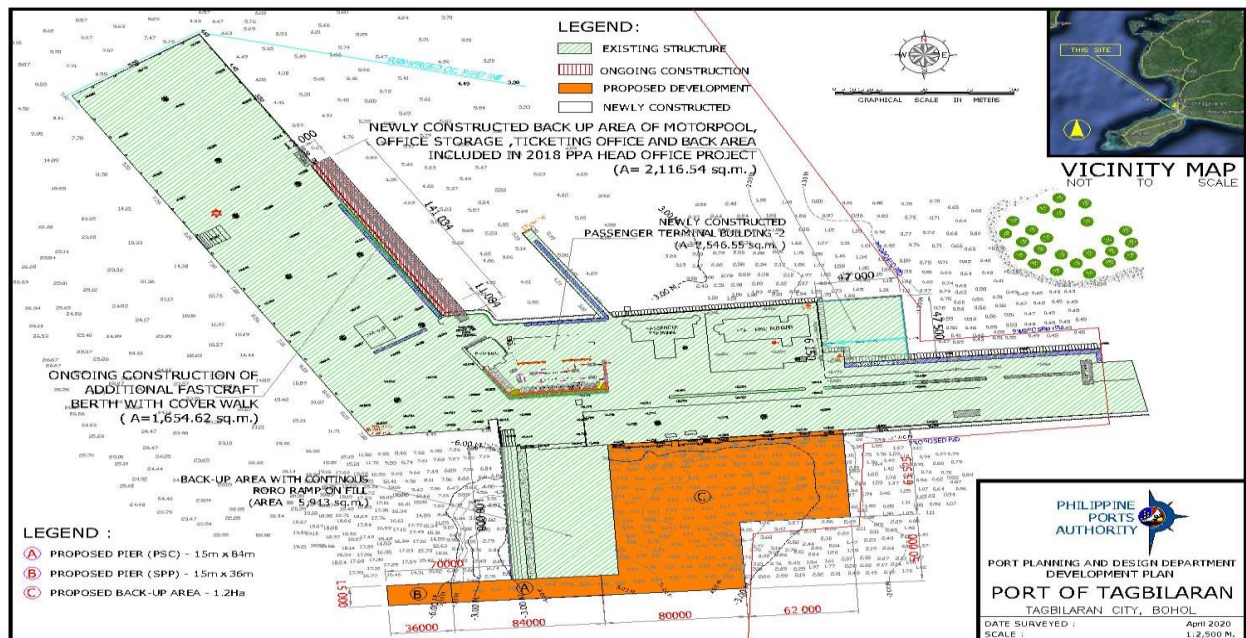

DEVELOPMENT PLAN

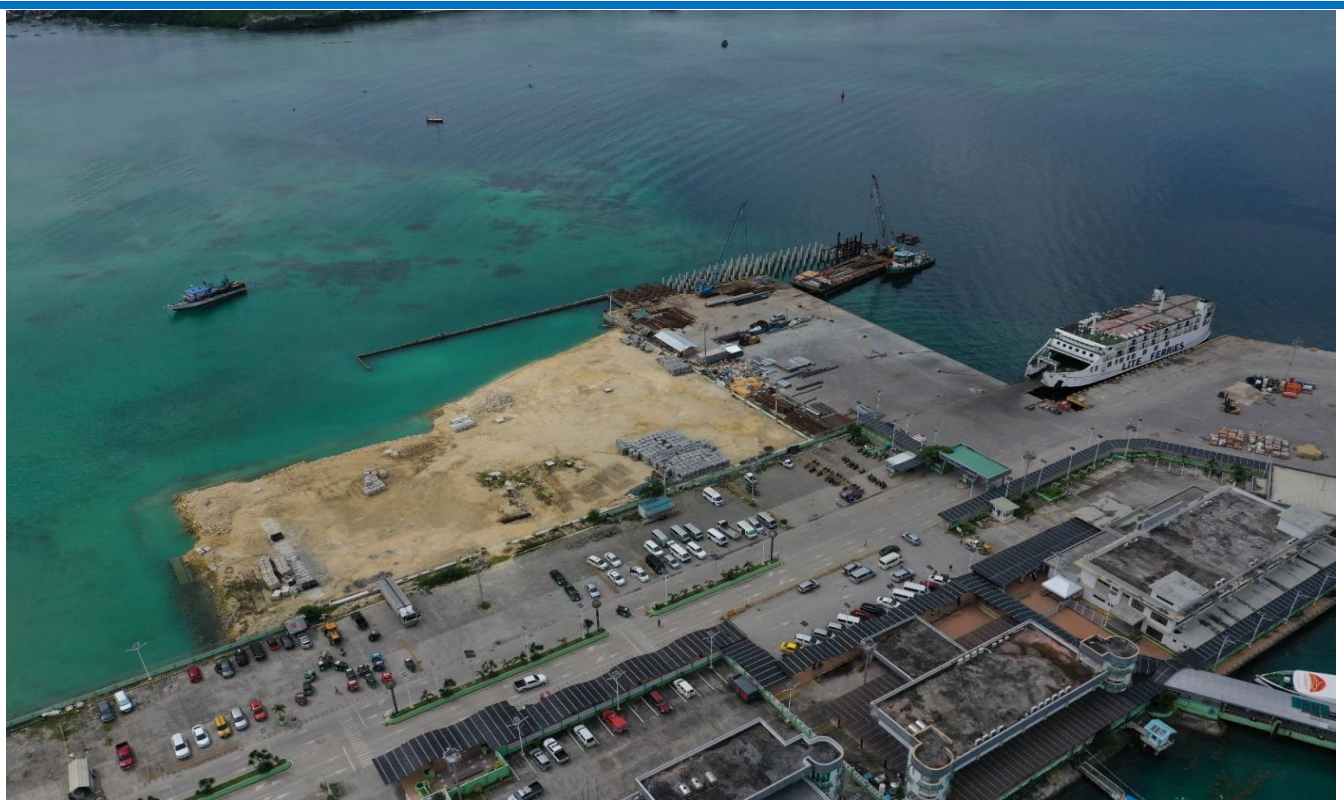


ONGOING CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	: CONSTRUCTION OF PASSENGER TERMINAL BUILDING (PTB)
LOCATION	: PORT OF UBAY
CONTRACTOR	: JFAP CONSTRUCTION
SCOPE OF WORK	: A. PASSENGER TERMINAL BUILDING
DATE OF BIDDING	: 12 January 2021
DATE OF AWARD	: 27 January 2021
DATE OF NOTICE TO PROCEED	: 23 March 2021
CONTRACT DURATION	: 450 calendar days
APPROVED BUDGET AMOUNT	: ₱87,464,312.09
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱86,936,163.03
EFFECTIVITY DATE	: 26 March 2021
ORIGINAL EXPIRY DATE	: 18 June 2022
TIME EXTENSION NO. 1	149 calendar days <ul style="list-style-type: none">- Covering the delays caused by (a) unworkable bad weather condition for the period 26 March 2021 to 25 April 2022, and (b) necessary restoration works on the damaged structures brought by super typhoon "Odette" including cleaning / clearing of the entire construction area and delivery of new construction materials.
LATEST REVISED EXPIRY DATE (First Revision)	: 14 November 2022
PROJECT STATUS (As of 25 January 2023)	: - The project is 87.918% complete with a negative slippage of 12.082%.
REMARKS:	: - On-going. <ul style="list-style-type: none">- Negative slippage was due to unworkable weather condition.- Warning letters were sent to the contractor to fast track the completion of the project.- Contractor's request for time extension is under evaluation.

CONSTRUCTION OF PASSENGER TERMINAL BUILDING (PTB) PORT OF UBAY

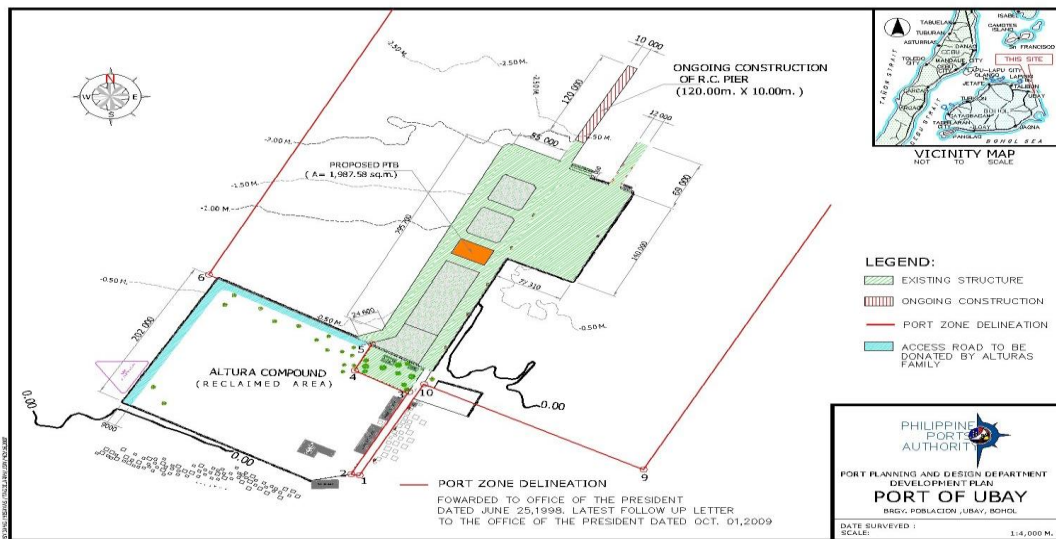

DEVELOPMENT PLAN




ONGOING CONSTRUCTION


PROJECT BRIEF

PROJECT TITLE	: JAGNA PORT EXPANSION PROJECT
LOCATION	: PORT OF JAGNA, JAGNA, BOHOL
CONTRACTOR	: PREMIUM MEGASTRUCTURES, INC.
SCOPE OF WORK	: A. BACK-UP AREA B. CONTINUOUS RORO RAMP
DATE OF BIDDING	: 29 June 2021
DATE OF AWARD	: 27 August 2021
DATE OF NOTICE TO PROCEED	: 12 October 2021
CONTRACT DURATION	: 660 <i>calendar days</i>
APPROVED BUDGET AMOUNT	: ₱409,790,595.71
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱405,688,591.71
EFFECTIVITY DATE	: 12 October 2021
ORIGINAL EXPIRY DATE	: 02 August 2023
PROJECT STATUS (As of 25 January 2023)	: - The project is 37.651% complete with a negative slippage of 39.807%.
REMARKS	: - On-going. - Negative slippage was due to unworkable weather condition and delayed fabrication and delivery of piles. - Warning letters were sent to the contractor to undertake measures to cope with the project's delay - Contractor's request for time extension is under evaluation.

JAGNA PORT EXPANSION PROJECT PORT OF JAGNA, JAGNA, BOHOL

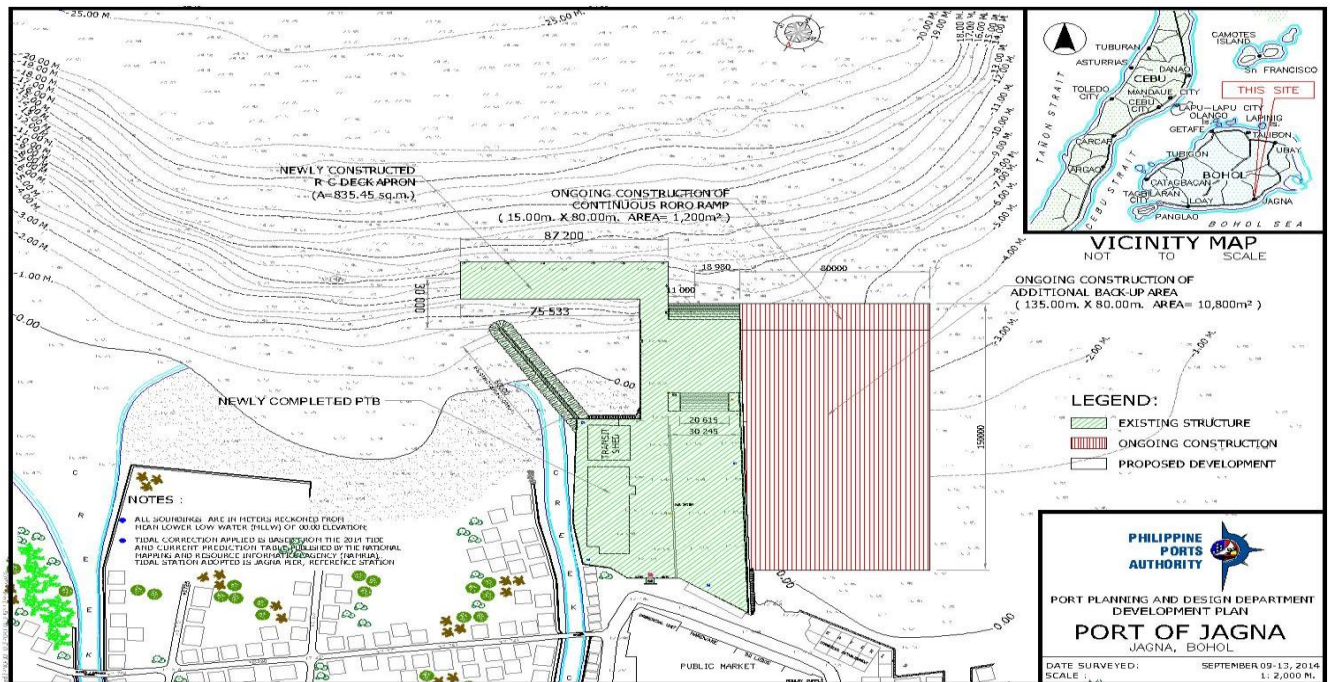

DEVELOPMENT PLAN

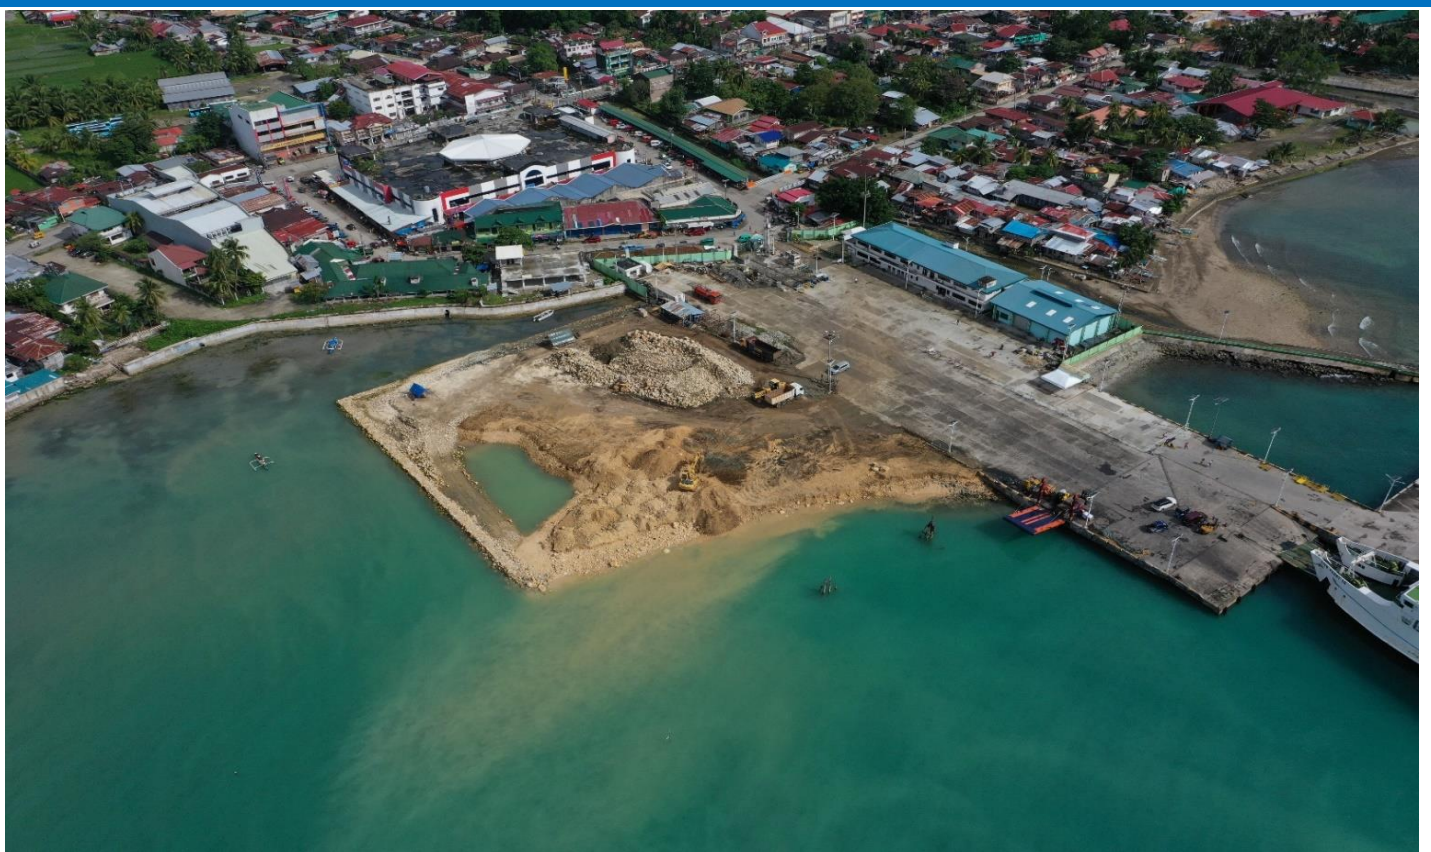


ONGOING CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	: CONSTRUCTION OF PORT OPERATIONAL AREA WITH CONTINUOUS RORO RAMP AND FASTCRAFT BERTH
LOCATION	: PORT OF GETAFE, BOHOL
CONTRACTOR	: MAC BUILDERS
SCOPE OF WORK	: A. PORT OPERATIONAL AREA, CONTINUOUS RORO AND FASTCRAFT BERTH
DATE OF BIDDING	: 24 November 2021
DATE OF AWARD	: 17 January 2022
DATE OF NOTICE TO PROCEED	: 09 February 2022
CONTRACT DURATION	: 660 <i>calendar days</i>
APPROVED BUDGET AMOUNT	: ₱465,079,912.22
SOURCE OF FUNDS	: PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	: PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	: ₱458,987,999.98
EFFECTIVITY DATE	: 09 February 2022
ORIGINAL EXPIRY DATE	: 30 November 2023
PROJECT STATUS (As of 25 January 2023)	: - The project is 33.156% complete with a negative slippage of 9.011%.
REMARKS	: - On-going. - Negative slippage was due to unworkable weather condition and upheaval of unsuitable materials during reclamation.

CONSTRUCTION OF PORT OPERATIONAL AREA WITH CONTINUOUS RORO RAMP AND FASTCRAFT BERTH PORT OF GETAFE, BOHOL

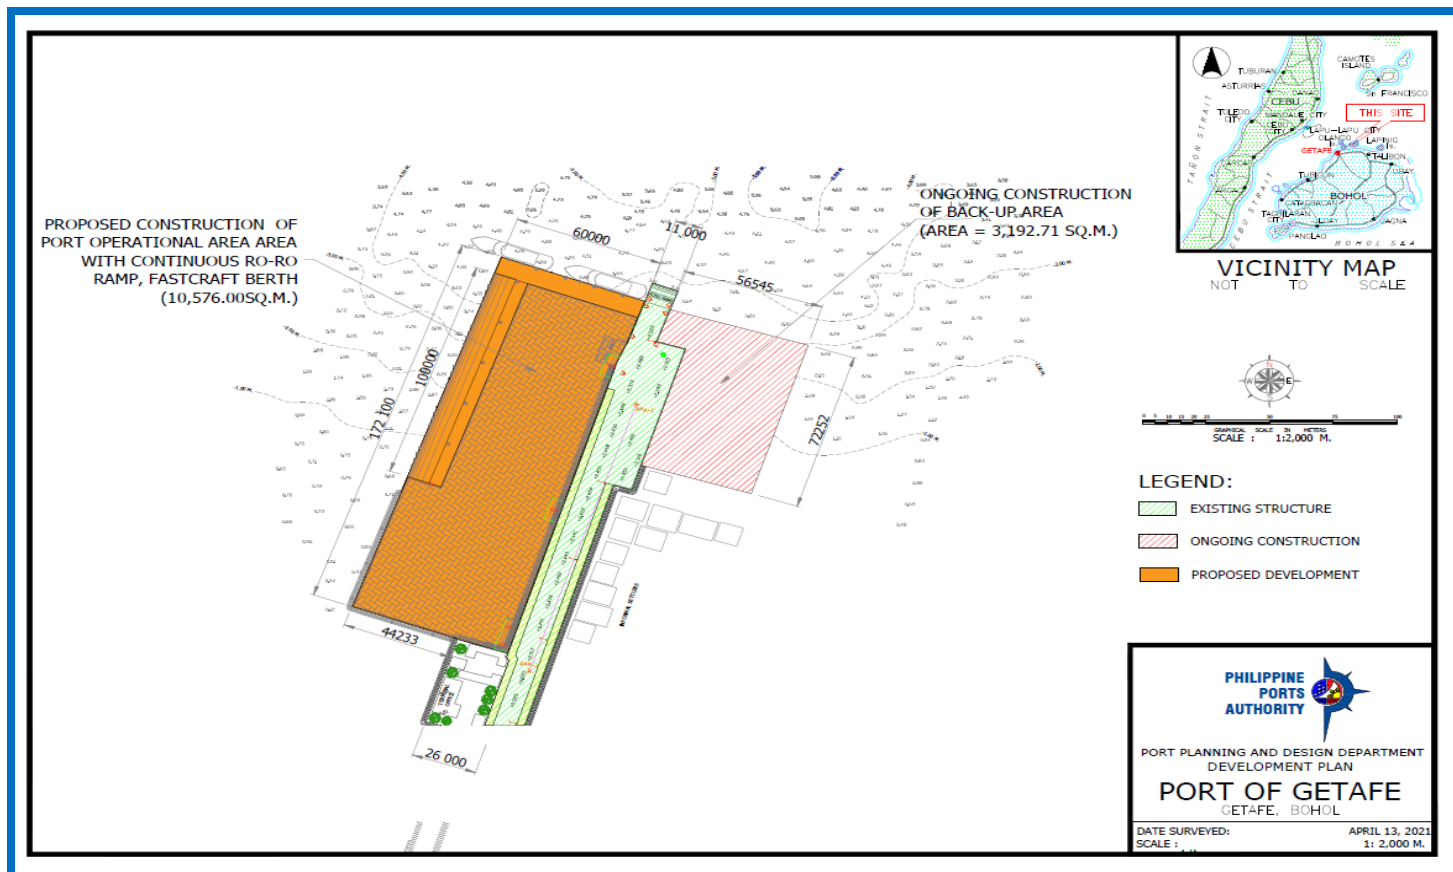

DEVELOPMENT PLAN




ONGOING CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	:	CONSTRUCTION OF PORT OPERATIONAL AREA
LOCATION	:	PORT OF GUADALUPE, MAASIN CITY, SOUTHERN LEYTE
CONTRACTOR	:	MAC BUILDERS
SCOPE OF WORK	:	A. DEMOLITION, EXCAVATION AND REMOVAL WORKS B. PORT OPERATIONAL AREA
DATE OF BIDDING	:	18 May 2022
DATE OF AWARD	:	06 June 2022
DATE OF NOTICE TO PROCEED	:	09 December 2022
CONTRACT DURATION	:	360 calendar days
APPROVED BUDGET AMOUNT	:	₱129,207,028.61
SOURCE OF FUNDS	:	PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	:	PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	:	₱127,088,000.00
EFFECTIVITY DATE	:	12 December 2022
ORIGINAL EXPIRY DATE	:	06 December 2023
PROJECT STATUS (As of 25 January 2023)	:	- Mobilization and sourcing of materials are on-going.
REMARKS	:	

CONSTRUCTION OF PORT OPERATIONAL AREA PORT OF GUADALUPE, MAASIN CITY, SOUTHERN LEYTE

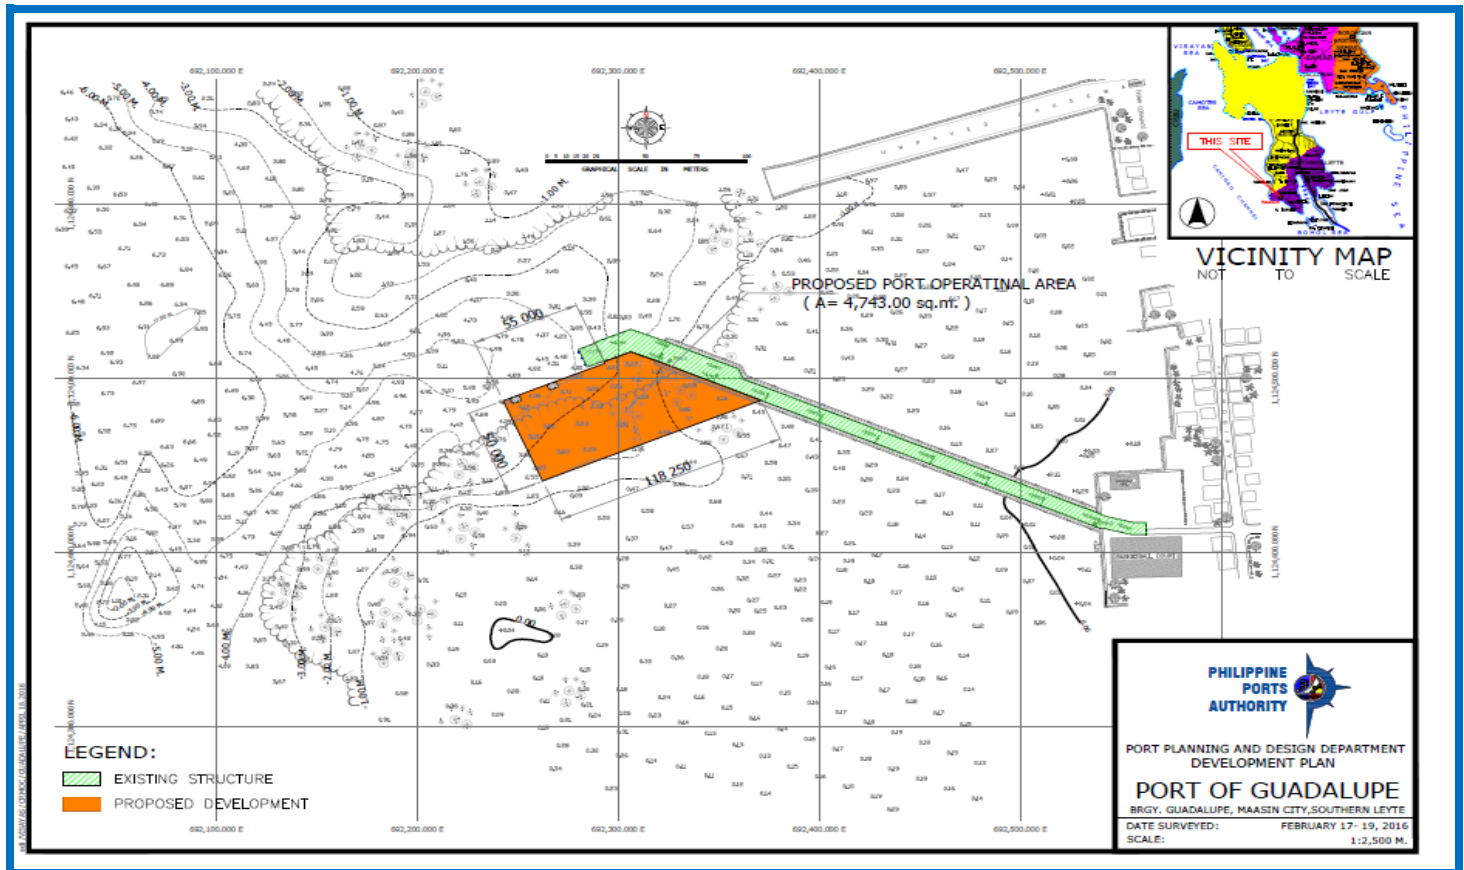


DEVELOPMENT PLAN




ONGOING CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	:	IMPROVEMENT/EXPANSION OF EXISTING PORT OPERATIONAL AREA AND CONSTRUCTION OF TERMINAL MANAGEMENT OFFICE, PASSENGER SHED, PUMPHOUSE, POEWRHOUSE AND GUARD HOUSE
LOCATION	:	PORT OF SAN JUAN, SAN JUAN, SOUTHERN LEYTE
CONTRACTOR	:	
SCOPE OF WORK	:	A. IMPROVEMENT/EXPANSION OF EXISTING PORT OPERATIONAL AREA = 1,303.06 SQ.M. B. CONSTRUCTION OF TERMINAL MANAGEMENT OFFICE, PASSENGER SHED, PUMPHOUSE, POWERHOUSE AND GUARD HOUSE AREA = 202.52 SQ.M.)
DATE OF BIDDING	:	
DATE OF AWARD	:	
DATE OF NOTICE TO PROCEED	:	
CONTRACT DURATION	:	300 calendar days
APPROVED BUDGET AMOUNT	:	₱51,256,030.95
SOURCE OF FUNDS	:	PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	:	PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	:	₱57,919,314.97
EFFECTIVITY DATE	:	
ORIGINAL EXPIRY DATE	:	
PROJECT STATUS	:	
(As of 25 November 2022)		
REMARKS	:	

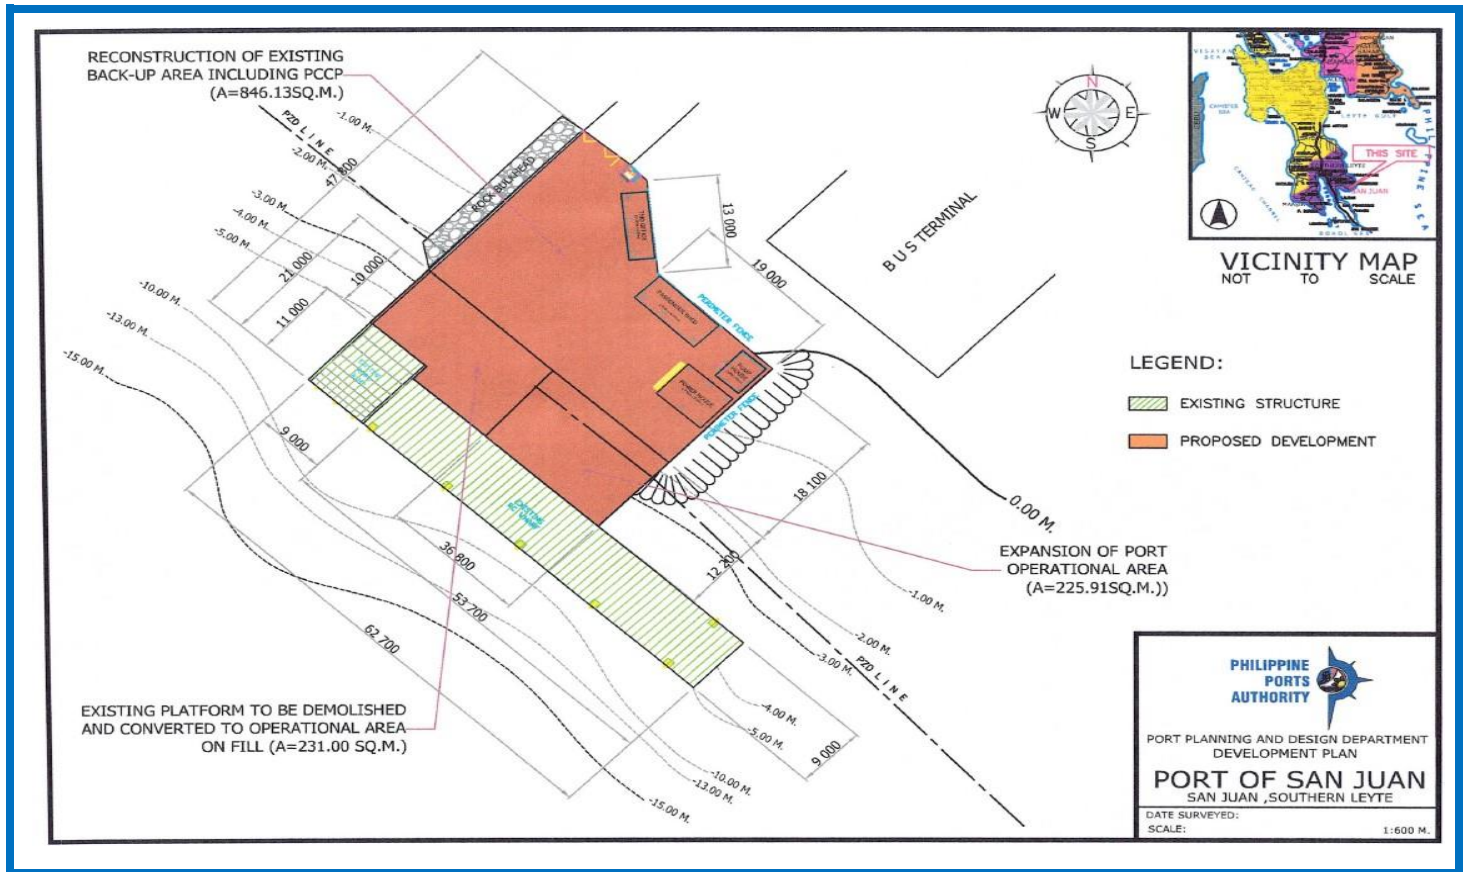


DEVELOPMENT PLAN




ONGOING CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	:	UPGRADING, EXPANSION AND CONSTRUCTION OF POB (PHASE 1)
LOCATION	:	PORT OF LILOAN, SOUTHERN LEYTE
CONTRACTOR	:	HI-TONE CONS. & DEV'T CORP. / KHAN KON CHI & DEV'T CORP. - JOINT VENTURE
SCOPE OF WORK	:	A. DEMOLITION, REMOVAL AND EXCAVATION WORKS B. UPGRADING AND EXPANSION OF PORT OPERATIONAL AREA C. CONTINUOUS RORO RAMP, RC PLATFORM AND RORO RAMP D. CONSTRUCTION OF PORT OPERATIONS BUILDING & OTHER STRUCTURES
DATE OF BIDDING	:	13 January 2023
DATE OF AWARD	:	
DATE OF NOTICE TO PROCEED	:	
CONTRACT DURATION	:	660 calendar days
APPROVED BUDGET AMOUNT	:	₱381,397,811.71
SOURCE OF FUNDS	:	PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	:	PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	:	₱379,887,713.43
EFFECTIVITY DATE	:	
ORIGINAL EXPIRY DATE	:	
PROJECT STATUS	:	
REMARKS	:	

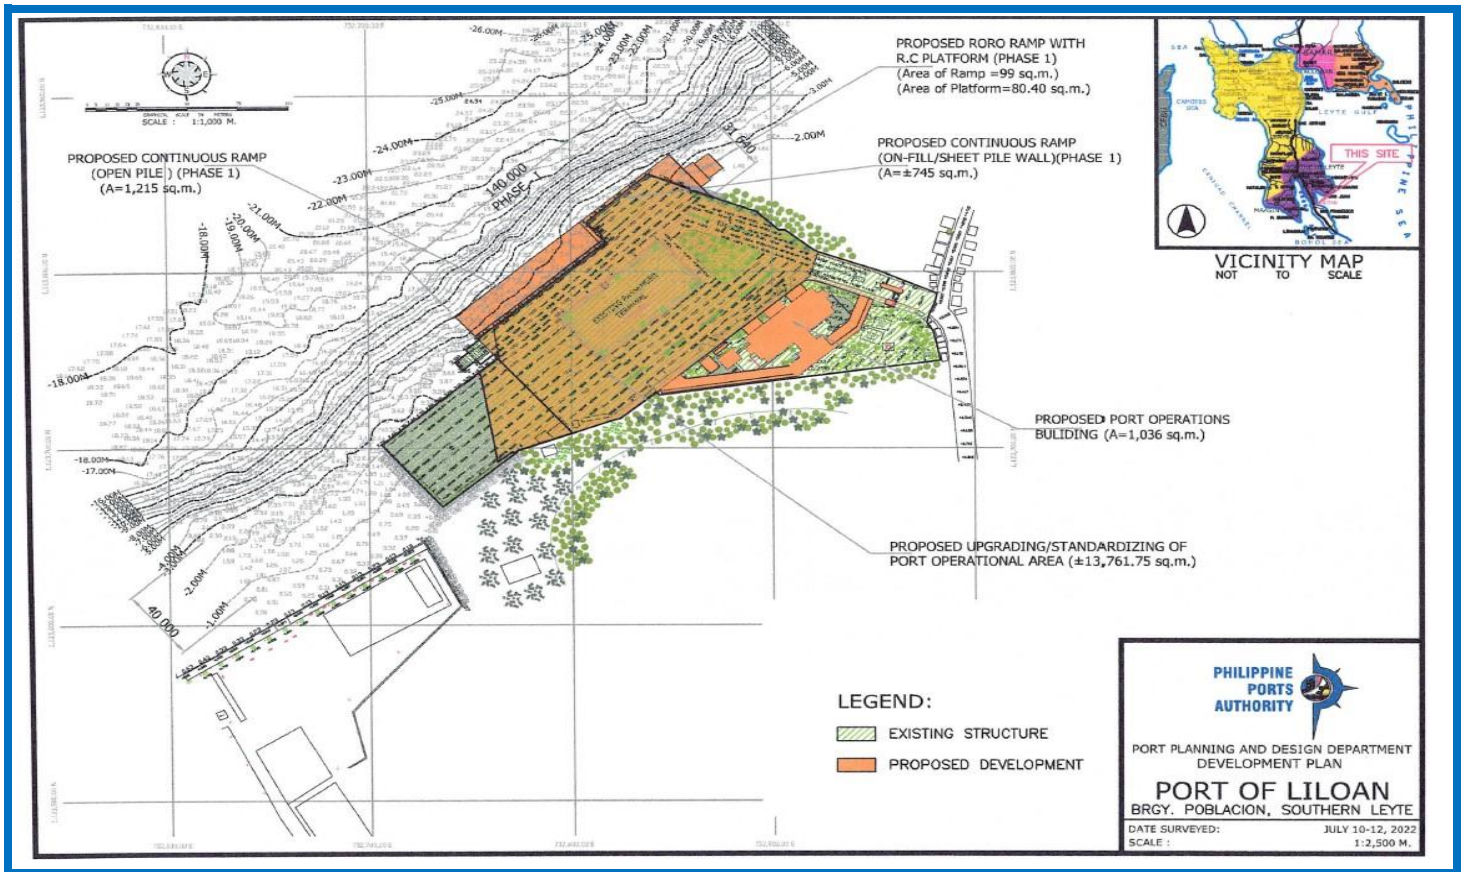


DEVELOPMENT PLAN




ONGOING CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE	:	SAN RICARDO PORT REHABILITATION/ IMPROVEMENT PROJECT
LOCATION	:	BRGY. BENIT, SAN RICARDO, SOUTHERN LEYTE
CONTRACTOR	:	KHAN KON CHI CONST. & DEV'T CORP.
SCOPE OF WORK	:	A. DEMOLITION, REMOVAL AND EXCAVATION WORK B. PORT OPERATIONAL AREA C. RORO RAMP, RC PLATFORM AND BREASTING DOLPHIN D. REHABILITATION OF PTB/DRIVER'S LOUNGE
DATE OF BIDDING	:	13 January 2023
DATE OF AWARD	:	
DATE OF NOTICE TO PROCEED	:	
CONTRACT DURATION	:	600 calendar days
APPROVED BUDGET AMOUNT	:	₱180,119,055.35
SOURCE OF FUNDS	:	PPA CORPORATE BUDGET
IMPLEMENTING OFFICE	:	PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)
ORIGINAL CONTRACT AMOUNT	:	₱178,984,203.57
EFFECTIVITY DATE	:	
ORIGINAL EXPIRY DATE	:	
PROJECT STATUS	:	
REMARKS	:	

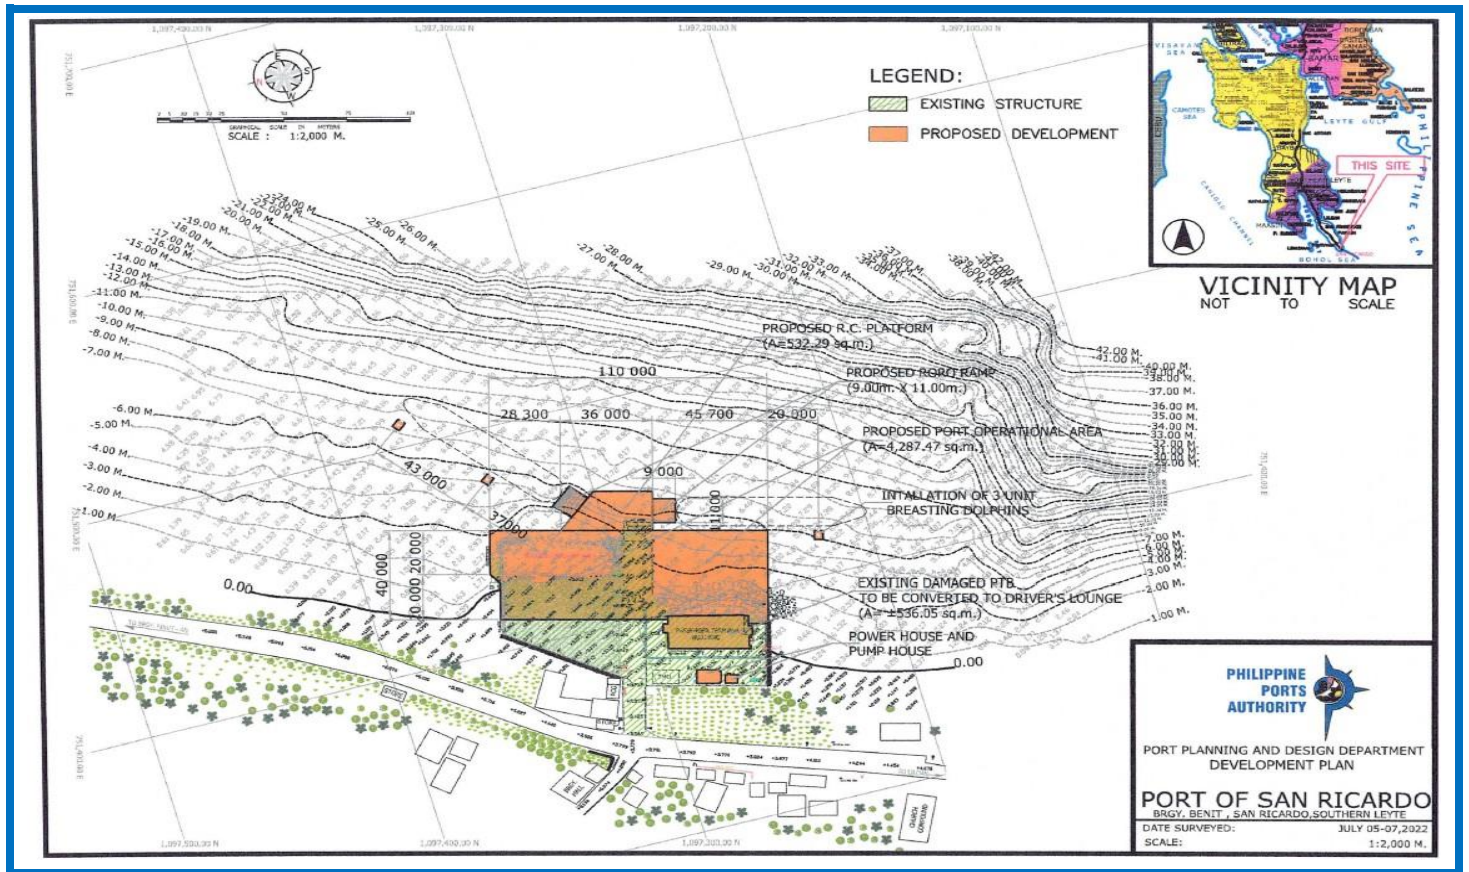

DEVELOPMENT PLAN



ONGOING CONSTRUCTION
