

PROJECT BRIEF

- PROJECT TITLE** : **REHABILITATION AND UPGRADING OF EXISTING BERTH AND BACK UP AREA**
- LOCATION** : **PIER 18, VITAS, TONDO, MANILA**
- CONTRACTOR** : **MRB II CONSTRUCTION CORPORATION**
- SCOPE OF WORK** : **A. REHABILITATION AND UPGRADING OF EXISTING BERTH AND BACK-UP AREA (AREA = 15,213.85 SQ.M.)**
1. Remove and turn-over to authority existing mooring bollard (22 sets) and existing RDF (22 sets), demolish and dispose existing concrete pavement (3,468 sq.m.), existing building structure (280 sq.m.) and existing sheet pile wall/retaining wall (52 cu.m.), remove and dispose plants/green (290 sq.m.) and excavate, backfill and compaction of existing fill materials (4,733 sq.m.).
 2. Construction of rock bulkhead (13,994 cu.m.), fill materials (25,912 cu.m.), reinforced concrete for retaining walls, anchor wall, mooring block, coping wall, R.C. curb, R.C. ditch, lateral drainage and perimeter fence (1,583 cu.m. of concrete and 174,236 kg of reinforcing steel bars of various sizes).
 3. Supply and drive of concrete sheet piles (0.35m x 0.525m PSC sheet piles - 10,108 l.m. and R.C. corner sheet piles - 70 l.m.), including chipping and cutting of newly driven piles up to required elevation (727 pcs).
 4. Construction of CHB wall (959 sq.m.), including plastering (1,918 sq.m.), barbed wire fence (178 sq.m.) and painting for concrete and metal surface (2,139 sq.m. and 11 sq.m., respectively).
 5. Construction of Portland cement concrete pavement (PCCP, 300mm thk. - 1,234 sq.m.) and interlocking concrete block pavement (12,880 sq.m.), including aggregate base coarse (2,251 cu.m.), cement treated base coarse (1,932 cu.m.), sand cushion (644 cu.m.) and concrete edging (404 sq.m.).
 6. Supply and install of geotextile fabric (5,691 sq.m.), tie-rod of various sizes (56 sets - 36mmØ x 13.00m and 191 sets - 60mmØ x 16.00m and anchor block (56 pcs), including gravel bedding (122 cu.m.) and lean concrete (56 cu.m.).
 7. Supply and install Rubber Dock Fenders, V-type, 500H x 2000L (33 sets) and mooring bollards, 50 tons, T-head (28 sets).
- B. PORT LIGHTING SYSTEM**
1. Supply and installation of steel tapered lamp post, 10.00m ht., hot-dipped galvanized (3 sets) with 70 watt LED solar lamp fixture (3 sets) and floodlight steel post, 18.00m ht., hot-dipped galvanized (7 sets) with 500 watt LED floodlight fixture (14 sets).
- DATE OF BIDDING** : **23 August 2018**
- DATE OF AWARD** : **26 September 2018**

DATE OF NOTICE TO PROCEED : **21 November 2018**
CONTRACT DURATION : **600 calendar days**
APPROVED BUDGET AMOUNT : **₱301,318,609.49**
SOURCE OF FUNDS : **PPA CORPORATE BUDGET**
IMPLEMENTING OFFICE : **PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)**

ORIGINAL CONTRACT AMOUNT : **₱298,988,736.73**
VARIATION ORDER NO. 1 : **₱25,825,791.85**
(Change Order No. 1/ Extra Work Order No. 1) - Covering the quantity adjustments of some of the original items of work and inclusion of additional works brought about by the approval / issuance of revised plans / drawings covering the above-mentioned issues and concerns.

REVISED CONTRACT AMOUNT : **₱324,814,528.58**
(First Revision)
VARIATION ORDER NO. 2 : **₱229,982.94**
(Change Order No. 2/ Extra Work Order No. 2) - Covering the quantity adjustment of some items of work and additional works as called for by the approved revised plans/drawings incorporating the implementation of the rectification plan recommended by PPDD.

REVISED CONTRACT AMOUNT : **₱325,044,511.52**
(Second Revision)
EFFECTIVITY DATE : **21 November 2018**
ORIGINAL EXPIRY DATE : **12 July 2020**
TIME EXTENSION NO. 1 : **285 calendar days**
Covering the time elapsed being affected by the issued suspension orders, e.g. privately owned portion of the project area; pending evaluation of corresponding revised plans/approval of variation order no. 1 re: issues and concerns with PRA and additional time covering the changes/revisions of the project.

REVISED EXPIRY DATE : **21 February 2022**
(First Revision)
TIME ADJUSTMENT NO. 2 : **116 calendar days**
- Due to Variation Order No. 2


LATEST (2) REVISED EXPIRY DATE : **08 January 2023**
(Second Revision)
TIME EXTENSION NO. 3 : **225 calendar days**
- Covering the time elapsed due to unworkable bad weather conditions and busy port operations.

REVISED EXPIRY DATE : **21 August 2023**
(Third Revision)
TIME EXTENSION NO. 4 : **101 calendar days**
- Covering the time elapsed due to unworkable bad weather conditions and busy port operations.

REVISED EXPIRY DATE : **30 November 2023**
(Fourth Revision)
PROJECT STATUS : - The project is 91.037 complete with a negative slippage of 3.946%.
(As of 25 September 2023)
REMARKS : - On-going.
OFFICER-IN-CHARGE : **MELANIE T. NAPIZA**
(Project Manager)

CONTACT NUMBER : **8-527-4435**
EMAIL ADDRESS : napizam@yahoo.com

REHABILITATION AND UPGRADING OF EXISTING BERTH AND BACK-UP AREA, PIER 18, VITAS, TONDO, MANILA

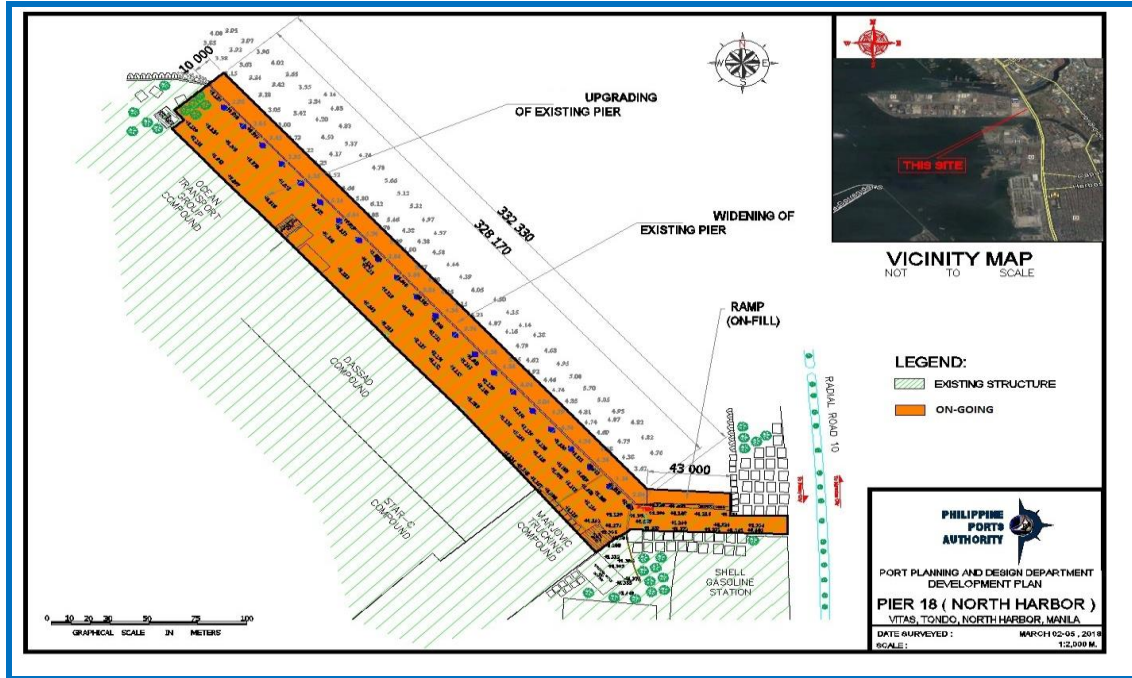

DEVELOPMENT PLAN




ONGOING CONSTRUCTION

PROJECT BRIEF

| | | |
|--|---|---|
| PROJECT TITLE | : | CONSTRUCTION OF BACK-UP AREA & PORT OPERATIONS BUILDING (POB) |
| LOCATION | : | PORT OF MAUBAN, QUEZON |
| CONTRACTOR | : | RT CRISMAN BUILDERS AND CONSTRUCTION SUPPLY |
| SCOPE OF WORK | : | A. CONSTRUCTION OF BACK-UP AREA & WIDENING OF ROCK CAUSEWAY <ol style="list-style-type: none">1. Chipping of existing R.C. Curb (186 l.m.).2. Supply and placing of 3,500 PSI concrete (173 cu.m.).3. Supply and installation of steel reinforcement (9,206 cu.m.).4. Supply and installation of steel reinforcement (9,206 cu.m.).5. Installation of geotextile fabric (1,450 sq.m.).6. Supply and placing of fill materials (12,899 cu.m.).7. Construction of 300mm thk. PCC Pavement (3,761 sq.m.). B. CONSTRUCTION OF PORT OPERATION BUILDING <ol style="list-style-type: none">1. Supply and driving of 400 x 400mm PSC foundation piles (840 l.m.).2. Construction of 1-storey Port Operation Building (625 sq.m., 250 pax).3. Construction of Pumphouse (12.24 sq.m.).4. Construction of R.C. Ductbank, Handhole & Pedestal (33 cu.m.).5. Supply, delivery, installation of gang chairs (1 lot). |
| DATE OF BIDDING | : | 21 November 2018 |
| DATE OF AWARD | : | 07 December 2018 |
| DATE OF NOTICE TO PROCEED | : | 03 April 2019 |
| CONTRACT DURATION | : | 450 calendar days |
| APPROVED BUDGET AMOUNT | : | ₱136,670,234.17 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : | PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : | ₱135,606,952.10 |
| EFFECTIVITY DATE | : | 26 April 2019 |
| ORIGINAL EXPIRY DATE | : | 18 July 2020 |
| TIME ADJUSTMENT NO. 1/ TIME EXTENSION NO. 1 | : | 244 calendar days - Covering the time elapsed of the suspended period (a) from 18 November 2019 to 07 December 2020 due to issues with Philippine Reclamation Authority (PRA regarding reclamation projects; and from 17 March 2020 to 15 May 2020 due to the imposition of Enhance Community Quarantine (ECQ) brought by COVID-19 crisis. |

| | |
|--|---|
| REVISED EXPIRY DATE (First Revision) | : 08 August 2021 |
| TIME ADJUSTMENT NO. 2/ TIME EXTENSION NO. 2 | : 79 calendar days - Covering the delays brought by the unworkable days caused of bad weather condition for the period of April 26 to November 17, 2019 and December 08, 2020 to April 25, 2021. |
| REVISED EXPIRY DATE (Second Revision) | : 26 October 2021 |
| TIME ADJUSTMENT NO. 3/ TIME EXTENSION NO. 3 | : 110 calendar days - Covering the time elapsed due to unworkable bad weather conditions and issuance of quarantine restrictions/lockdown at Brgy. Daungan, Mauban, Quezon brought by the COVID-19 crisis. |
| REVISED EXPIRY DATE (Third Revision) | : 13 February 2022 |
| TIME EXTENSION NO. 4 | : 66 calendar days Covering the time elapsed due to unworkable bad weather conditions. |
| REVISED EXPIRY DATE (Fourth Revision) | : 20 April 2022 |
| TIME EXTENSION NO. 5 | : 38 calendar days Covering the time elapsed due to unworkable bad weather conditions. |
| LATEST REVISED EXPIRY DATE (Fifth Revision) | : 28 May 2022 |
| PROJECT STATUS (As of 25 September 2023) | : - The project is 93.376% complete with a negative slippage of 6.624%. |
| REMARKS: | : - Ongoing. - Negative slippage of the project was due to unworkable weather condition and slow pacing of work by the Contractor. - Warning letters were sent to the Contractor to fast track the completion of the project. |
| OFFICER-IN-CHARGE | : EXZUR G. GOMEZ (Project Manager) |
| CONTACT NUMBER | : 8-527-4435 |
| EMAIL ADDRESS | : gomezexzur@yahoo.com |

CONSTRUCTION OF BACK-UP AREA & PORT OPERATIONS BUILDING (POB) PORT OF MAUBAN, QUEZON

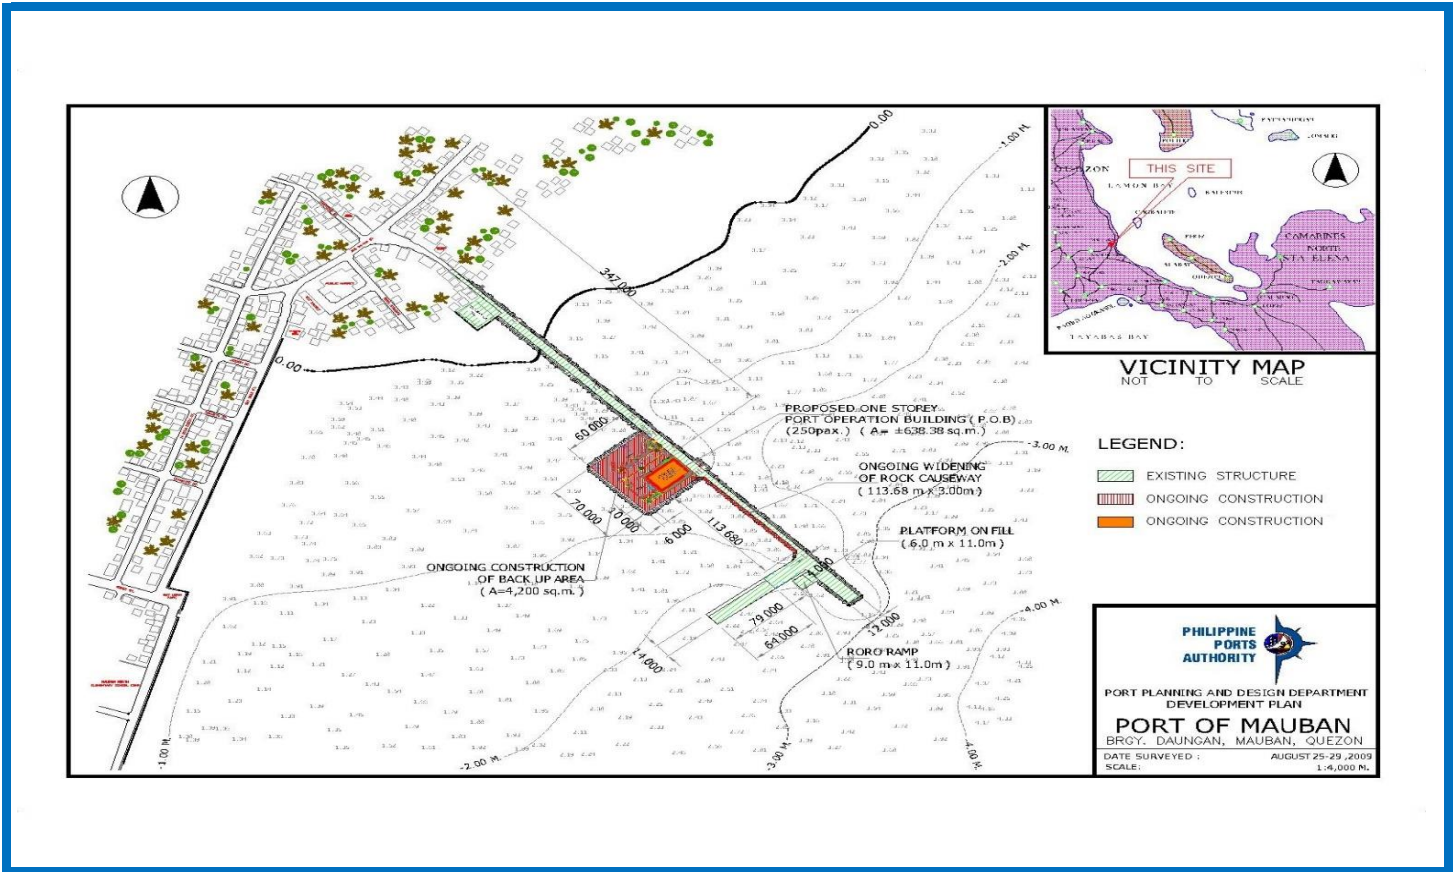

DEVELOPMENT PLAN



ONGOING CONSTRUCTION

PROJECT BRIEF

| | |
|----------------------------|---|
| PROJECT TITLE | : CAWAYAN PORT IMPROVEMENT PROJECT |
| LOCATION | PORT OF CAWAYAN, MASBATE |
| CONTRACTOR | : MGB CONSTRUCTION AND TRADING |
| SCOPE OF WORK | : A. DEMOLITION & REMOVAL WORKS <ol style="list-style-type: none">1. Demolition & disposal of existing wooden structures (10 sq.m.)2. Removal of existing mooring cleats (4 sets)3. Chipping portion of existing RC curb (58 l.m.)4. Chipping existing deflector wall (204 l.m.)5. Demolition & disposal of existing concrete pavement (867 sq.m.) B. BACK-UP AREA & CAUSEWAY <ol style="list-style-type: none">1. Sub-grade preparation (1,007 sq.m.)2. Scrapping of existing gravel materials (3,086 cu.m.)3. Excavation of existing seabed (103 cu.m.)4. Supply & placing of 3,500 PSI concrete (473 cu.m.)5. Supply & installation of steel reinforcement (24,115 kg.)6. Supply & placing of 50 to 2,000 kg/pc rocks (10,883 cu.m.)7. Supply & installation of tie-rods (4 sets)8. Supply & placing of geotextile fabric filter (3,403 sq.m.)9. Supply & placing of fill materials (16,986 cu.m.)10. Construction of Portland Cement Concrete Pavement (6,999 sq.m.)11. Re-installation of old mooring cleats (4 sets)12. Construction of Perimeter security fence & gate (147 l.m.) C. PORT OPERATIONS BUILDING, PUMPHOUSE AND GUARDHOUSE <ol style="list-style-type: none">1. Supply and driving 450 x 450mm PSC foundation piles (270 l.m.)2. Construction of 1-storey Port Operations Building, (672.54 sq.m.) complete3. Construction of Pumphouse & appurtenances (12.24 sq.m.)4. Construction of Guardhouse & appurtenances (5.33 sq.m.) |
| DATE OF BIDDING | : 11 December 2019 |
| DATE OF NOTICE OF AWARD | : 24 January 2020 |
| DATE OF NOTICE OF AWARD | : 18 June 2020 |
| ORIGINAL CONTRACT DURATION | : 450 calendar days |
| APPROVED BUDGET AMOUNT | : ₱149,138,830.31 |
| SOURCE OF FUNDS | : PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : ₱146,998,000.58 |
| EFFECTIVITY DATE | : 01 July 2020 |
| ORIGINAL EXPIRY DATE | : 23 September 2021 |

TIME EXTENSION NO. 1**: 369 calendar days**

- Covering the delays caused by (a) suspension order issued on reclamation activities caused by issues and concerns raised by the Philippine Reclamation Authority (PRA) and (b) late transport / conveyance of major construction equipment at the site due to prevailing rough sea condition at its point of origin in Tabaco, Albay for the period February 23 to September 25, 2021.

REVISED EXPIRY DATE

(First Revision)

: 27 September 2022**PROJECT STATUS**

(As of 25 September 2023)


- The project is 6.372% complete with a negative slippage of 93.628%.

REMARKS


- Ongoing
- Negative slippage of the project was due to delayed delivery of materials, non-mobilization of equipment and lack of manpower.
- Warning letters were sent to the contractor to undertake drastic action to fast track the completion of the project
- The contractor has a pending request for time extension due to encountered imposition of restriction orders caused by COVID-19 Pandemic, suspension of quarry, impassable roads due to on-going infrastructure projects and unworkable / prevailing rough sea conditions.
- Notice of Contract Termination was issued to the contractor on 01 August 2023, in pursuant to the Government Procurement Policy Board Circular No. 03-2019.
- The contractor requested for reconsideration / withdrawal of the Contract Termination and seeking for opportunity to undertake and complete the contract for the project.
- The contractor's request for reconsideration / withdrawal of the Contract Termination is under evaluation.

OFFICER-IN-CHARGE**: EUFEMIO C. VELASCO**
(Project Manager)**CONTACT NUMBER****8-527-4435****EMAIL ADDRESS**ec_velascojr@yahoo.com

CAWAYAN PORT IMPROVEMENT PROJECT PORT OF CAWAYAN, MASBATE

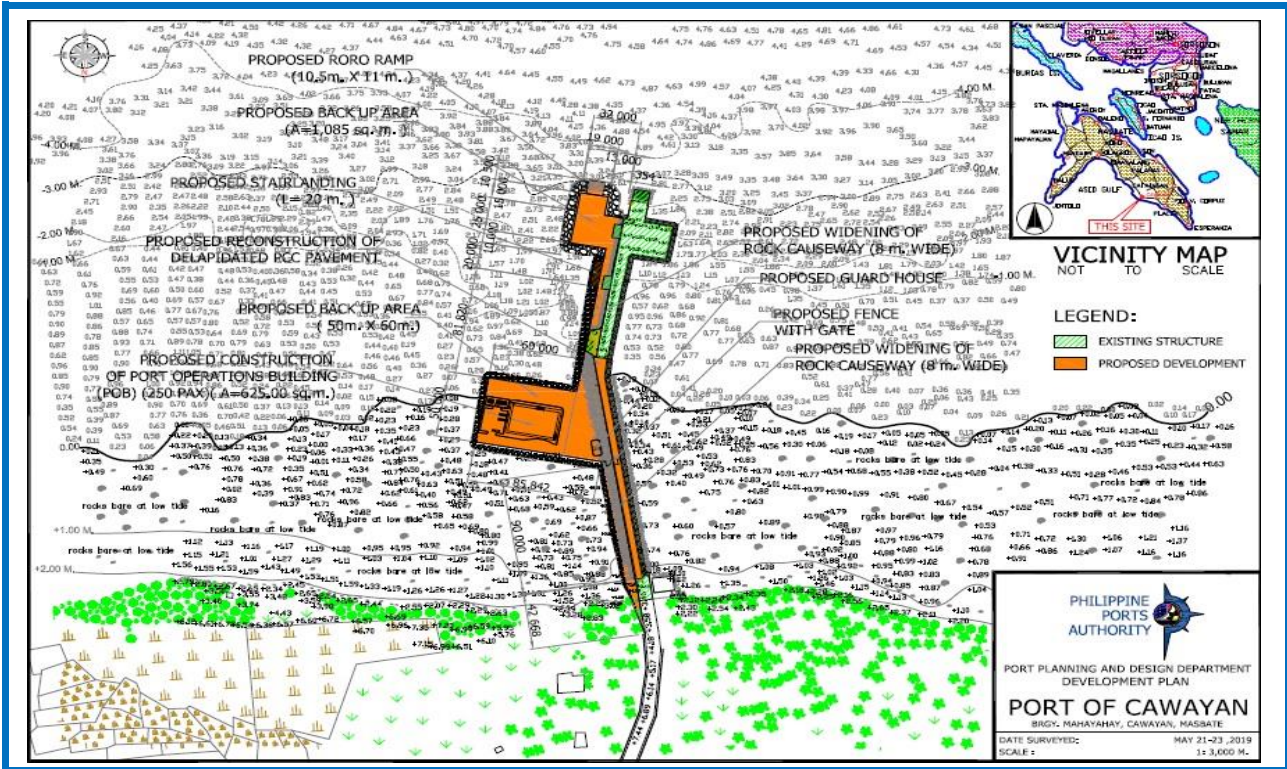

DEVELOPMENT PLAN

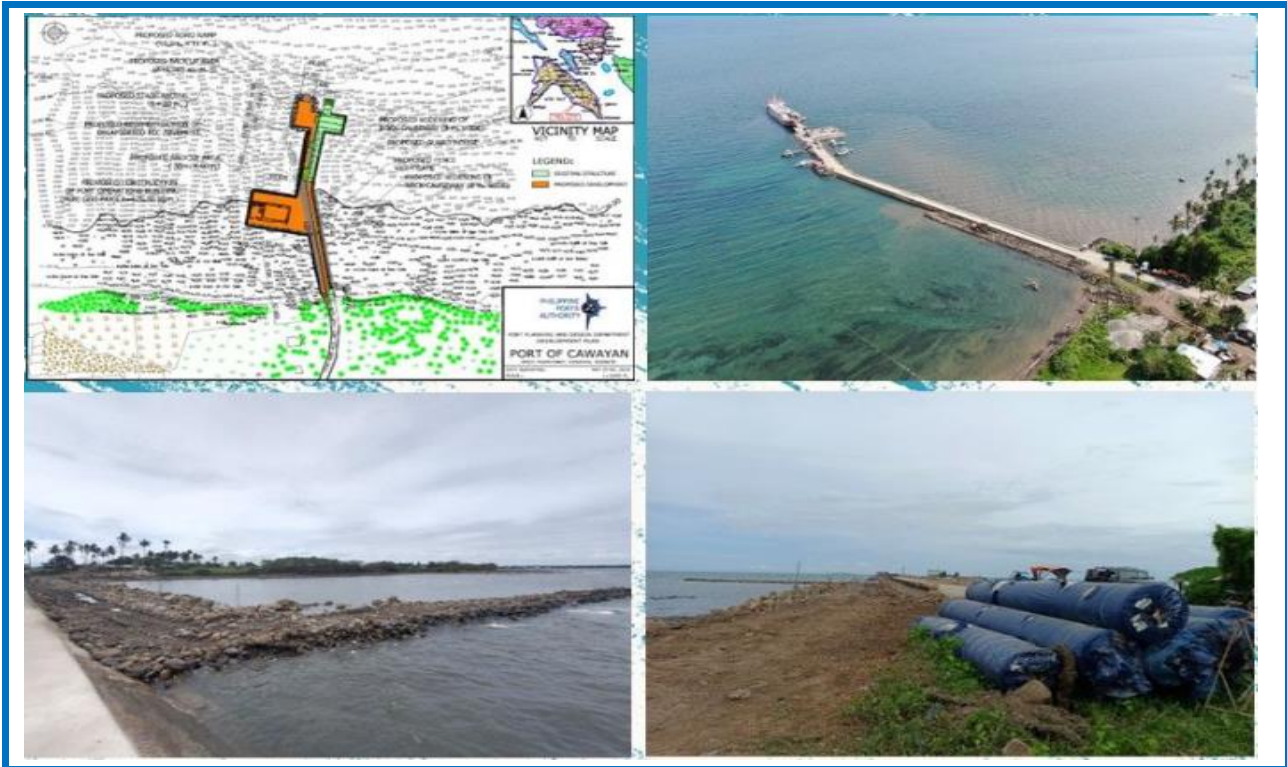


ONGOING CONSTRUCTION


PROJECT BRIEF

| | |
|---|--|
| PROJECT TITLE | : CONSTRUCTION OF BREAKWATER |
| LOCATION | : PORT OF CURRIMAO, CURRIMAO, ILOCOS NORTE |
| CONTRACTOR | : KHAN KON CHI CONSTRUCTION AND DEVELOPMENT CORPORATION/ HI-TONE CONSTRUCTION AND DEVELOPMENT CORPORATION/JV |
| SCOPE OF WORK | : A. BREAKWATER WITH 2-UNITS BEACON LIGHT <ol style="list-style-type: none">1. Excavation of existing seabed along the toe of breakwater (5,495 cu.m.)2. Supply and placing of 3,500 PSI concrete (7 cu.m.)3. Supply and installation of steel reinforcement (529 kg.)4. Supply and placing of 300-500 kg/pc. Rocks (20,527 cu.m.)5. Supply and placing of 1,000 to 1,500 kg/pc. Rocks (8,056 cu.m.)6. Supply and placing of 3,000 to 4,000 kg/pc. Rocks (34,842 cu.m.)7. Supply and placing of 5,000 to 6,000 kg/pc. Rocks (3,757 cu.m.)8. Supply and install beacon lights including accessories (2 set) |
| DATE OF BIDDING | : 11 December 2020 |
| DATE OF AWARD | : 21 January 2021 |
| DATE OF NOTICE TO PROCEED | : 24 February 2021 |
| CONTRACT DURATION | : 660 calendar days |
| APPROVED BUDGET AMOUNT | : ₱394,620,254.73 |
| SOURCE OF FUNDS | : PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : ₱394,066,383.93 |
| EFFECTIVITY DATE | : 26 February 2021 |
| ORIGINAL EXPIRY DATE | : 17 December 2022 |
| TIME EXTENSION NO. 1 | : 51 calendar days <ul style="list-style-type: none">- Covering the time elapsed due to unworkable bad weather and rough sea conditions. |
| REVISED EXPIRY DATE (First Revision) | : 06 February 2023 |
| TIME EXTENSION NO. 2 | : 110 calendar days <ul style="list-style-type: none">- Covering the time elapsed due to unworkable bad weather and rough sea conditions. |
| REVISED EXPIRY DATE (Second Revision) | : 27 May 2023 |
| PROJECT STATUS (As of 25 August 2023) | : - The project is 92.943% complete. |
| REMARKS | : - The project was suspended since 01 May 2023 due to scarcity of materials from the approved source. - Contractor's request for time extension due to unworkable weather and rough sea conditions is under evaluation. Awaiting submission of supporting documents. |
| OFFICER-IN-CHARGE | : GERALINE C. BAUTISTA (Project Manager) |
| CONTACT NUMBER | : 8-527-4435 |
| EMAIL ADDRESS | : geraline_bautista@yahoo.com |

CONSTRUCTION OF BREAKWATER, PORT OF CURRIMAO PORT OF CURRIMAO, CURRIMAO, ILOCOS NORTE

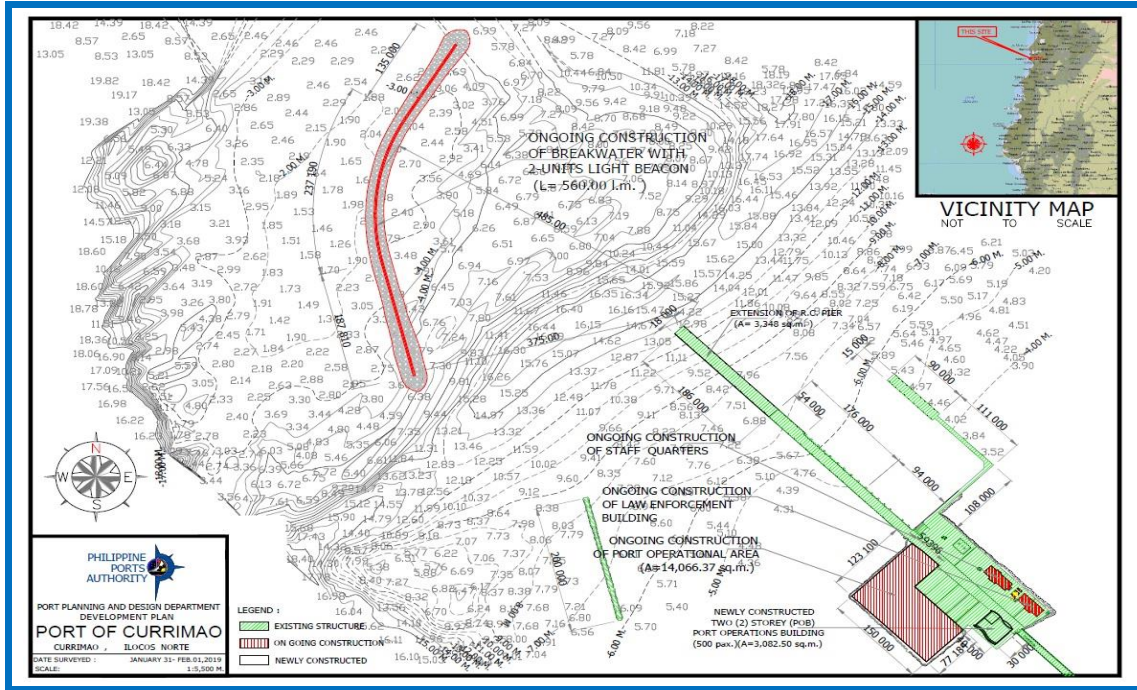

DEVELOPMENT PLAN

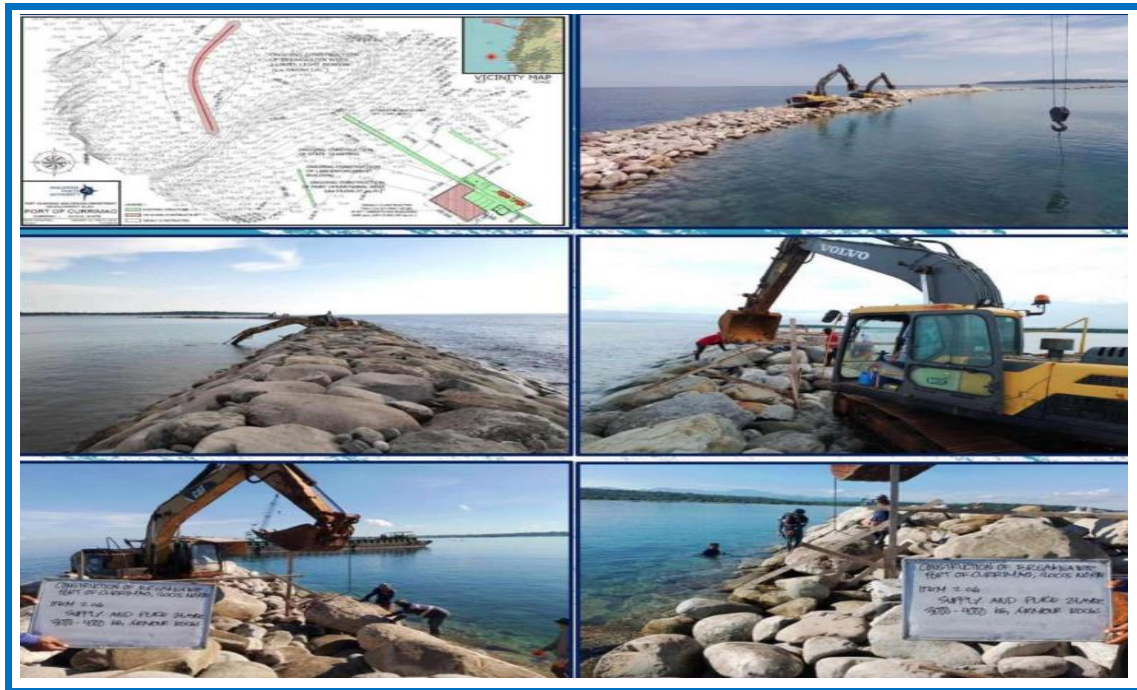

ONGOING CONSTRUCTION

PROJECT BRIEF

| | |
|--|---|
| PROJECT TITLE | : CONSTRUCTION OF BREAKWATER |
| LOCATION | : PORT OF ABRA DE ILOG, ORIENTAL MINDORO |
| CONTRACTOR | : GOLDRIDGE CONST. AND DEV'T CORP. |
| SCOPE OF WORK | : A. BREAKWATER WITH 2-UNITS BEACON LIGHT <ol style="list-style-type: none">1. Excavation of existing seabed (2,901 cu.m.)2. Supply and placing of 300-500 kg/pc. Rocks (26,642 cu.m.)3. Supply and placing of 3,000 kg/pc. Rocks (12,502 cu.m.)4. Supply, fabrication and installation of 7.36 ton/pc. Tetrapod (6,065 pc.)5. Supply and installation of beacon lights & accessories (2 sets) |
| DATE OF BIDDING | : 20 October 2021 |
| DATE OF AWARD | : 11 November 2021 |
| DATE OF NOTICE TO PROCEED | : 10 December 2021 |
| CONTRACT DURATION | : 780 calendar days |
| APPROVED BUDGET AMOUNT | : ₱529,905,132.08 |
| SOURCE OF FUNDS | : PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : PCMD - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : ₱525,888,678.00 |
| VARIATION ORDER NO. 1 (Change Order No. 1/ Extra Work Order No. 1) | : ₱49,072,019.70 - Covering the quantity adjustments of some of the original items of work brought by the approved pre-construction survey plan which are necessary for the protection, improvement and completion of the project. |
| REVISED CONTRACT AMOUNT (First Revision) | : ₱574,960,697.70 |
| EFFECTIVITY DATE | : 11 December 2021 |
| ORIGINAL EXPIRY DATE | : 29 January 2024 |
| TIME EXTENSION NO. 1 | : 147 calendar days - Due to Variation Order No. 1 |
| REVISED EXPIRY DATE | : 24 June 2024 |
| PROJECT STATUS (As of 15 October 2023) | : - Completed on 13 October 2023 |
| REMARKS: | : - |
| OFFICER-IN-CHARGE | : EUFEMIO C. VELASCO JR. (Project Manager) |
| CONTACT NUMBER | : 8-527-4435 |
| EMAIL ADDRESS | : ec_velascojr@yahoo.com |

PROJECT BRIEF

| | | |
|----------------------------------|----------|---|
| PROJECT TITLE | : | PUERTO GALERA PORT EXPANSION PROJECT |
| LOCATION | : | PORT OF PUERTO GALERA, ORIENTAL MINDORO |
| CONTRACTOR | : | GREAT SWISS METAL BUILDERS, INC. |
| SCOPE OF WORK | : | A. DEMOLITION, EXCAVATION AND REMOVAL WORKS <ol style="list-style-type: none">1. Excavation of existing seabed & fill materials (142 cu.m.)2. Demolition, disposal of existing pavement (774 sq.m.)3. Scraping of existing gravel base course (194 cu.m.)4. Demolition, disposal of existing fence (124 l.m.)5. Removal, turn-over of existing bollard, cleat, fender & lar post (1 lot) B. PORT OPERATIONAL AREA <ol style="list-style-type: none">1. Supply, delivery & driving of PSC sheet piles & RC corner piles (1,665 l.m.)2. Supply & placing of 3,500 psi concrete (297 cu.m.)3. Supply & installation of steel reinforcement (26,375 kg.)4. Supply & placing of core rocks & armour rocks (2,129 cu.m.)5. Supply & installation of fabricated concrete blocks (4 sets)6. Supply & installation of tie-rod of various sizes (25 sets)7. Supply & placing of fill materials (121,095 cu.m.)8. Construction of PCC Pavement including agg. Base course (3,373 sq.m.)9. Construction of security fence (1 lot)10. Supply & installation of Portlighting system (4 sets) C. R.C. PIER & RO-RO RAMP <ol style="list-style-type: none">1. Supply, delivery, driving & cutting of steel pipe piles (281 1,276 l.m.)2. Supply, delivery, driving & chipping of PSC piles (42 no.)3. Supply & placing of 3,500 psi concrete filler for SPP (346 cu.m.)4. Supply & installation of reinforcing steel cage for SPP (4 sets)5. Supply & placing of 3,500 PSI concrete for superstructure (392 cu.m.)6. Supply & installation of steel reinforcement for superstructure (49,954 kg.)7. Supply & installation of construction joints (50 l.m.)8. Supply & installation of Rubber Dock Fenders (10 sets)9. Supply & installation of mooring bollards (10 sets) |
| DATE OF AWARD | : | 06 December 2021 |
| DATE OF NOTICE TO PROCEED | : | 28 December 2021 |
| CONTRACT DURATION | : | 480 calendar days |
| APPROVED BUDGET AMOUNT | : | ₱149,509,773.48 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |

IMPLEMENTING OFFICE : **PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)**

ORIGINAL CONTRACT AMOUNT : **₱147,623,885.09**

EFFECTIVITY DATE : **04 January 2022**

ORIGINAL EXPIRY DATE : **28 April 2023**

TIME EXTENSION NO. 1 : **125 calendar days**
- Covering the delays brought about by unworkable bad weather period 04 January 2022 to 07 February 2023.

REVISED EXPIRY DATE : **31 August 2023**
(First Revision)

PROJECT STATUS : - The project is 87.869% complete with a negative slippage of 12.131%.
(As of 25 September 2023)


REMARKS : - On-going.
- Negative slippage of the project was due to unworkable weather condition and delayed start of pile driving activity.
- Contractor's request for time extension is under evaluation

OFFICER-IN-CHARGE : **ALLAN L. BELEN**
(Project Manager)

CONTACT NUMBER : **8-527-4435**

EMAIL ADDRESS : allanbelen25@gmail.com

PUERTO GALERA PORT EXPANSION PROJECT PORT OF PUERTO GALERA, ORIENTAL MINDORO

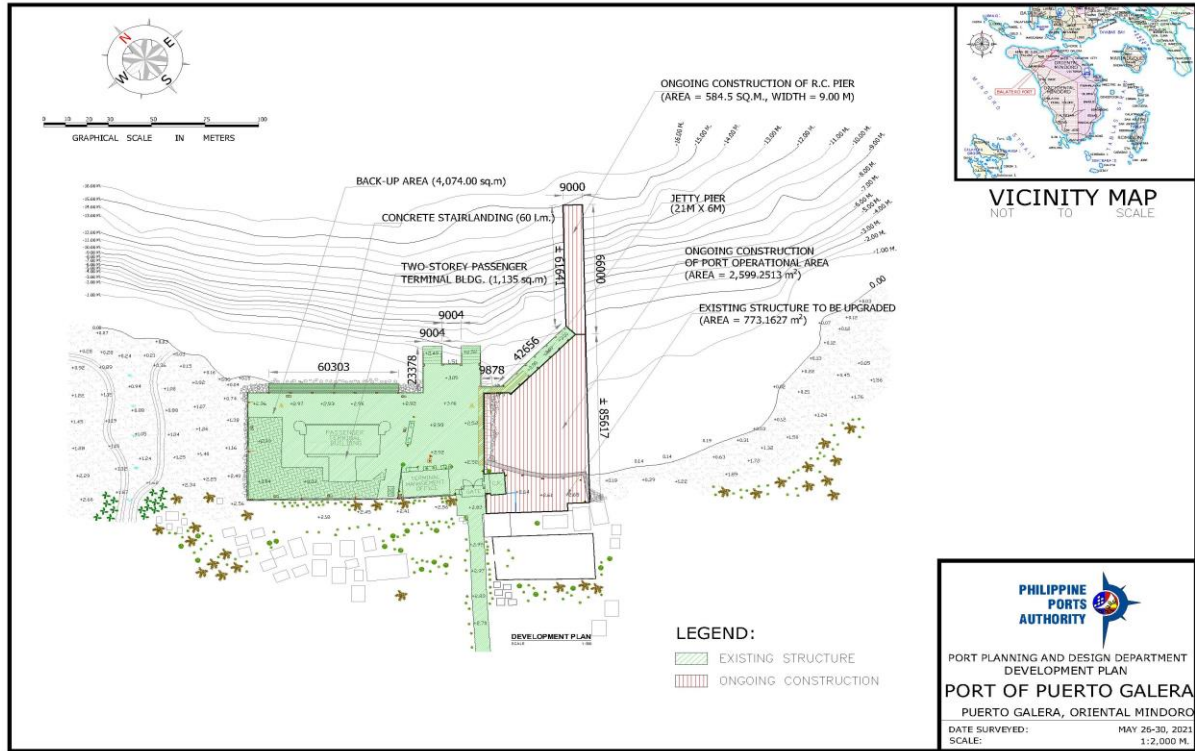

DEVELOPMENT PLAN



ONGOING CONSTRUCTION

PROJECT BRIEF

| | | |
|----------------------------|---|---|
| PROJECT TITLE | : | BALANACAN PORT EXPANSION PROJECT (2021) |
| LOCATION | : | PORT OF BALANACAN, MOGPOG, MARINDUQUE |
| CONTRACTOR | : | J.C. PIÑON CONSTRUCTION, INC. |
| SCOPE OF WORK | : | A. DEMOLITION, EXCAVATION AND REMOVAL WORKS <ol style="list-style-type: none">1. Excavation of existing seabed (129 cu.m.)2. Demolition & disposal of existing fence (33 l.m.)3. Removal of existing guard rail (1 lot)4. Clearing and grubbing (1,450 sq.m.) B. PORT OPERATIONAL AREA & ACCESS ROAD <ol style="list-style-type: none">1. Supply, delivery & driving of PSC sheet piles & RC corner piles (2,624 l.m.)2. Supply & placing of 3,500 psi concrete (845 cu.m.)3. Supply & installation of steel reinforcement (51,548 kg.)4. Supply & placing of grouted riprap (242 cu.m.)5. Supply & placing of core rocks & armour rocks (15,560 cu.m.)6. Supply & placing of fill materials (30,104 cu.m.)7. Construction of PCC pavement including agg. Base course (10,170 sq.m.)8. Construction of security fence (196 l.m.)9. Supply & installation of port lighting system (1 lot)10. Construction of Guardhouse & Gate (1 lot) C. R.C. WHARF <ol style="list-style-type: none">1. Supply, delivery & driving of PSC test pile (3 units)2. Supply, delivery & driving of PSC piles (4,740 l.m.)3. Supply & placing of 3,500 psi concrete for superstructure (392 cu.m.)4. Supply & installation of steel reinforcement for superstructure (58,138 kg.)5. Supply & installation of construction joints (156 l.m.)6. Supply & installation of Rubber Dock Fenders (8 sets)7. Supply & installation of mooring bollards (8 sets) |
| DATE OF BIDDING | : | 24 August 2021 |
| DATE OF NOTICE OF AWARD | : | 29 September 2021 |
| DATE OF NOTICE TO PROCEED | : | 26 October 2021 |
| ORIGINAL CONTRACT DURATION | : | 540 calendar days |
| APPROVED BUDGET AMOUNT | : | ₱294,441,838.26 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : | PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : | ₱290,888,143.76 |

VARIATION ORDER NO. 1 : **₱22,867,435.03**
(Change Order No. 1/ Extra Work Order No. 1) - Covering the lay-by areas intended for the weighbridge facility and emergency lane as requested by PMO-Marinduque/Quezon, provision of PCCP for the newly completed back-up area (Phase I), and quantity adjustment of some of the original items of work due variance in the seabed elevation between the construction plans and approved pre-construction survey plans

REVISED CONTRACT AMOUNT : **₱313,755,578.79**
(First Revision)

EFFECTIVITY DATE : **26 October 2021**

ORIGINAL EXPIRY DATE : **18 April 2023**

TIME EXTENSION NO. 1 : **131 calendar days**
- To facilitate the execution of some of the affected items of work and additional/new work items as detailed in the approved Variation Order No. 1.

REVISED EXPIRY DATE : **27 August 2023**

PROJECT STATUS : - Completed on 15 September 2023.
(As of 25 September 2023)


REMARKS : - As-built plan for submission of the contractor and recapitulation is under preparation.

OFFICER-IN-CHARGE : **GERALINE C. BAUTISTA**
(Project Manager)

CONTACT NUMBER : **8-527-4435**

EMAIL ADDRESS : geraline_bautista@yahoo.com

BALANACAN PORT EXPANSION PROJECT (2021) PORT OF BALANACAN, MOGPOG, MARINDUQUE

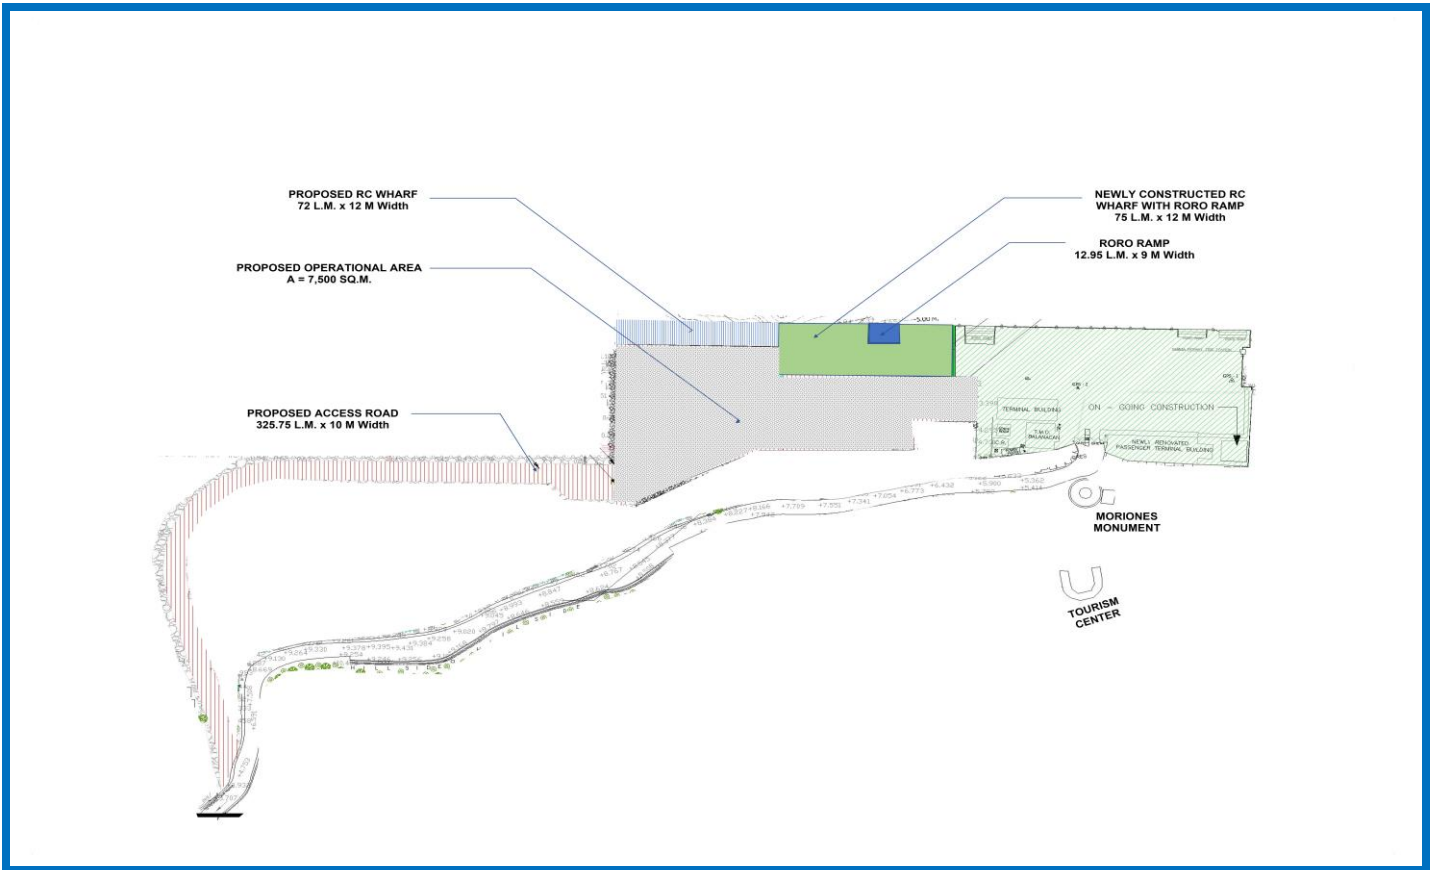

DEVELOPMENT PLAN



ONGOING CONSTRUCTION

PROJECT BRIEF

| | | |
|---------------------------|---|--|
| PROJECT TITLE | : | PLARIDEL PORT DEVELOPMENT / IMPROVEMENT PROJECT |
| LOCATION | : | PORT OF PLARIDEL (SIAIN), QUEZON |
| CONTRACTOR | : | MAC BUILDERS |
| SCOPE OF WORK | : | <p>A. DEMOLITION AND REMOVAL WORKS</p> <ol style="list-style-type: none">1. Demolition & disposal of existing R.C deck (1,000 sq.m.)2. Cutting & disposal of existing R.C. pile up to elevation +1.00m (67 nos.)3. Cutting & disposal of existing R.C. pile up to seabed elevation (84 nos.) <p>B. ROCK CAUSEWAY</p> <ol style="list-style-type: none">1. Excavation of existing seabed (5,170 cu.m.)2. Supply & placing of concrete (206 cu.m.)3. Supply & installation of reinforcing steel bars (18,238 kg.)4. Supply & placing of rocks (6,563 cu.m.)5. Supply & placing of fill materials (1,491 cu.m.)6. Supply & placing of aggregate base course (118 cu.m.)7. Construction of Concrete Pavement (589 sq.m.) <p>C. R.C. PIER</p> <ol style="list-style-type: none">1. Supply & delivery of Steel Pipe Piles (443 m.t.)2. Handling, pitching & driving of Steep Pipe Piles (4,193 l.m.)3. Splicing of Steel Pipe Piles (182 nos.)4. Cutting of newly driven Steel Pipe Piles (91 nos.)5. Extraction of clogged materials inside SPP (72 cu.m.)6. Supply & placing of 3,500 PSI concrete for SPP & deck (608 cu.m.)7. Supply & installation of reinforcing steel bars for SPP & Deck (97,293 kg.)8. Supply & installation of construction joints (24 l.m.)9. Supply & installation of mooring bollards (16 sets)10. Supply & installation of Rubber Dock Fenders (16 sets) |
| DATE OF BIDDING | : | 04 June 2021 |
| DATE OF AWARD | : | 06 July 2021 |
| DATE OF NOTICE TO PROCEED | : | 29 July 2021 |
| CONTRACT DURATION | : | 540 calendar days |
| APPROVED BUDGET AMOUNT | : | ₱142,829,373.05 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : | PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : | ₱140,688,941.10 |

VARIATION ORDER NO. 1 : **₱9,602,001.63**
(Change Order No. 1/ Extra Work Order No. 1) - Covering the quantity adjustments of some of the additional works on the repair of existing back-up area and additional 8 meters rock causeway.

REVISED CONTRACT AMOUNT : **₱150,290,942.73**
(First Revision)

EFFECTIVITY DATE : **29 July 2021**

ORIGINAL EXPIRY DATE : **19 January 2023**

TIME EXTENSION NO. 1 : **84 calendar days**
Covering the time elapsed due to Restriction of Work from 01 August 2021 to 20 October 2021 brought by the imposition of Community Quarantine caused by the COVID-19 pandemic.

REVISED EXPIRY DATE : **13 April 2023**
(First Revision)

TIME EXTENSION NO. 2 : **275 calendar days**
Due to Variation Order No. 1

REVISED EXPIRY DATE : **13 January 2024**
(Second Revision)

PROJECT STATUS : - The project is 78.438% complete with a negative slippage of 8.959%.
(As of 25 September 2023)

REMARKS: : - Ongoing.
- Negative slippage of the project was due to unworkable weather condition and slow pacing of work by the contractor.
- Warning letters were sent to the Contractor to undertake measures to cope with the project's delay.

OFFICER-IN-CHARGE : **EXZUR G. GOMEZ**
(Project Manager)

CONTACT NUMBER : **8-527-4435**

EMAIL ADDRESS : gomezexzur@yahoo.com

PROJECT BRIEF

- PROJECT TITLE** : **SAN ANDRES PORT EXPANSION PROJECT**
- LOCATION** : **PORT OF SAN ANDRES, QUEZON**
- CONTRACTOR** : **RCE GLOBAL CONSTRUCTION, INC.**
- SCOPE OF WORK** : **A. CONSTRUCTION OF PORT OPERATIONAL AREA (AREA = 5,684.38 SQ.M.)**
1. Chip-off existing slotted RC curb and smoothen with mortar (83 l.m.)
 2. Remove existing lamp post and turn-over to the Authority (6 no.)
 3. Demolish and dispose existing fence and smoothen with mortar (89 l.m.)
 4. Excavation of fill materials for catch drain manhole, reinforced concrete pipe culvert, floodlight foundation and duct bank (171 cu.m.)
 5. Supply and placing of 3,500 PSI concrete (54 cu.m.)
 6. Supply and installation of steel reinforcement (3,151 kg.)
 7. Supply and placing of 50 to 1,000 kg/pc rocks (9,693 cu.m.)
 8. Supply and placing of geotextile fabric filter (2,256 sq.m.)
 9. Supply and placing of fill materials (27,928 cu.m.)
 10. Supply, place and compact gravel bedding for catch drain manhole, lamp post foundation and duct bank (9 cu.m.)
 11. Supply, spread and compact aggregate base course (1,137 cu.m.)
 12. Construct Portland Cement Concrete Pavement (300mm thk) including dowel bars and construction joint (5,684 sq.m.)
 13. Construct security fence with cyclone wire and barbed wire including accessories (60 l.m.)
 14. Construct catch drain manhole including concrete cover with angular frame (11 set)
 15. Supply and install reinforced concrete pipe culvert 610mmØ (150 l.m.)
 16. Construct port lighting system including all appurtenances (1 lot)
- B. CONSTRUCTION OF RORO RAMP AND RC PLATFORM**
- RORO RAMP (AREA = 9MX11M)**
- RC PLATFORM 1 (AREA = 729 SQ.M.)**
- RC PLATFORM 2 (AREA = 243 SQ.M.)**
1. Supply and drive 0.40m x 0.40m PSC piles (4,230 l.m.) and chip/cut and dispose portion up to required elevation (162 no.)
 2. Supply and place 3,500 PSI concrete (515 cu.m.) and reinforcing steel bars (84,569 kg of various sizes) for superstructure
 3. Supply and install hot-dipped galvanized BWT 100mm x 12mm for construction joint-1, including dowel bars (36 l.m.)

4. Supply and install hot-dipped galvanized angle bar, 100mm x 100mm x 10mm for construction joint, including dowel bars (36 l.m.)
5. Supply and install Rubber Dock Fenders (V500H x 1500L - 4 sets)
6. Supply and install mooring bollard, (35-tons, t-head - 2 sets)

DATE OF BIDDING : **03 August 2021**

DATE OF NOTICE OF AWARD : **11 November 2021**

DATE OF NOTICE TO PROCEED : **07 December 2021**

ORIGINAL CONTRACT DURATION : **450 calendar days**

APPROVED BUDGET AMOUNT : **₱183,250,222.31**

SOURCE OF FUNDS : **PPA CORPORATE BUDGET**

IMPLEMENTING OFFICE : **PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)**

ORIGINAL CONTRACT AMOUNT : **₱176,538,323.78**

EFFECTIVITY DATE : **10 December 2021**

ORIGINAL EXPIRY DATE : **04 March 2023**

TIME EXTENSION NO. 1 : **65 calendar days**
Covering the delays encountered due to bad weather conditions for the period 10 December 2021 to 31 August 2022.

LATEST REVISED EXPIRY DATE : **08 May 2023**
(First Revision)

PROJECT STATUS : - The project is 87.842% complete with a negative slippage of 12.158%.
(As of 25 September 2023)


REMARKS : - On-going.
- Negative slippage of the project was due to unworkable weather condition.
- Contractor's request for time extension is under evaluation. Awaiting submission of supporting documents.

OFFICER-IN-CHARGE : **EUFEMIO C. VELASCO**
(Project Manager)

CONTACT NUMBER : **8-527-4435**

EMAIL ADDRESS : ec_velascojr@yahoo.com

SAN ANDRES PORT EXPANSION PROJECT PORT OF SAN ANDRES, QUEZON

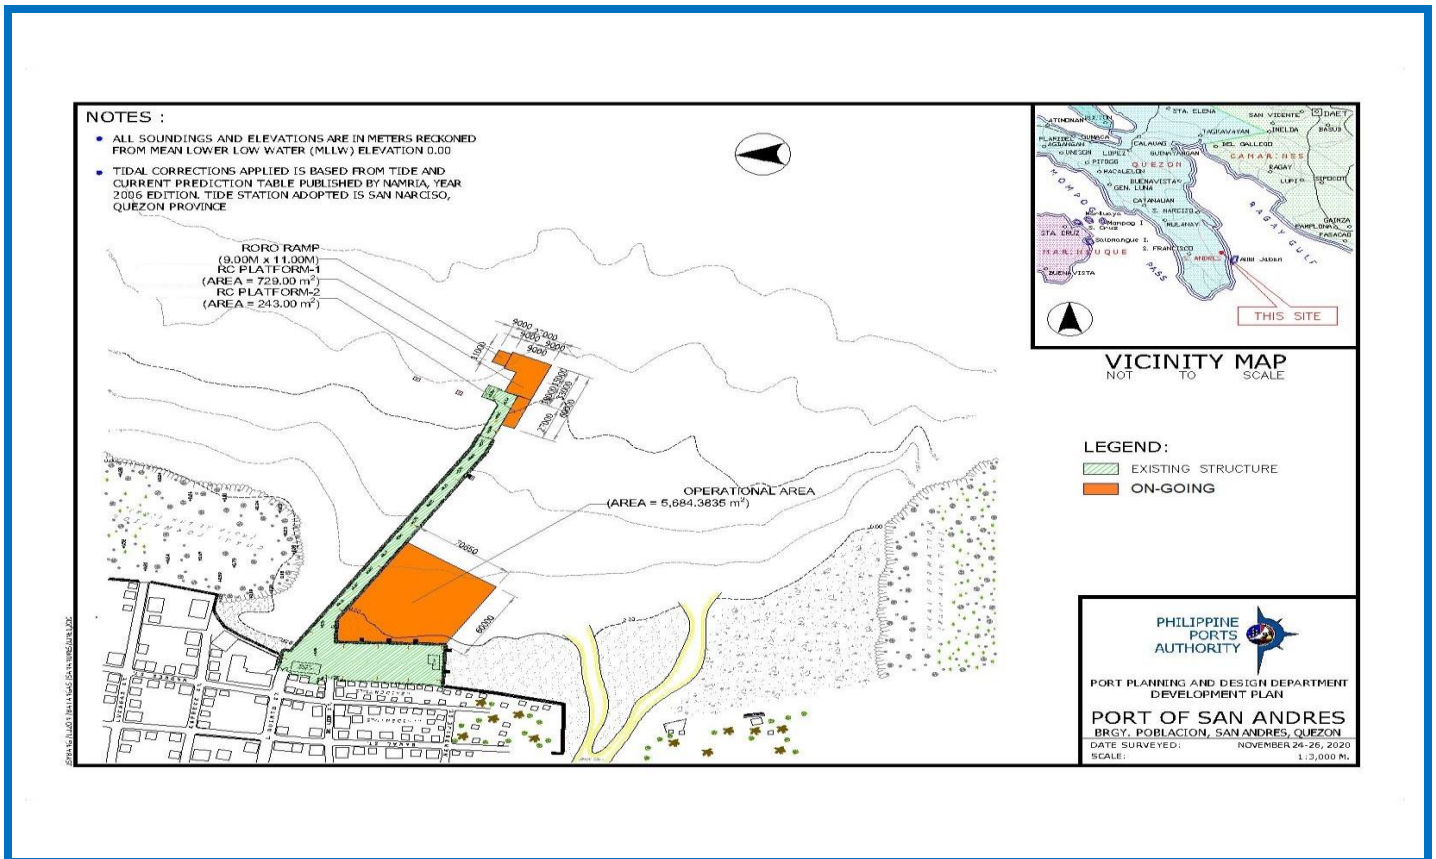

DEVELOPMENT PLAN



ONGOING CONSTRUCTION

PROJECT BRIEF

| | | |
|--|----------|--|
| PROJECT TITLE | : | CONSTRUCTION OF RORO RAMP AND RC PIER EXTENSION |
| LOCATION | : | PORT OF MANDAON, MASBATE |
| CONTRACTOR | : | PREMIUM MEGASTRUCTURES INC. |
| SCOPE OF WORK | : | A. DEMOLITION AND REMOVAL WORKS <ol style="list-style-type: none">Demolish and disposed existing RoRo ramp (Area = 99 sq.m.)Chip/cut and dispose portion of existing PSC piles up to required elevation for built-up (9 no.)Remove and turn-over to PPA existing Rubber Dock Fender (5 no.) B. RORO RAMP AND RC PIER EXTENSION <ol style="list-style-type: none">Supply, drive & cut of 500mm x 12mm thk SPP (3,204 l.m., 463 m.t.) including application of polyurethane external coating (2,515 sq.m.)Extraction of clogged materials (181 cu.m.), placing concrete filler (348 cu.m.) and reinforcing steel cage for SPP (89,660 kg.)Supply and place 3,500 PSI concrete for superstructure (803 cu.m.)Supply and install reinforcing steel bars (120,652 kg.)Supply and install hot-dipped galv. 100mm x 100mm angle bar for construction joints (44 l.m.) C. MOORING AND FENDERING SYSTEM <ol style="list-style-type: none">Supply and install Rubber Dock Fender V-type, 500H x 1500L (39 set)Supply and install mooring bollard 35 Tons T-head (18 set) |
| DATE OF BIDDING | : | 29 June 2021 |
| DATE OF NOTICE OF AWARD | : | 27 August 2021 |
| DATE OF NOTICE TO PROCEED | : | 12 October 2021 |
| ORIGINAL CONTRACT DURATION | : | 360 calendar days |
| APPROVED BUDGET AMOUNT | : | ₱109,869,661.78 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : | PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : | ₱108,889,860.11 |
| VARIATION ORDER NO. 1 | : | ₱443,395.88 |
| (Change Order No. 1/ Extra Work Order No. 1) | - | Covering the additional quantities as called for by the demolition/removal works and the time needed to facilitate the said changes and the unworkable days brought about by rough sea conditions from 07 October 2022 to 31 January 2023. |
| REVISED CONTRACT AMOUNT | : | ₱109,333,255.99 |
| (First Revision) | | |
| EFFECTIVITY DATE | : | 12 October 2021 |
| ORIGINAL EXPIRY DATE | : | 06 October 2022 |

**TIME EXTENSION NO. 1 /
TIME ADJUSTMENT NO. 1**

- : **334 calendar days**
- Covering the delays due to COVID-19 Delta and Omicron Variants, late issuance of Environmental Compliance certificate and unworkable days brought by rough sea conditions.

REVISED EXPIRY DATE
(First Revision)

: **05 September 2023**

TIME EXTENSION NO. 2

- : **203 calendar days**
- Due to Variation Order No. 1
- Due to Weather Disturbances

REVISED EXPIRY DATE
(First Revision)

: **27 March 2024**

PROJECT STATUS
(As of 25 September 2023)

- : - The project is 68.703% complete and progressing ahead of 10.753%.

REMARKS

- : - On-going.

OFFICER-IN-CHARGE

: **MA. NANCY S. SILVA**
(Project Manager)


CONTACT NUMBER

8-527-4435


EMAIL ADDRESS

nanz0128@yahoo.com

CONSTRUCTION OF RORO RAMP AND RC PIER EXTENSION PORT OF MANDAON, MASBATE

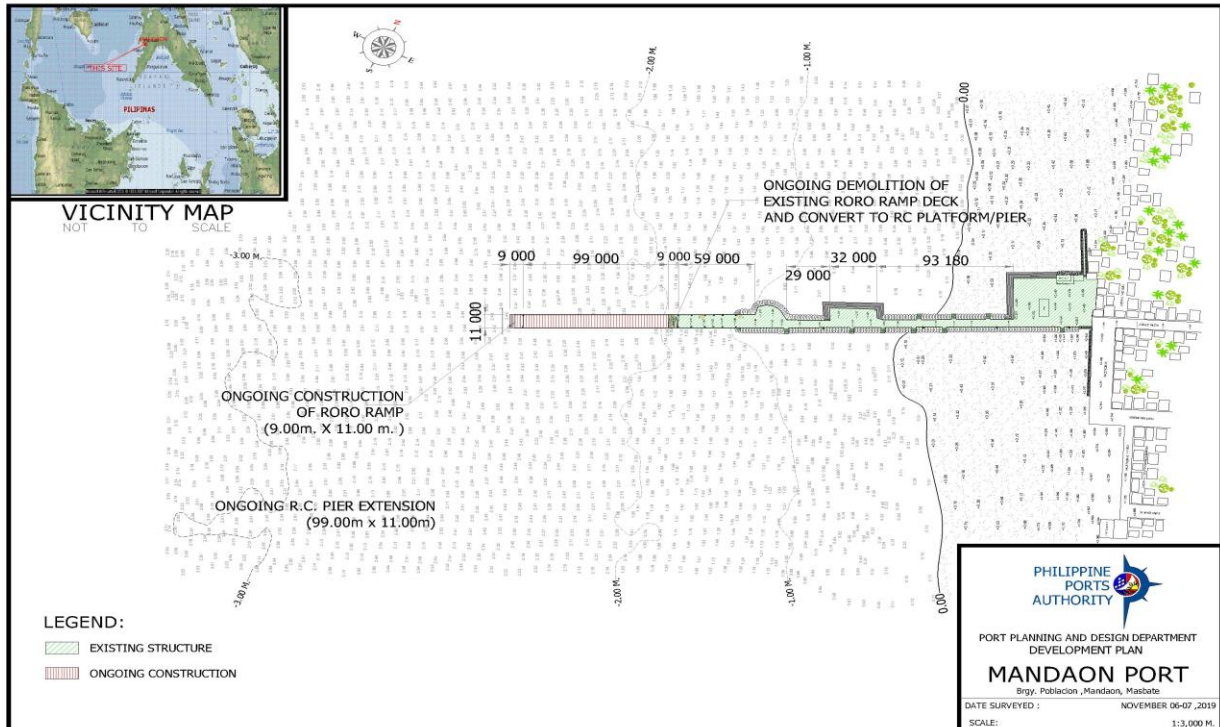

DEVELOPMENT PLAN

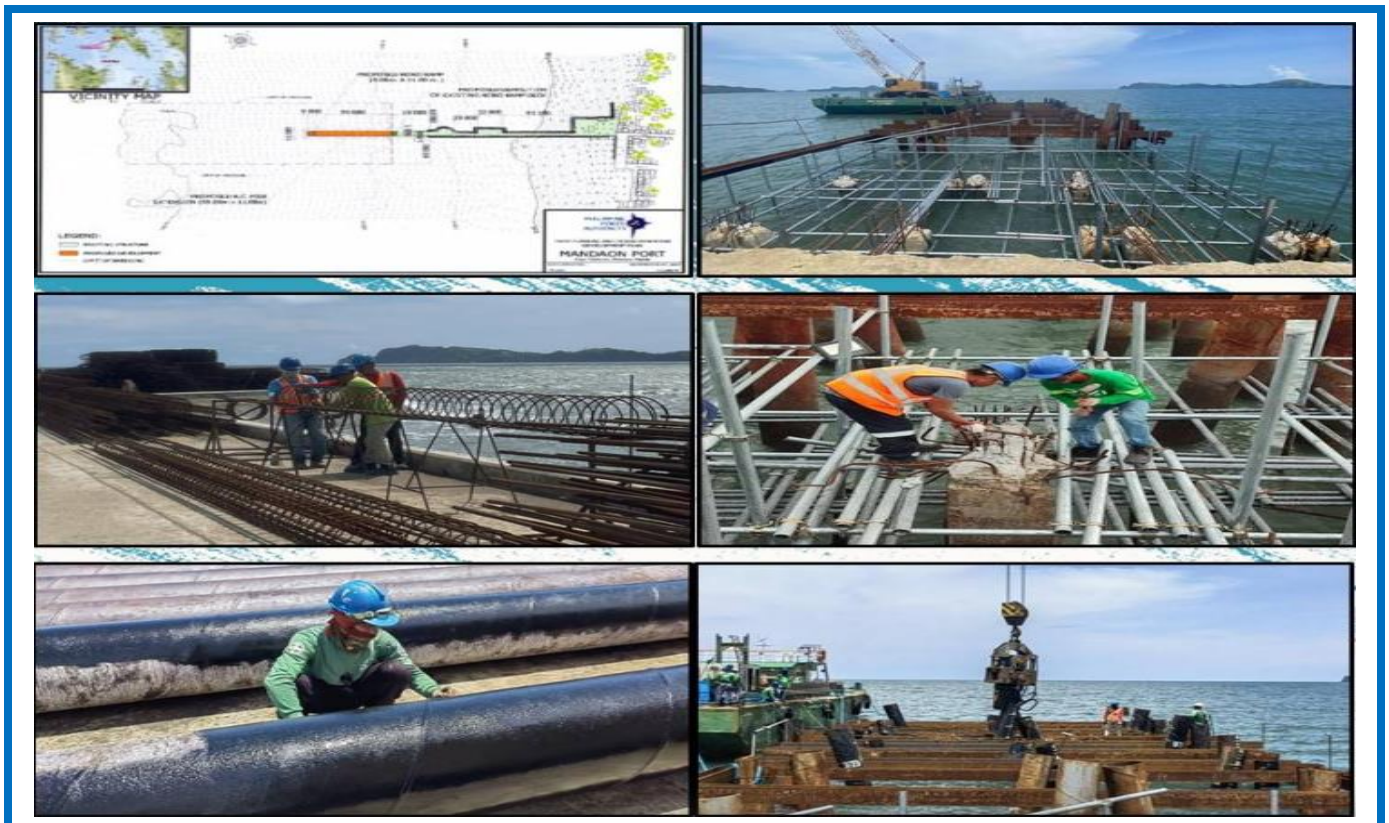

ONGOING CONSTRUCTION

PROJECT BRIEF


- PROJECT TITLE** : **LEGAZPI PORT REHABILITATION PROJECT**
- LOCATION** : **PORT OF LEGAZPI, LEGAZPI, ALBAY**
- CONTRACTOR** : **SUNWEST CONSTRUCTION AND DEVT CORP/
KHAN KON CHI CONSTRUCTION AND
DEVELOPMENT CORP./ J.V.**
- SCOPE OF WORK** : **A. REHABILITATION OF EXISTING BACK-UP AREA**
1. Removal of existing lamp post (2 units), damaged portion of concrete pavement (9,607 sq.m.) and scattered rocks (479 cu.m.) including disposal and turning-over of recovered materials with value to PPA authority
 2. Excavation of existing fill materials up to required elevation (1,897 cu.m.)
 3. Supply and delivery to site tubular sheet piles, 900mm diameter x 13mm thick x 24m long (2,402 m.t.) including driving (7,728 l.m.), application of protective coating (10,015 sq.m.) and installation of various steel accessories (35,627 kg.)
 4. Supply and place concrete fill for tubular sheet piles (580 cu.m.) including installation of steel reinforcements (72,360 kg.) and sand filler (356 cu.m.)
 5. Supply and delivery to site 400mm x 400mm x 15m long RC piles (5 units) including driving (75 l.m.) and chipping of piles up to required elevation (5 units)
 6. Supply and installation of tie-rods of various sizes and lengths; a) 32mm diameter x 16m (33 sets), b) 32mm diameter x 12m (1 set), c) 70mm diameter x 20m (140 sets), d) 70mm diameter x 18m (18 sets), e) 70mm diameter x 16m (1 set), f) 70mm diameter x 15m (1 set) and g) 70mm diameter x 14m (1 set)
 7. Supply and place 50-100 kg/pc core rocks (6,501 cu.m.)
 8. Supply and place sand and gravel fill (27,726 cu.m.), geotextile filter (5,906 sq.m.), aggregate subbase course (5,153 cu.m.) and gravel bedding (135 cu.m.)
 9. Construct 300mm thick Portland Cement Concrete Pavement (15,632 sq.m.) including placement of gravel base course (3,127 cu.m.)
 10. Supply and place 3,500 PSI concrete (1,731 cu.m.) including steel reinforcement (133,496 kg.)
 11. Supply and installation of 50T, T-head mooring bollards (17 sets) and V-type Rubber Dock Fenders, V600H x 2000L (32 sets)
 12. Supply and installation of 750mm diameter RCPC (58 l.m.) and steel gratings (480 l.m.)

B. PORT LIGHTING SYSTEM

1. Supply and installation of hot-dipped galvanized floodlight steel poles, 12 meter-high (5 units) and 10 meter-high (1 unit), with 250 watt LED floodlight fixtures (42 sets), including accessories, protective devices, conduit pipes and fittings and electrical wires and cables of various sizes

| | |
|--|---|
| DATE OF BIDDING | : 26 May 2021 |
| DATE OF AWARD | : 25 June 2021 |
| DATE OF NOTICE TO PROCEED | : 09 August 2021 |
| CONTRACT DURATION | : 630 calendar days |
| APPROVED BUDGET AMOUNT | : ₱498,251,930.50 |
| SOURCE OF FUNDS | : PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : ₱495,881,192.21 |
| EFFECTIVITY DATE | : 09 August 2021 |
| ORIGINAL EXPIRY DATE | : 30 April 2023 |
| TIME ADJUSTMENT NO. 1/ TIME EXTENSION NO. 1 | : 171 calendar days - Covering the delay brought by the unworkable bad weather condition. |
| REVISED EXPIRY DATE (First Revision) | : 18 October 2023 |
| PROJECT STATUS (As of 25 September 2023) | : - The project is 80.044% complete with a negative slippage of 15.533%. |
| REMARKS: | : - Ongoing. - Negative slippage was due to unworkable weather condition and issued state of calamity in the Province of Albay. - Warning letters were sent to the Contractor to undertake measures to cope with the project's delay. - The Contractor has a pending request for time extension due to unworkable days. |
| OFFICER-IN-CHARGE | : EMIL JOSE GARCIA (Project Manager) |
| CONTACT NUMBER | : 8-527-4435 |
| EMAIL ADDRESS | : |

LEGAZPI PORT REHABILITATION PROJECT PORT OF LEGAZPI, LEGAZPI, ALBAY

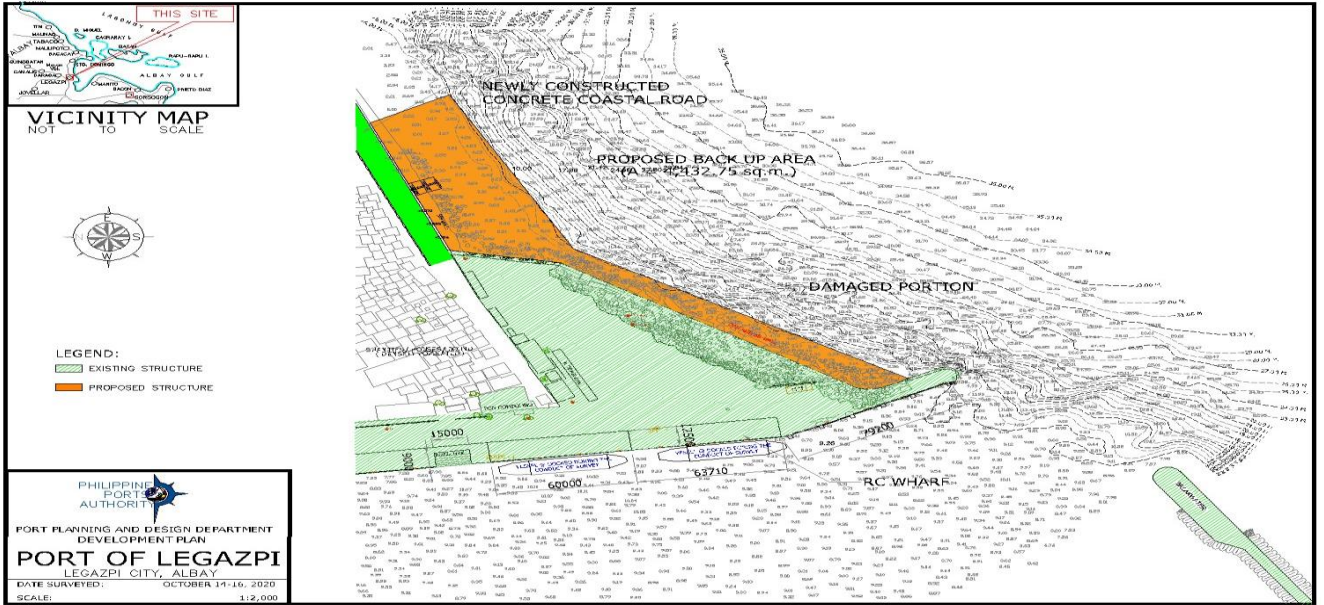

DEVELOPMENT PLAN



ONGOING CONSTRUCTION

PROJECT BRIEF

| | | |
|---|----------|--|
| PROJECT TITLE | : | CONSTRUCTION OF STAFF QUARTERS, LAW ENFORCEMENT BUILDING AND GATE |
| LOCATION | : | PORT OF CURRIMAO, CURRIMAO ILOCOS NORTE |
| CONTRACTOR | : | DLM KONSTRUCT, INCORPORATED |
| SCOPE OF WORK | : | <ol style="list-style-type: none">1. Construction of 2-storey Staff Quarters Building complete with foundation piles, architectural finishes, electro mechanical, water/sewerage system.2. Construction of 3-storey Law Enforcement Building, complete with foundation piles, architectural finishes, electro/mechanical, water/sewerage system.3. Construction of Pumphouse & appurtenances (1-unit)4. Construction of Guardhouse (1-unit)5. Supply/installation of Gate (1-unit)6. Supply, delivery & installation of distribution transformer & accessories (1-lot)7. Supply & installation of fire protection system (1 lot)8. Supply & installation of wastewater treatment facility (1-lot) |
| DATE OF BIDDING | : | 27 July 2021 |
| DATE OF AWARD | : | 07 September 2021 |
| DATE OF NOTICE TO PROCEED | : | 28 October 2021 |
| CONTRACT DURATION | : | 480 calendar days |
| APPROVED BUDGET AMOUNT | : | ₱207,484,188.46 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : | PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : | ₱206,973,844.74 |
| EFFECTIVITY DATE | : | 02 November 2021 |
| ORIGINAL EXPIRY DATE | : | 24 February 2023 |
| TIME EXTENSION NO. 1 / TIME ADJUSTMENT NO. 1 | : | 100 calendar days <ul style="list-style-type: none">- Covering the time elapsed of the suspension of work activities due to non-removal of existing temporary field office on the proposed area from December 10, 2021, to January 23, 2022 and delay due to unworkable days caused by bad weather conditions from January 27, 2022 up to October 17, 2022. |
| REVISED EXPIRY DATE (First Revision) | : | 04 June 2023 |

PROJECT STATUS

(As of 25 September 2023)

: - The project is 96.598% complete with a negative slippage of 3.402%.

REMARKS:

- : - Ongoing.
- Negative slippage of the project was due to unworkable weather condition.
- Warning letters were sent to the Contractor to undertake measures to cope with the project's delay.
- Variation Order with time adjustment / extension covering the additional works as requested by PMO and inclusion of other items of work that were reflected in the approved plans but were not included in pay items of work in the BOQ is for management approval.

OFFICER-IN-CHARGE

: **EXZUR G. GOMEZ**
(Project Manager)


CONTACT NUMBER

: **8-527-4435**

EMAIL ADDRESS

: gomezexzur@yahoo.com

CONSTRUCTION OF STAFF QUARTERS, LAW ENFORCEMENT BUILDING AND GATE PORT OF CURRIMAO, CURRIMAO ILOCOS NORTE

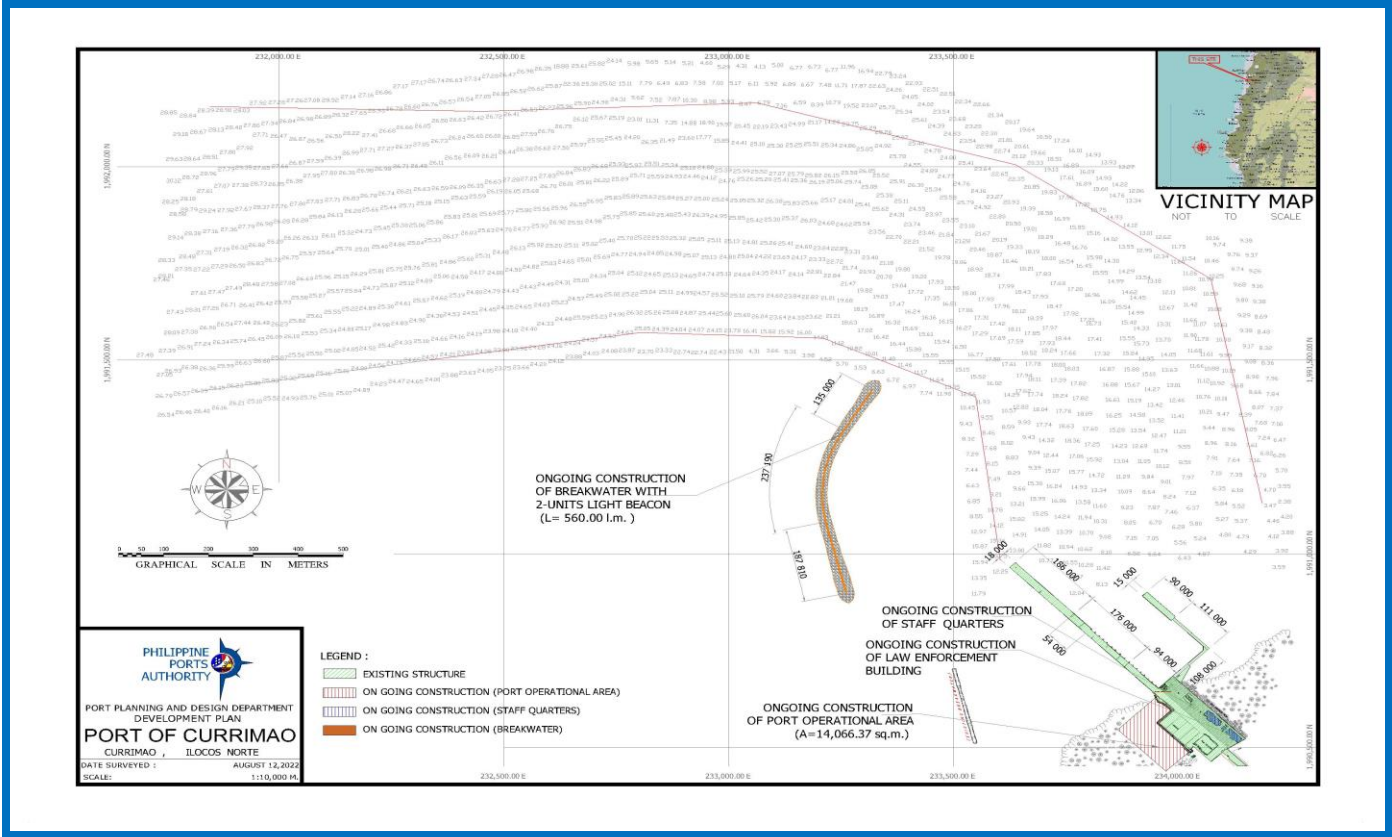

DEVELOPMENT PLAN



ONGOING CONSTRUCTION

PROJECT BRIEF

| | | |
|---------------------------|---|--|
| PROJECT TITLE | : | REHABILITATION / IMPROVEMENT OF CLAVERIA PORT |
| LOCATION | : | PORT OF CLAVERIA, TAGGAT NORTE, CAGAYAN |
| CONTRACTOR | : | HI-TONE CONSTRUCTION AND DEVELOPMENT CORP./ KXBG CONSTRUCTION AND DEVELOPMENT CORP. - JV |
| SCOPE OF WORK | : | <p>A. DEMOLITION, REMOVAL AND EXCAVATION WORKS</p> <ol style="list-style-type: none">1. Demolition & disposal of existing concrete pavement (1,402 sq.m.)2. Demolition & disposal of existing curb, seat and deflector wall (428 cu.m.)3. Excavation of existing seabed (9,403 cu.m.)4. Excavation and backfilling of fill materials (98 cu.m.)5. Extraction of existing rocks (1,518 cu.m.)6. Removal of existing concrete blocks (994 pcs.) <p>B. BACK-UP AREA WITH RO-RO RAMP ON-FILL</p> <ol style="list-style-type: none">1. Supply, delivery & driving of steel sheet piles (575 m.t.; 5,596 l.m.)2. Supply & installation steel waling (36,703 kg.)3. Cutting of newly driven sheet piles (494 nos.)4. Supply & installation of tie-rods of various sizes (126 sets)5. Reinforced concrete works (1,311 cu.m.)6. Supply & installation of core rocks (7,512 cu.m.)7. Supply & placing of fill materials (43,577 cu.m.)8. Reinstallation of newly removed concrete blocks (459 pcs)9. Construction of PCC pavement (10,287 sq.m.)10. Supply & installation of Rubber Dock Fenders (5 sets)11. Supply & installation of mooring bollards (2 sets)12. Construction of security fence and gate (153 l.m.)13. Port lighting and drainage system (1 lot) |
| DATE OF BIDDING | : | 27 May 2021 |
| DATE OF AWARD | : | 25 June 2021 |
| DATE OF NOTICE TO PROCEED | : | 05 August 2021 |
| CONTRACT DURATION | : | 660 calendar days |
| APPROVED BUDGET AMOUNT | : | ₱249,220,579.21 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : | PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : | ₱247,815,087.76 |

EFFECTIVITY DATE : **05 August 2021**

ORIGINAL EXPIRY DATE : **26 May 2023**

TIME EXTENSION NO. 1 : **204 calendar days**
- Covering the temporary suspension and repair of damaged structures due to Typhoon "Neneng".

REVISED EXPIRY DATE : **16 December 2023**
(First Revision)

PROJECT STATUS : - The project is 99.613% complete and progressing ahead of
(As of 25 September 2023) 13.188%.


REMARKS: : - Ongoing.

OFFICER-IN-CHARGE : **EMIL JOSE GARCIA**
(Project Manager)

CONTACT NUMBER : **8-527-4435**

EMAIL ADDRESS :

REHABILITATION/IMPROVEMENT OF CLAVERIA PORT PORT OF CLAVERIA, TAGGAT NORTE, CAGAYAN

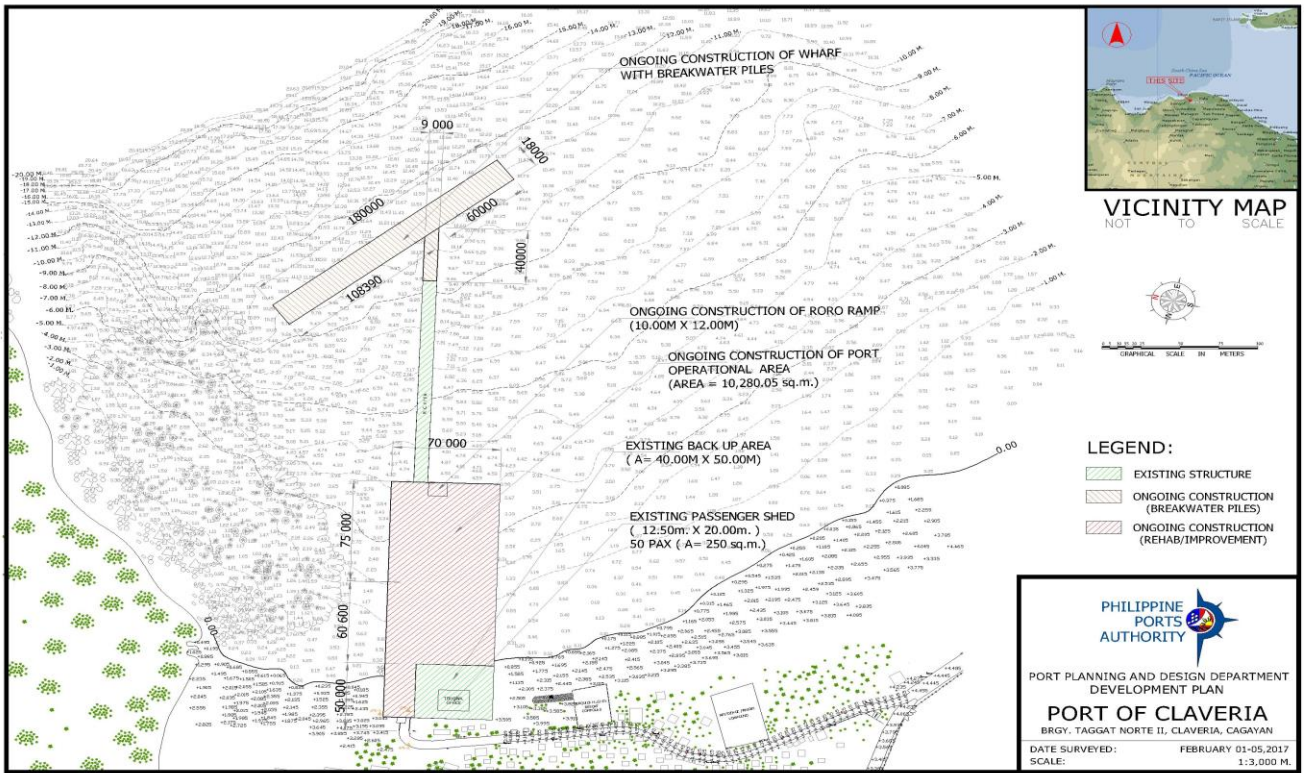

DEVELOPMENT PLAN



ONGOING CONSTRUCTION

PROJECT BRIEF

| | | |
|--|---|--|
| PROJECT TITLE | : | CONSTRUCTION OF WHARF WITH BREAKWATER PILES |
| LOCATION | : | PORT OF CLAVERIA, TAGGAT NORTE, CAGAYAN |
| CONTRACTOR | : | MRBII CONSTRUCTION CORPORATION/KHAN KON CHI CONSTRUCTION AND DEVELOPMENT CORP./JV |
| SCOPE OF WORK | : | A. PIER EXTENSION & WHARF WITH BREAKWATER PILES <ol style="list-style-type: none">1. Supply & delivery of steel pipe piles (3,377 m.t.)2. Handling & driving steel pipe piles (17,421 l.m.)3. Cutting of newly driven steel pipe piles (685 units)4. Supply & installation of reinforcing band tip (18,695 kg.)5. Extraction of clogged materials (831 cu.m.)6. Supply & place concrete filler for steel pipe piles (3,260 cu.m.)7. Supply & installation of reinforcing steel cage (519,853 kg.)8. Supply & placing of concrete for the superstructure (2,552 cu.m.)9. Supply & installation of reinforcing steel bar for the superstructure (320,785 kg.)10. Supply & installation of construction joints (78 l.m.)11. Supply & installation of Rubber Dock Fenders (16 sets)12. Supply & installation of mooring bollards (31 sets) |
| DATE OF BIDDING | : | 03 June 2021 |
| DATE OF AWARD | : | 06 July 2021 |
| DATE OF NOTICE TO PROCEED | : | 05 August 2021 |
| CONTRACT DURATION | : | 750 calendar days |
| APPROVED BUDGET AMOUNT | : | ₱623,005,524.18 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : | PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : | ₱618,759,218.79 |
| VARIATION ORDER NO. 1 (Change Order No. 1/ Extra Work Order No. 1) | : | ₱16,274,512.56 - Covering the quantity adjustment of some of the original items of work as called for the required/additional pile length of steel pipe piles is necessary for the protection and completion of the project and to suit the actual field condition. |
| REVISED CONTRACT AMOUNT (First Revision) | : | ₱635,033,731.35 |
| EFFECTIVITY DATE | : | 05 August 2021 |
| ORIGINAL EXPIRY DATE | : | 24 August 2023 |

TIME EXTENSION NO. 1

: **180 calendar days**

- Covering the time elapsed due to unworkable bad weather and rough sea conditions.

REVISED EXPIRY DATE

(First Revision)

: **20 February 2024**

PROJECT STATUS

(As of 25 September 2023)

- The project is 77.464% complete with a negative slippage of 15.763%.

REMARKS:

- Ongoing.
- Negative slippage was due to unworkable weather and rough sea conditions.

OFFICER-IN-CHARGE

: **EMIL JOSE GARCIA**

(Project Manager)


CONTACT NUMBER

: **8-527-4435**


EMAIL ADDRESS

:

CONSTRUCTION OF WHARF BREAKWATER PILES PORT OF CLAVERIA, TAGGAT NORTE, CAGAYAN

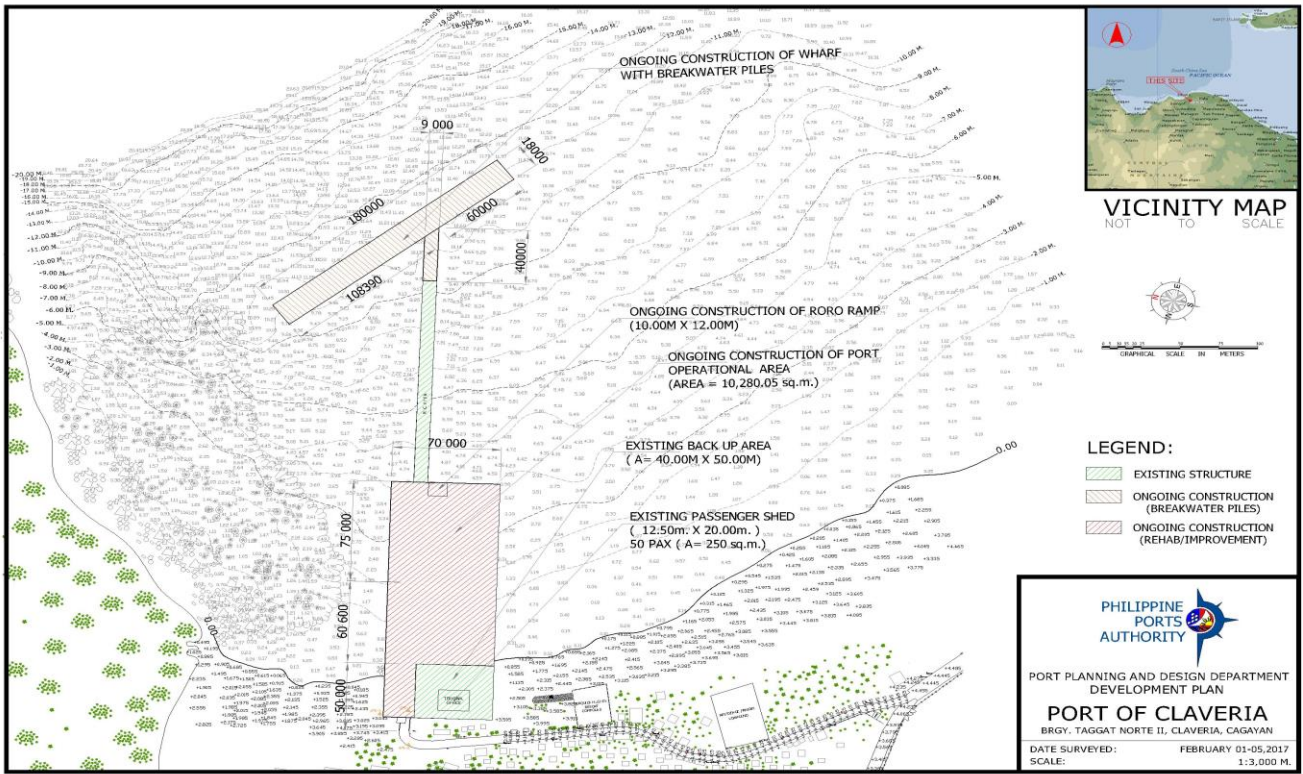

DEVELOPMENT PLAN

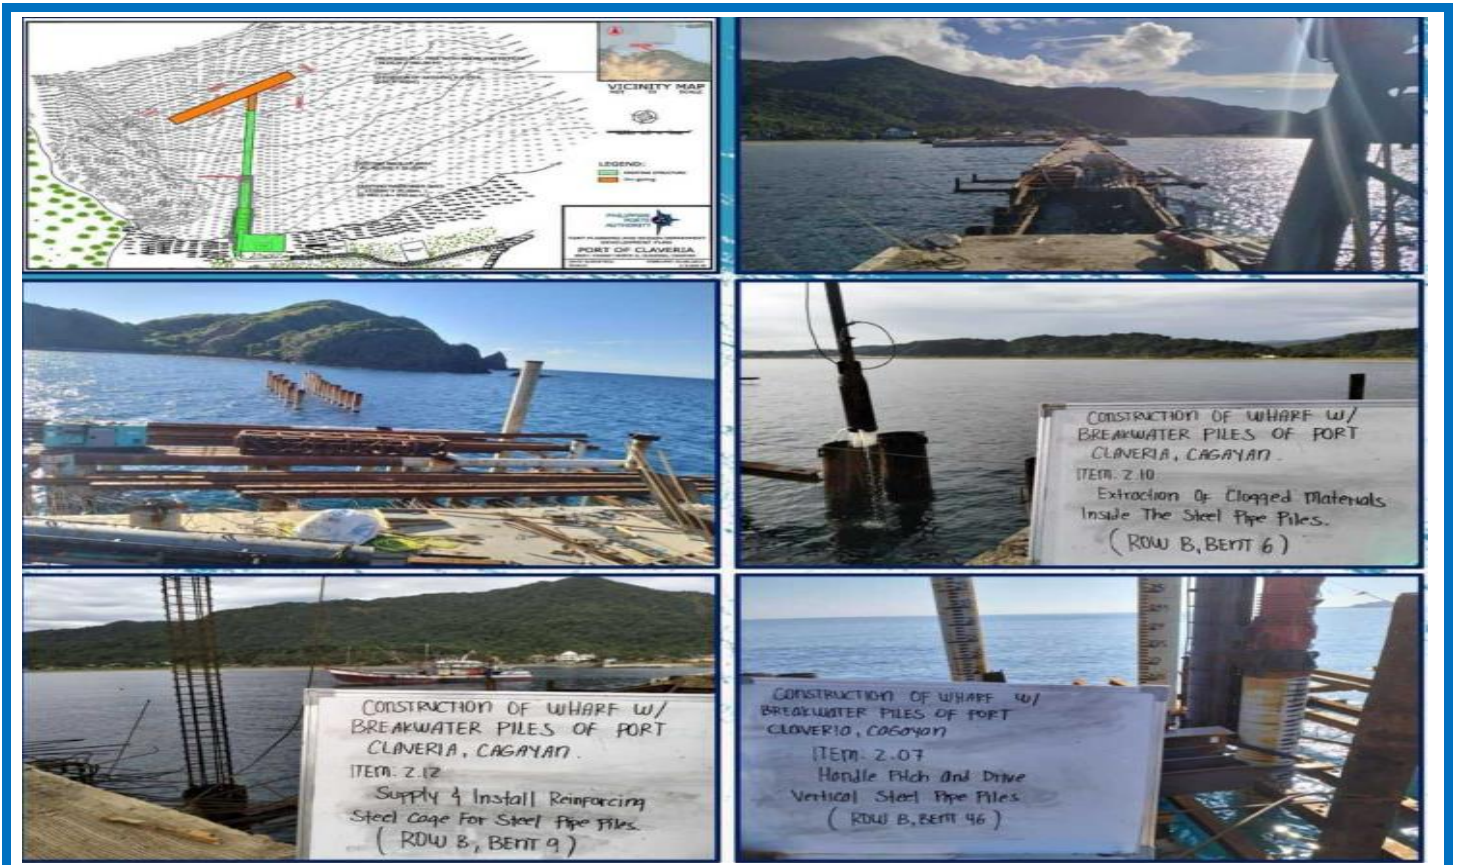

ONGOING CONSTRUCTION

PROJECT BRIEF

| | | |
|----------------------------|---|---|
| PROJECT TITLE | : | CONSTRUCTION OF RC PLATFORM WITH RORO RAMP AND RC PIER |
| LOCATION | : | PORT OF SAN ANDRES, CATANDUANES |
| CONTRACTOR | : | |
| SCOPE OF WORK | : | <p>A. DEMOLITION & REMOVAL WORKS</p> <ol style="list-style-type: none">1. Demolish and dispose existing structure (RoRo Ramp) for build up (77 sq.m.)2. Chip-off portion of existing R.C. Curb (34 l.m.)3. Chip-off portion of existing mooring block to be aligned to pier (15 cu.m.)4. Removed and turn over to PPA existing mooring bits, mooring cleats and rubber dock fenders affected by demolition (12 no.)5. Chip-off existing concrete piles for build-up (12 no.) <p>B. RC PLATFORM, RORO RAMP AND RC PIER</p> <ol style="list-style-type: none">1. Supply and drive A252 Grade 2, 500mm Ø Steel Pipe Piles (536 m.t. - 4,663 l.m.) including application of polyurethane external coating (1,584 sq.m.), installation of reinforcing band tip (111 pcs), splicing (111 pcs) and cutting (111 pcs)2. Supply and place 3,500 psi concrete filler (224 cu.m.) and reinforcing steel cage (67,348 kgs of various sizes) for steel pipe piles including extraction of clogged materials (60 cu.m.)3. Supply and place 3,500 psi concrete (664 cu.m.) and reinforcing steel bars (108,767 kg of various sizes) for superstructure4. Supply and install of Rubber Dock Fenders (V500 x 1500L - 16 sets) and mooring bollard, (35-tons, T-head - 8 sets) |
| DATE OF BIDDING | : | |
| DATE OF NOTICE OF AWARD | : | |
| DATE OF NOTICE TO PROCEED | : | |
| ORIGINAL CONTRACT DURATION | : | 450 calendar days |
| APPROVED BUDGET AMOUNT | : | ₱108,004,897.34 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : | PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : | ₱122,045,533.99 |
| EFFECTIVITY DATE | : | |
| ORIGINAL EXPIRY DATE | : | |
| PROJECT STATUS | : | |
| REMARKS | : | <p>- Failure of bidding on 25 June 2021. - For re-advertisement.</p> |
| OFFICER-IN-CHARGE | : | |
| CONTACT NUMBER | : | |
| EMAIL ADDRESS | : | |

CONSTRUCTION OF RC PLATFORM WITH RORO RAMP AND RC PIER PORT OF SAN ANDRES, CATANDUANES



DEVELOPMENT PLAN

ONGOING CONSTRUCTION

PROJECT BRIEF

| | |
|----------------------------------|--|
| PROJECT TITLE | : CONSTRUCTION OF CRUISE SHIP PORT |
| LOCATION | : PORT OF CORON, PALAWAN |
| CONTRACTOR | : PREMIUM MEGASTRUCTURES, INC. |
| SCOPE OF WORK | : A. PORT OPERATIONAL AREA <ol style="list-style-type: none">1. Excavation & backfilling works (6,015 cu.m.)2. Supply & placing of 3,500 PSI concrete (1,241 cu.m.)3. Supply & installation of steel reinforcement (42,273 kg.)4. Supply & placing of core rocks & armour rocks (12,433 cu.m.)5. Supply & installation of pre-cast concrete blocks (313 sets)6. Supply & installation of pre-cast concrete caisson (2 sets)7. Supply & installation of gravity type mooring concrete block (2 sets)8. Placing & compaction of excavated seabed materials (124 cu.m.)9. Supply & installation of geotextile fabric (6,300 sq.m.)10. Supply & placing of fill materials (62,474 cu.m.)11. Construction of PCC Pavement including Agg. Base Course (19,094 sq.m.)12. Construction of Security Fence & Gate (1 lot)13. Supply & installation of Portlighting System (1 lot)14. Supply & installation of Rubber Dock Fenders (35 sets)15. Supply & installation of mooring bollard (12 sets) B. PROVISION OF PONTOON BARGE <ol style="list-style-type: none">1. Design, fabrication & delivery of steel pontoon barge including processing of required documents for the construction of the vessel and MARINA certificates (1 lot) |
| DATE OF BIDDING | : 11 May 2022 |
| DATE OF AWARD | : 06 June 2022 |
| DATE OF NOTICE TO PROCEED | : 09 December 2022 |
| CONTRACT DURATION | : 540 calendar days |
| APPROVED BUDGET AMOUNT | : ₱425,070,501.09 |
| SOURCE OF FUNDS | : PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : ₱418,150,000.00 |
| EFFECTIVITY DATE | : 12 December 2022 |
| ORIGINAL EXPIRY DATE | : 03 June 2024 |

PROJECT STATUS

(As of 25 September 2023)

- : - The project was suspended effective 12 December 2022 due to pending issuance of Environmental Compliance Certificate (ECC) and issues/clearances from PRA and DENR in compliance with the Presidential Directive No. 2022-016.
- Awaiting for the endorsement of the Barangay to LGU on the exemption to Marine Protected Areas.

REMARKS:

:

OFFICER-IN-CHARGE

: **EUFEMIO C. VELASCO JR.**

(Project Manager)


CONTACT NUMBER

8-527-4435


EMAIL ADDRESS

ec_velascojr@yahoo.com

CONSTRUCTION OF CRUISE SHIP PORT PORT OF CORON, PALAWAN

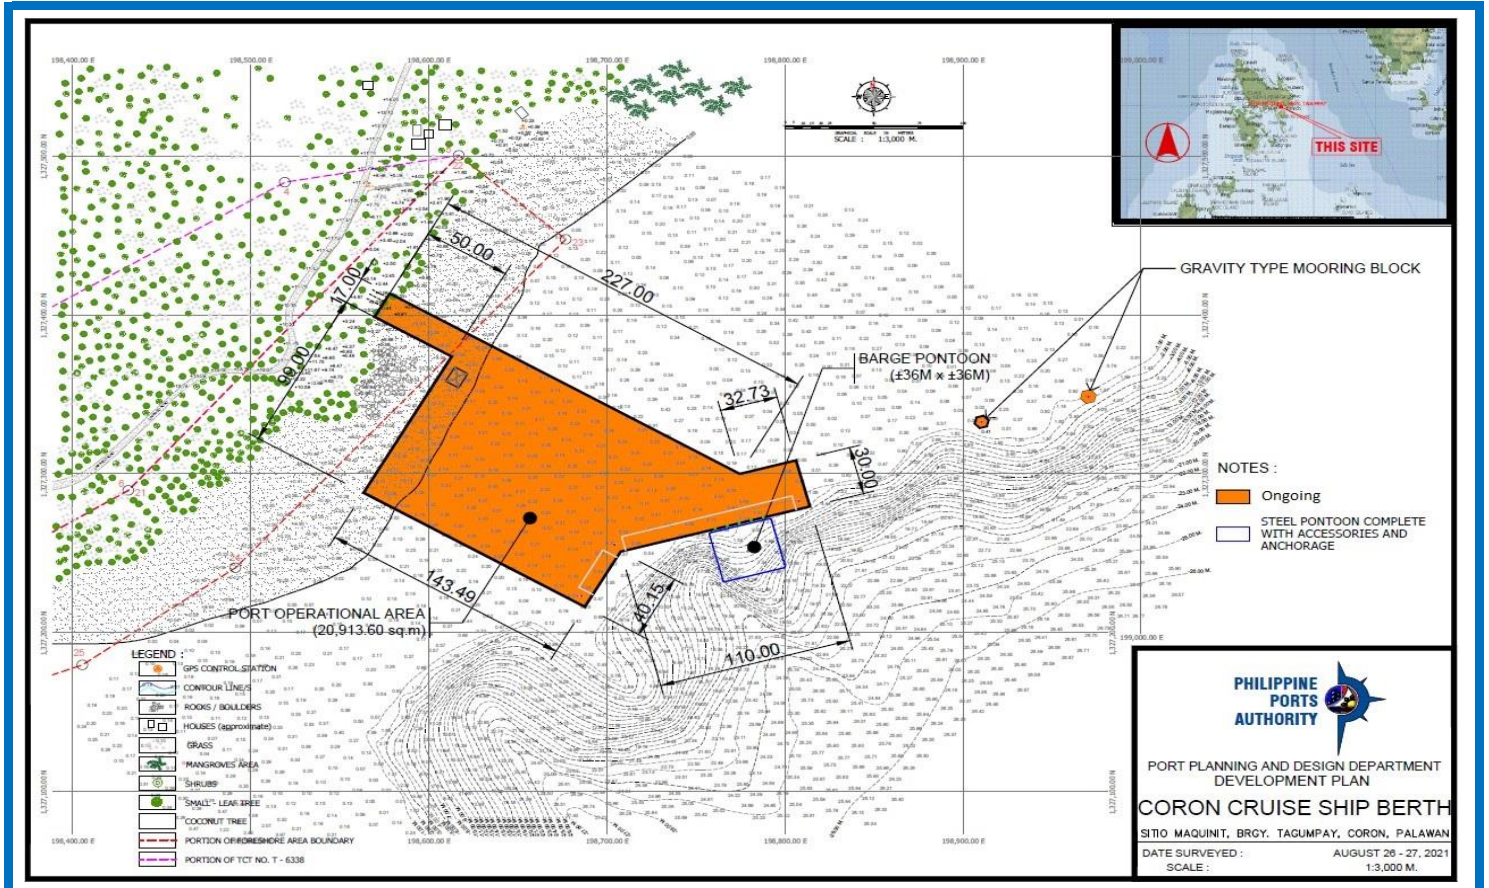

DEVELOPMENT PLAN

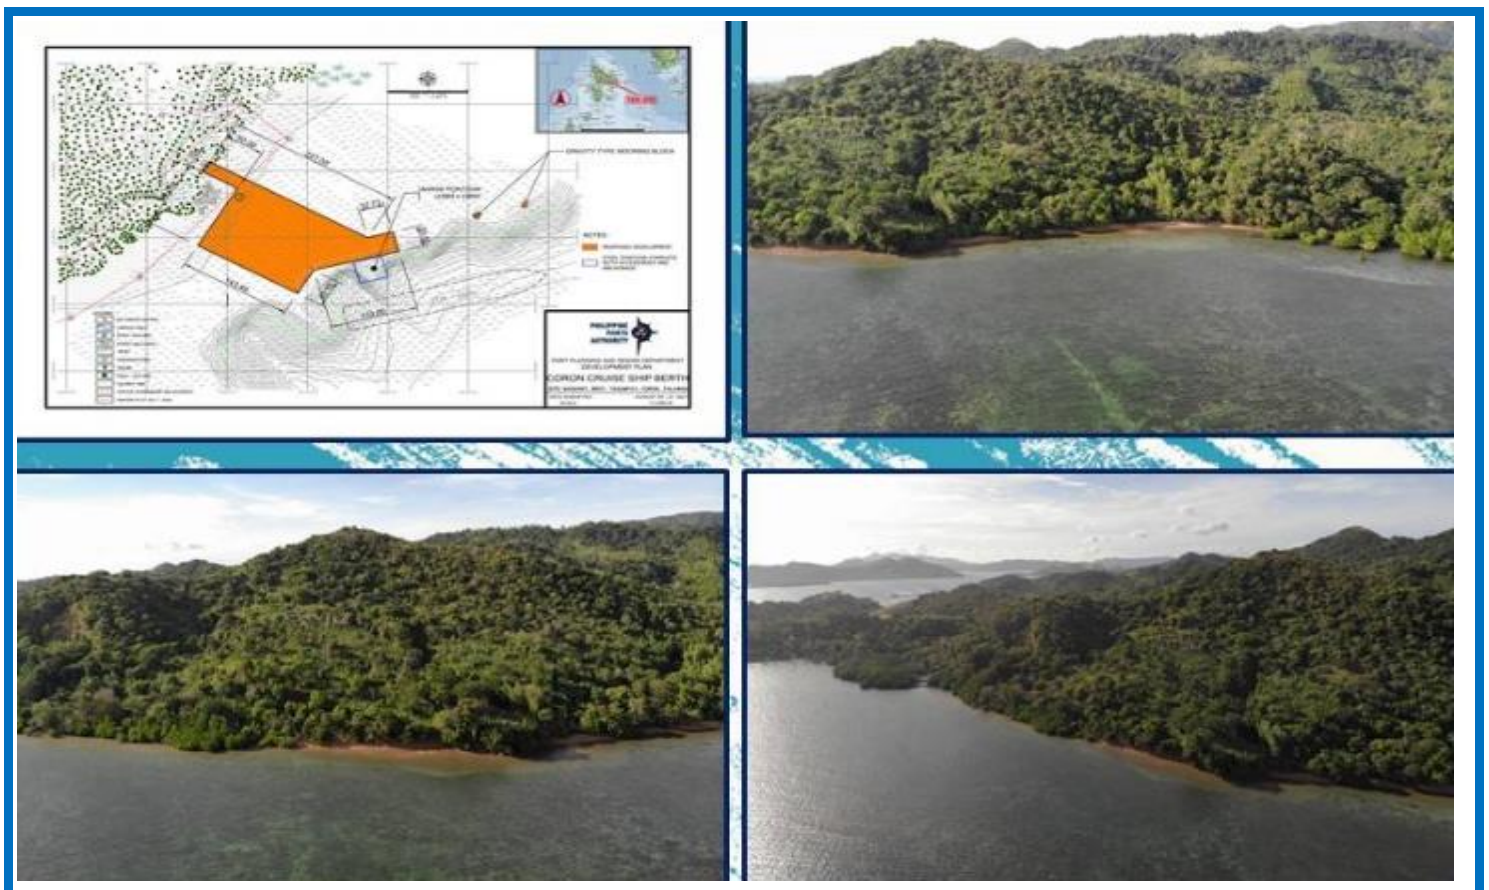

ONGOING CONSTRUCTION

PROJECT BRIEF

| | | |
|---------------------------|---|--|
| PROJECT TITLE | : | CONSTRUCTION OF PORT OPERATIONAL AREA AND EXPANSION OF EXISTING RC PIER |
| LOCATION | : | PORT OF EL NIDO, BRGY. BUENA SUERTE, EL NIDO, PALAWAN |
| CONTRACTOR | : | |
| SCOPE OF WORK | : | A. CONSTRUCTION OF PORT OPERATIONAL AREA WITH CONTINUOUS RORO RAMP (Area = 2,245.70 sq.m.) <ol style="list-style-type: none">1. Chip-off existing RC curb (97 l.m.), removal of existing mooring bollards and fenders and excavate existing seabed (889 cu.m.) and fill materials (89 cu.m.)2. Supply and deliver to site PSC and RC sheet piles (2,582 l.m.) including chipping of driven piles up to elevation (179 units)3. Supply and install concrete blocks (4 units) and rubble concrete (3 cu.m.)4. Supply and place 3,500 PSI concrete (310 cu.m.) including steel reinforcements (25,983 kg)5. Supply and install core rocks (3,480 cu.m.), armour rocks (1,273 cu.m.) and tie rods (48 units)6. Supply and place geotextile filter (1,690 sq.m.), sand & gravel fill (7,479 cu.m.), subbase (1,232 cu.m.)7. Supply and drive PSC square piles (105 l.m.) including chipping of driven piles up to required elevation (7 units)8. Supply and install V-type Rubber Dock Fenders (500H x 1, 500L, units) and 35 ton capacity mooring bollards (3 units)9. Supply and install Port Lighting System B. EXPANSION OF EXISTING RC PIER (Area = 540 sq.m.) <ol style="list-style-type: none">1. Supply and drive 400mm x 400mm PSC test piles (2 units)2. Supply and drive PSC square piles (1,684 l.m.) including chipping of driven piles up to required elevation (74 units)3. Supply and place 3,500 PSI concrete (259 cu.m.) including steel reinforcements (36,550 kg) and construction joints (12 l.m.) for superstructure4. Supply and install V-type Rubber Dock Fenders (500H x 1,500L, 10 units) and 35 ton capacity mooring bollards (10 units) |
| DATE OF BIDDING | : | |
| DATE OF AWARD | : | |
| DATE OF NOTICE TO PROCEED | : | |
| CONTRACT DURATION | : | 360 calendar days |
| APPROVED BUDGET AMOUNT | : | ₱128,288,247.58 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : | PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |

ORIGINAL CONTRACT AMOUNT : **₱144,965,719.76**

EFFECTIVITY DATE :

ORIGINAL EXPIRY DATE :

PROJECT STATUS : - Bidding was conducted on 12 May 2022.
- Disqualification of the lowest bidder, thus, for post qualification on the 2nd lowest bidder.


REMARKS: :

OFFICER-IN-CHARGE :


CONTACT NUMBER

EMAIL ADDRESS

CONSTRUCTION OF PORT OPERATIONAL AREA AND EXPANSION OF EXISTING RC PIER PORT OF EL NIDO, BRGY. BUENA SUERTE, EL NIDO, PALAWAN

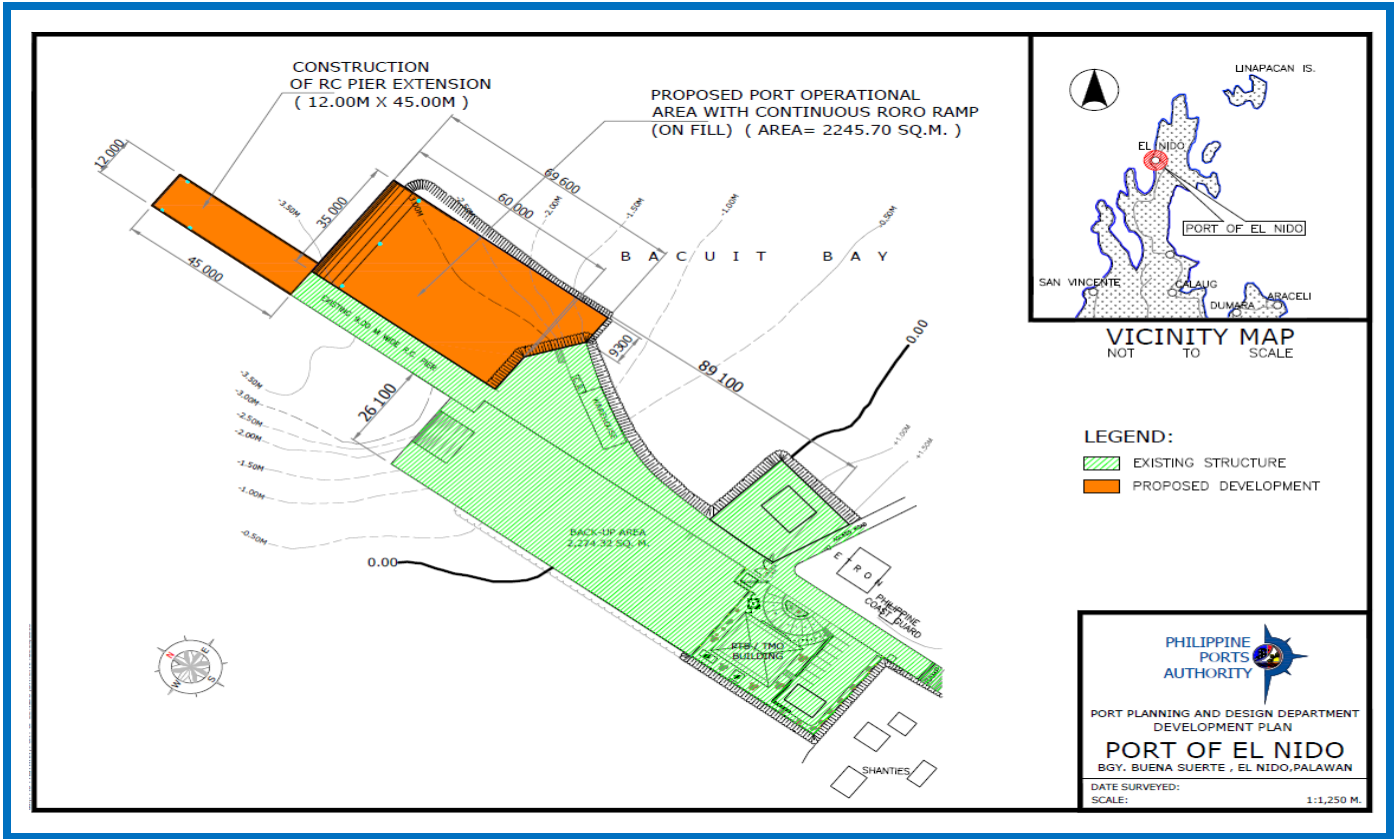

DEVELOPMENT PLAN



ONGOING CONSTRUCTION

PROJECT BRIEF

| | | |
|----------------------------------|----------|--|
| PROJECT TITLE | : | CONSTRUCTION OF PORT OPERATIONAL AREA |
| LOCATION | : | PORT OF CALAPAN, CALAPAN, ORIENTAL MINDORO |
| CONTRACTOR | : | ONE HUNDRED PERCENT CONST. AND DEV'T. CORP. / ORIENT STAR CONST. - J.V. |
| SCOPE OF WORK | : | A. CONSTRUCTION OF OPERATIONAL AREA <ol style="list-style-type: none">1. Chip-off portion of existing wall, flushed to deck level and smoothed with mortar (85 l.m.)2. Excavate fill materials for catch drain manhole, lateral drainage, lamp post foundation and concrete pedestal post (401 cu.m.)3. Supply & place 3,500 psi concrete for RC curb, shear keys, lateral drainage, catch drain manhole, lamp post foundation and concrete pedestal post (626 cu.m.)4. Supply & install steel reinforcement for RC curb, shear keys, lateral drainage, catch drain manhole, lamp post foundation and concrete pedestal post (29,719 kg)5. Supply and place 50-100 kg/pc core rocks (9,575 cu.m.)6. Supply and place 1,000 kg/pc armour rocks (5,205 cu.m.)7. Supply and install geotextile fabric (7,472 sq.m.)8. Supply and place sand gravel fill (62,756 cu.m.)9. Supply, place and compact aggregate subbase course (17,949 cu.m.)10. Supply, spread and compact aggregate base course (3,179 cu.m.)11. Supply, place and compact gravel bedding (30 cu.m.)12. Supply, spread and compact cement treated base course (3,032 cu.m.)13. Supply, spread and compact levelling course sand cushion (1,011 cu.m.)14. Supply, deliver and install interlocking concrete paving blocks (10,215 sq.m.)15. Re-install existing interlocking concrete paving blocks (10,000 sq.m.)16. Supply and install box culvert including 460mmØ reinforced concrete pipe for outfall (75 l.m.)17. Supply and install lateral drainage metal grating & manhole cover (298 l.m.)18. Supply & install port lighting system (1 lot)19. Construct perimeter fence at sea side (1 lot)20. Construct perimeter fence at south side (1 lot) |
| DATE OF BIDDING | : | 28 December 2021 |
| DATE OF AWARD | : | 28 January 2022 |
| DATE OF NOTICE TO PROCEED | : | 22 February 2022 |
| CONTRACT DURATION | : | 600 calendar days |

APPROVED BUDGET AMOUNT : ***₱270,159,503.27***

SOURCE OF FUNDS : **PPA CORPORATE BUDGET**

IMPLEMENTING OFFICE : **PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)**

ORIGINAL CONTRACT AMOUNT : ***₱267,441,018.21***

EFFECTIVITY DATE : **22 February 2022**

ORIGINAL EXPIRY DATE : **14 October 2023**

PROJECT STATUS : - The project is 98.565% complete with a negative slippage of
(As of 25 September 2023) 0.575%.


REMARKS: : - Ongoing.

OFFICER-IN-CHARGE : **ALLAN L. BELEN**
(Project Manager)

CONTACT NUMBER **8-527-4435**

EMAIL ADDRESS **allanbelen25@gmail.com**

CONSTRUCTION OF PORT OPERATIONAL AREA PORT OF CALAPAN, CALAPAN, ORIENTAL MINDORO

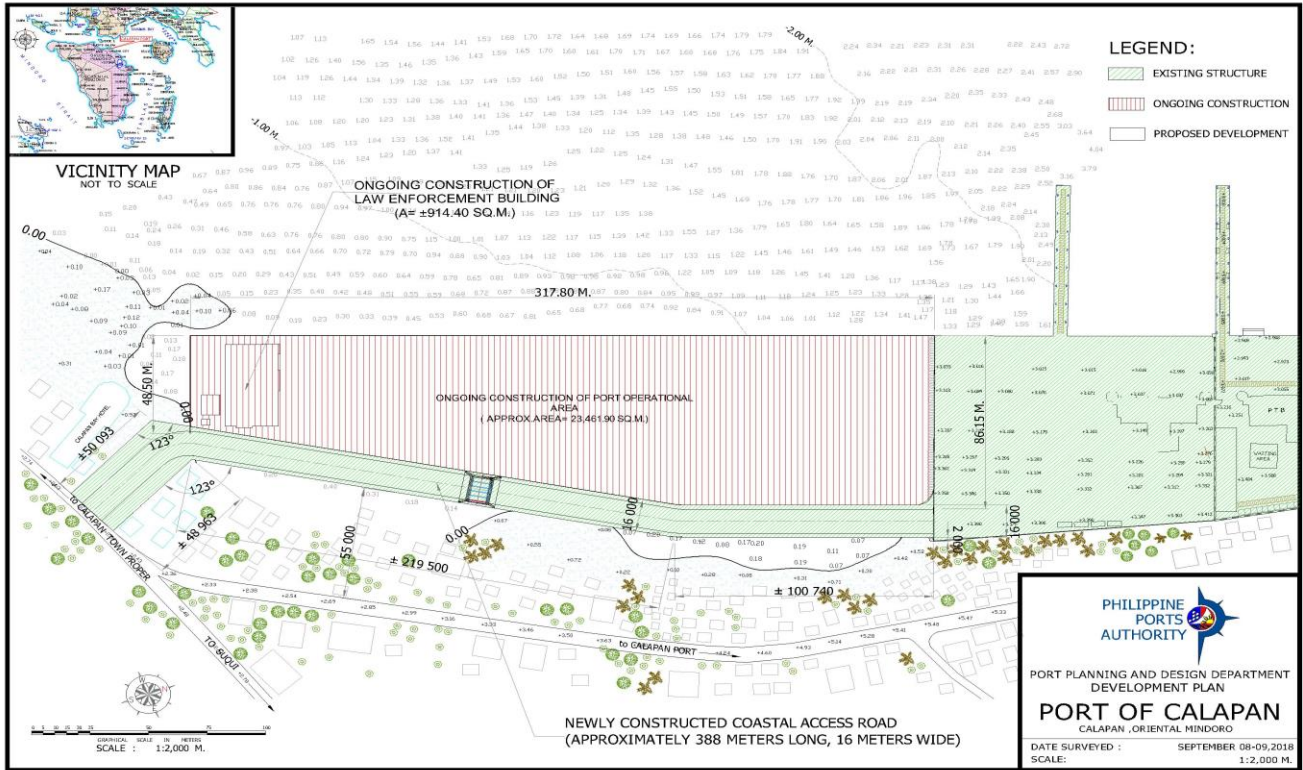

DEVELOPMENT PLAN




ONGOING CONSTRUCTION

PROJECT BRIEF

| | | |
|---|---|---|
| PROJECT TITLE | : | PORT OF CALAPAN IMPROVEMENT PROJECT |
| LOCATION | : | PORT OF CALAPAN, ORIENTAL MINDORO |
| CONTRACTOR | : | D.L. CERVANTES CONSTRUCTION CORPORATION/ ORIENT STAR CONSTRUCTION, INC./JV |
| SCOPE OF WORK | : | A. CONSTRUCTION OF PORT OPERATIONS BUILDING (POB) EXTENSION Area = 3,482.59 sq.m. B. CONSTRUCTION OF PTB ANNEX BUILDING Area = 1,734.47 sq.m. C. CONSTRUCTION OF LAW ENFORCEMENT BUILDING (LEB) Area = 2,769.41 sq.m. D. CONSTRUCTION OF NEW GATE |
| DATE OF BIDDING | : | 02 May 2022 |
| DATE OF AWARD | : | 26 May 2022 |
| DATE OF NOTICE TO PROCEED | : | 06 June 2022 |
| CONTRACT DURATION | : | 720 <i>calendar days</i> |
| APPROVED BUDGET AMOUNT | : | ₱271,956,324.11 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : | PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : | ₱270,994,310.84 |
| EFFECTIVITY DATE | : | 06 June 2022 |
| ORIGINAL EXPIRY DATE | : | 25 May 2024 |
| TIME ADJUSTMENT NO. 1 | : | 330 <i>calendar days</i> Covering the period being affected by the issuance of suspension / resumption orders, from June 2022 to 16 May 2023. |
| REVISED EXPIRY DATE (First Revision) | : | 20 April 2025 |
| PROJECT STATUS (As of 25 September 2023) | : | - The project is 23.674% complete and progressing ahead of 16.436%. |
| REMARKS: | : | - Portion of the project is still partially suspended. |
| OFFICER-IN-CHARGE | : | ALLAN L. BELEN (Project Manager) |
| CONTACT NUMBER | : | 8-527-4435 |
| EMAIL ADDRESS | : | allanbelen25@gmail.com |

PORT OF CALAPAN IMPROVEMENT PROJECT

PORT OF CALAPAN, ORIENTAL MINDORO

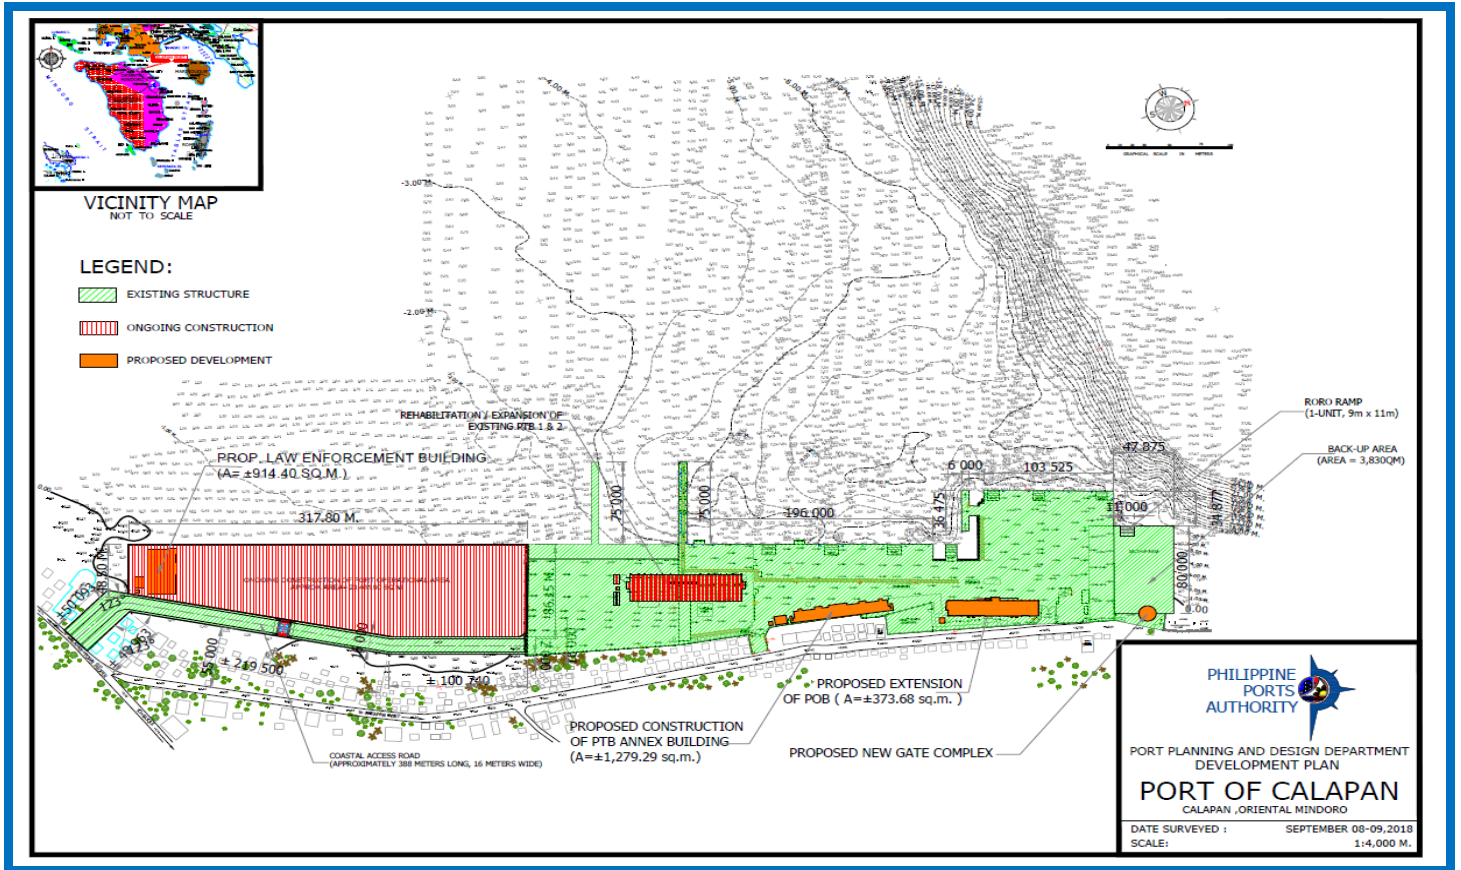

DEVELOPMENT PLAN



ONGOING CONSTRUCTION

PROJECT BRIEF

| | |
|---------------------------|--|
| PROJECT TITLE | : CONSTRUCTION OF PORT OPERATIONAL AREA WITH RORO RAMP |
| LOCATION | : PORT OF TABLAS (POCTOY), ODIONGAN, ROMBLON |
| CONTRACTOR | : MRBII CONSTRUCTION CORPORATION/ MANCOL CONSTRUCTION CORPORATION/JV |
| SCOPE OF WORK | : A. DEMOLITION, EXCAVATION AND REMOVAL WORKS <ol style="list-style-type: none">1. Chipping & disposal of existing R.C. Curb (43 l.m.)2. Demolition & disposal of existing RoRo Ramp & breasting dolphin (207 sq.m.)3. Cutting & disposal of existing piles (24 units)4. Excavation of existing seabed & fill materials (2,668 cu.m.)5. Removal of existing mooring bollard & Rubber Dock Fenders (3 sets)6. Demolition & disposal of existing fence (34 l.m.)7. Removal of existing lamp post (1 unit) B. PORT OPERATIONAL AREA WITH RORO RAMP <ol style="list-style-type: none">1. Supply, delivery & driving of PSC piles & RC corner piles (5,775 l.m.)2. Chipping & cutting of newly driven piles (385 units)3. Supply & placing of 3,500 psi concrete for retaining wall, etc (809 cu.m.)4. Supply & installation of steel reinforcement for retaining wall, etc (82,481 kg.)5. Supply & placing of core rocks & armour rocks (8,377 cu.m.)6. Supply & installation of tie-rod of various sizes (148 sets)7. Supply & placing of fill materials (38,005 cu.m.)8. Construction of PCC Pavement including aggregate base course (7,579 sq.m.)9. Supply & installation of Rubber Dock Fenders (28 sets)10. Supply & installation of mooring bollard (22 sets)11. Construction of Security Fence & Gate (1 lot)12. Supply & installation of Portlighting System (4 sets) |
| DATE OF BIDDING | : 17 January 2022 |
| DATE OF AWARD | : 07 February 2022 |
| DATE OF NOTICE TO PROCEED | : 17 February 2022 |
| CONTRACT DURATION | : 540 calendar days |
| APPROVED BUDGET AMOUNT | : ₱247,980,005.98 |
| SOURCE OF FUNDS | : PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : ₱244,300,886.77 |

VARIATION ORDER NO. 1 : **₱22,827,304.90**
(Change Order No. 1/ Extra Work Order No. 1) - Covering the quantity adjustment (overruns/underruns/deletion) of some of the original items of work and inclusion of additional works as called for by the approved revised plans / drawings which are necessary for the protection, improvement and completion of the project and to suit the actual field condition.

REVISED CONTRACT AMOUNT : **₱267,128,191.67**
(First Revision)

EFFECTIVITY DATE : **18 February 2022**

ORIGINAL EXPIRY DATE : **11 August 2023**

TIME ADJUSTMENT NO. 1 : **72 calendar days**
- Due to Variation Order No. 1

REVISED EXPIRY DATE : **22 October 2023**
(First Revision)

PROJECT STATUS : - The project is 94.983% complete and progressing ahead of 0.996%.
(As of 25 September 2023)


REMARKS: : - Ongoing.

OFFICER-IN-CHARGE : **MELANIE T. NAPIZA**
(Project Manager)

CONTACT NUMBER **8-527-4435**

EMAIL ADDRESS napizam@yahoo.com

CONSTRUCTION OF PORT OPERATIONAL AREA WITH RORO RAMP PORT OF TABLAS (POCTOY), ODIONGAN, ROMBLON

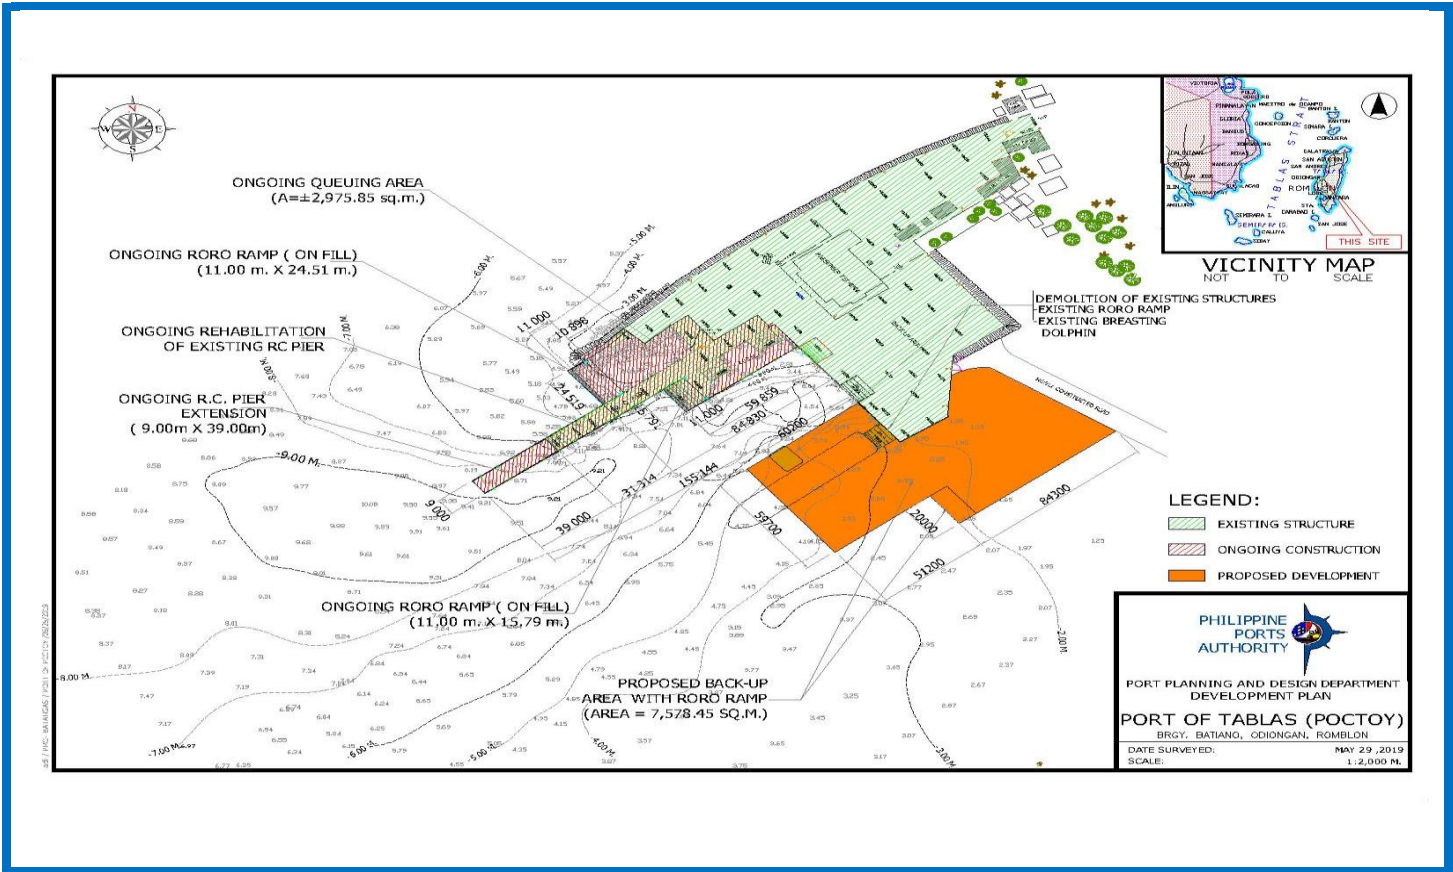

DEVELOPMENT PLAN



ONGOING CONSTRUCTION

PROJECT BRIEF

| | | |
|---------------------------|---|--|
| PROJECT TITLE | : | CONSTRUCTION OF PCG-PPA K-9 ACADEMY |
| LOCATION | : | SITIO BANA, BRGY. DOLORES, CLARK SPECIAL ECONOMIC ZONE, PAMPANGA |
| CONTRACTOR | : | E.U. JINGCO CONSTRUCTION CORPORATION/ BIG J STEEL CONSTRUCTION CORP./ JV |
| SCOPE OF WORK | : | A. CONSTRUCTION OF ADMINISTRATION BUILDING AND OTHER SUPPORT FACILITIES <ol style="list-style-type: none">1. Construction of Administration Building (Area = 448.47 sq.m.)2. Construction of Waste Water Treatment Plant3. Construction of Deep well Water Supply System4. Site Development (Area = 8,746.00 sq.m.) B. CONSTRUCTION OF QUARTERS <ol style="list-style-type: none">1. Construction of Male Quarters (Area = 461.47 sq.m.)2. Construction of Female Quarters (Area = 300.67 sq.m.) C. CONSTRUCTION OF KENNEL FACILITY <ol style="list-style-type: none">1. Construction of Kennel Facility (Area = 775.54 sq.m.) D. CONSTRUCTION OF POWERHOUSE AND PUMP HOUSE <ol style="list-style-type: none">1. Construction of Powerhouse (Area = 41.15 sq.m.)2. Construction of Pumphouse (Area = 18.87 sq.m.) |
| DATE OF BIDDING | : | 15 December 2021 |
| DATE OF AWARD | : | 19 January 2022 |
| DATE OF NOTICE TO PROCEED | : | 11 February 2022 |
| CONTRACT DURATION | : | 420 calendar days |
| APPROVED BUDGET AMOUNT | : | ₱94,796,949.45 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : | PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : | ₱92,886,092.73 |
| EFFECTIVITY DATE | : | 14 February 2022 |
| ORIGINAL EXPIRY DATE | : | 09 April 2023 |
| TIME EXTENSION NO. 1 | : | 55 calendar days Covering the delays encountered due to bad weather conditions for the period 01 May 2022 to 31 October 2022 and the issued Suspension Order from 3 March to 1 April 2022. |
| REVISED EXPIRY DATE | : | 03 June 2023 |

(First Revision)

TIME EXTENSION NO. 2

- : **69 calendar days**
- Covering the delays due to bad weather conditions for the period November 2022 to February 2023 and the delays caused by the late arrival of the required Tubular Steel Columns

REVISED EXPIRY DATE

(Second Revision)

: **11 August 2023**

TIME EXTENSION NO. 3

- : **54 calendar days**
- Covering the delays encountered due to bad weather conditions for the period 01 March 2023 to 31 July 2023

REVISED EXPIRY DATE

(Third Revision)

: **04 October 2023**

PROJECT STATUS

(As of 25 September 2023)

- : - The project is 90.275% complete with a negative slippage of 9.001%.

REMARKS:

- : - On-going.
- Negative slippage of the project was due to delayed delivery of materials and unworkable weather condition.
 - Warning letter was sent to contractor to the contractor to undertake measures to cope with the project's delay
 - Time extension covering the delays encountered due to bad weather condition was approved on 28 September 2023.

OFFICER-IN-CHARGE

: **VICENTE C. ACERIMO**
(Project Manager)

CONTACT NUMBER

8-527-4435

EMAIL ADDRESS

vacerimo@gmail.com

CONSTRUCTION OF PCG-PPA K-9 ACADEMY

SITIO BANA, BRGY. DOLORES, CLARK SPECIAL ECONOMIC ZONE, PAMPANGA



DEVELOPMENT PLAN



ONGOING CONSTRUCTION

PROJECT BRIEF

- PROJECT TITLE** : **CONSTRUCTION OF WHARF AND PORT OPERATIONAL AREA**
- LOCATION** : **PORT OF SAN JUAN, BATANGAS**
- CONTRACTOR** : **GREAT SWISS METAL BUILDERS CORPORATION**
- SCOPE OF WORK** : **A. WHARF AND PORT OPERATIONAL AREA**
1. Chip-off portion of existing RC curb, flushed to deck level and smoothed with mortar (47 l.m.)
 2. Demolition and disposal of existing coping wall (64 l.m.)
 3. Removal of existing mooring bollard (25 Tons, T-head) for re-installation (3 set)
 4. Excavation of existing seabed (3,543 cu.m.)
 5. Supply and drive of 400mm x 400mm PSC piles for floodlight foundation (20 l.m.)
 6. Supply and deliver to site U-type steel sheet piles and corner piles (500mm x 420mm x 10mm thk.) (268 m.t.)
 7. Supply and install cold formed pile shoe (300mm x 16mm thk.) (6002 kg.)
 8. Application of 2-component glass flake external coating for the U-type steel sheet piles (2,463 sq.m.)
 9. Handle, pitch and drive u-type steel sheet piles (3,630 l.m.)
 10. Supply and install Ø25mm dowel bars for steel sheet piles (6,268 kg)
 11. Supply and install steel channel/wale, dowel bars, steel plates, bolts and other accessories/incidentals for steel waling (9,658 kg.)
 12. Supply and place of 3,500 PSI concrete (570 cu.m.)
 13. Supply and install steel reinforcement (46,069 kg.)
 14. Supply and place of 50 to 2,000 kg/pc rocks (8,424 cu.m.)
 15. Supply and install of tie-rods (74 set)
 16. Supply and place of geotextile fabric filter (2,963 sq.m.)
 17. Supply and place of fill materials (17,269 cu.m.)
 18. Supply, place and compact aggregate base course (888 cu.m.)
 19. Excavation of fill materials for lateral drain and catch drain manhole (109 cu.m.)
 20. Supply, place and compact gravel bedding for lateral drain, catch drain manhole, anchor wall, retaining wall and ramp wing wall (35 cu.m.)
 21. Construct Portland Cement Concrete Pavement (300mm thk) including dowel bars and construction joint (4,330 sq.m.)
 22. Construct Portland cement Concrete Pavement for RoRo Ramp including dowel bars and construction joint (108 sq.m.)
 23. Supply and install Rubber Dock Fenders (V500H x 1500L - 21 sets) and mooring bollard, (25-Tons, T-head - 3 sets)
 24. Re-install mooring bollards (T-head type) including provision of new accessories (3 set)

25. Supply and install lateral drainage trench grate cover including angular frame (64 set)
26. Supply and install catch drain manhole trench grate cover including angular frame (1 set)
27. Construct Port Lighting System including all appurtenances (1 lot)

DATE OF BIDDING : **12 May 2022**

DATE OF AWARD : **06 June 2022**

DATE OF NOTICE TO PROCEED : **28 June 2022**

CONTRACT DURATION : **540 calendar days**

APPROVED BUDGET AMOUNT : **₱148,177,023.91**

SOURCE OF FUNDS : **PPA CORPORATE BUDGET**

IMPLEMENTING OFFICE : **PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)**

ORIGINAL CONTRACT AMOUNT : **₱145,988,000.27**

EFFECTIVITY DATE : **28 June 2022**

ORIGINAL EXPIRY DATE : **19 December 2023**

PROJECT STATUS : - The project is 82.365% complete with a negative slippage of 7.366%
(As of 25 August 2023)


REMARKS: : - Ongoing.
- Negative slippage of the project was due to unworkable weather condition.

OFFICER-IN-CHARGE : - **ALLAN L. BELEN**
(Project Manager)

CONTACT NUMBER : **8-527-4435**

EMAIL ADDRESS : allanbelen25@gmail.com

CONSTRUCTION OF WHARF AND PORT OPERATIONAL AREA PORT OF SAN JUAN, BATANGAS

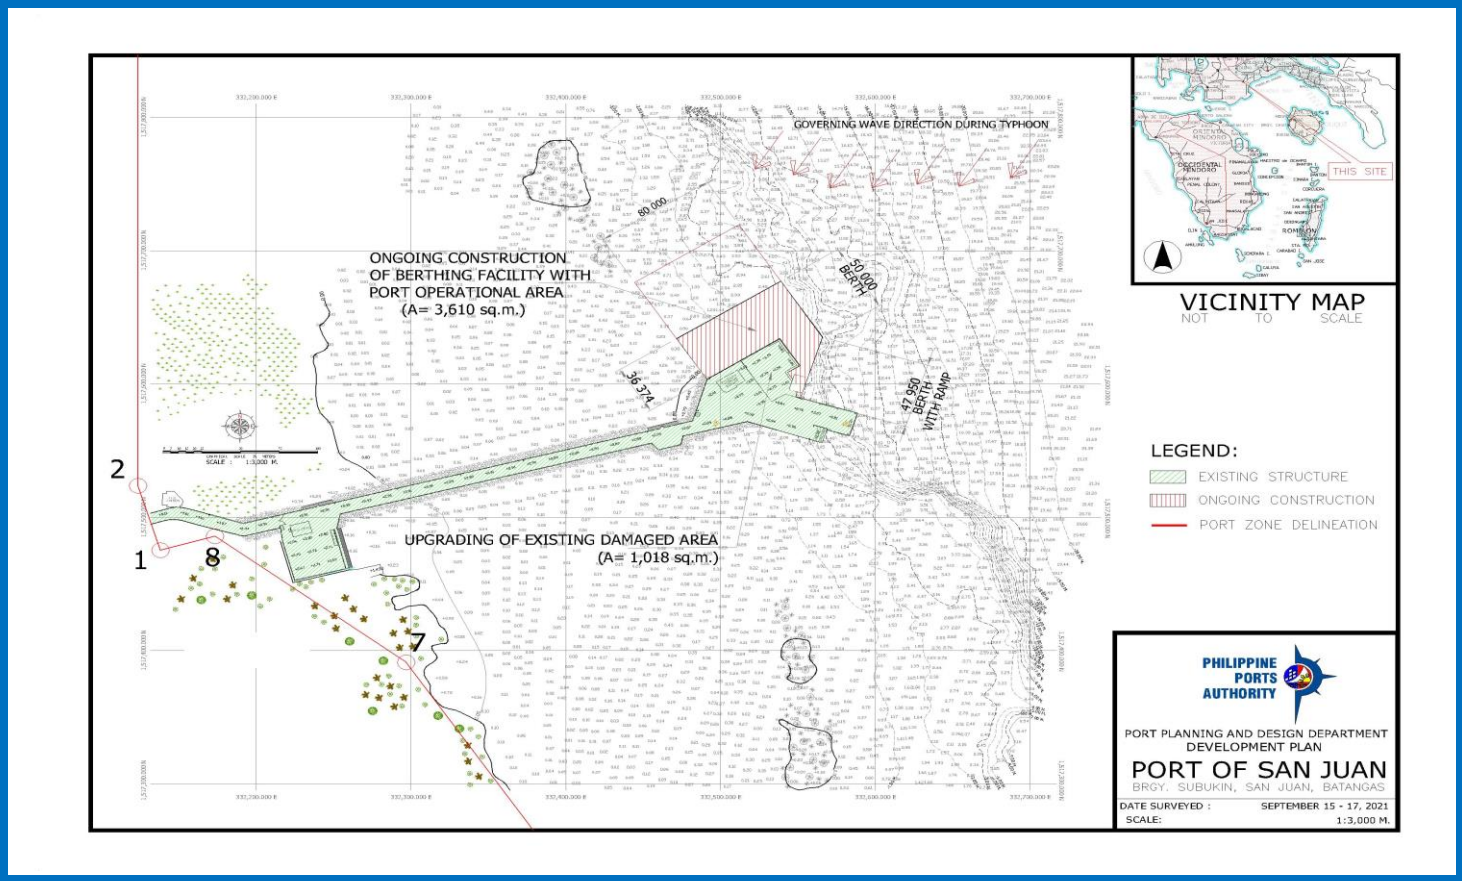

DEVELOPMENT PLAN



ONGOING CONSTRUCTION

PROJECT BRIEF

| | | |
|---------------------------|---|--|
| PROJECT TITLE | : | CONSTRUCTION OF TWO-STOREY TMO BUILDING |
| LOCATION | : | PORT OF BAUAN, BATANGAS |
| CONTRACTOR | : | W. RIVERA CONST. AND EQUIPT. RENTALS, INC. |
| SCOPE OF WORK | : | A. CONSTRUCTION OF TMO BUILDING <ol style="list-style-type: none">1. Supply, driving & chipping of 400 x 400mm PSC foundation piles2. Construction of 2-storey TMO building, complete with architectural finishes, electro/mechanical, water/sewerage system, painting, etc. (467.87 sq.m.)3. Supply, delivery & installation of distribution transformer & accessories4. Supply & installation of solar panel & accessories |
| DATE OF BIDDING | : | 11 September 2023 |
| DATE OF AWARD | : | 20 September 2023 |
| DATE OF NOTICE TO PROCEED | : | 02 October 2023 |
| CONTRACT DURATION | : | 300 calendar days |
| APPROVED BUDGET AMOUNT | : | ₱30,381,626.54 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : | PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : | ₱29,582,463.63 |
| EFFECTIVITY DATE | : | 02 October 2023 |
| ORIGINAL EXPIRY DATE | : | 27 July 2024 |
| PROJECT STATUS | : | |
| (As of 25 September 2023) | | |
| REMARKS: | : | |
| OFFICER-IN-CHARGE | : | |
| CONTACT NUMBER | : | |
| EMAIL ADDRESS | : | |

PROJECT BRIEF

- PROJECT TITLE** : **BALOGO PORT DEVELOPMENT PROJECT**
- LOCATION** : **PORT OF BALOGO, PASACAO, CAMARINES SUR**
- CONTRACTOR** : **KHAN KON CHI CONSTRUCTION AND DEVELOPMENT CORP./ SB CONSTRUCTION CORPORATION/JV**
- SCOPE OF WORK** :
- A. CONSTRUCTION OF PORT OPERATIONAL AREA AND ACCESS ROAD AREA = 5,150.00 SQ.M.**
 1. Supply and driving of steel sheet piles (102 m.t. equivalent to 1,320 l.m.), including cutting up to cut-off elevation (132 pcs)
 2. Supply and installation of steel channel wale (8,232 kg), tie-rod (33 sets - 60mmØ x 12m), geotextile fabric (3,467 sq.m.)
 3. Construction of rock bulkhead (4,564 cu.m.), including fill materials (19,666 cu.m.), reinforced concrete for retaining wall, anchor block, RC curb, CHB column and lamp post foundation (777 cu.m. of concrete and 61,917 kg of reinforcing steel bars of various sizes) and excavation of existing seabed prior to laying of rocks (1,389 cu.m.)
 4. Construction of CHB wall fence (313 sq.m.), including plastering with painting (731 sq.m.), and installation of various materials for cyclone wire mesh (392 sq.m.)
 5. Construction Portland Cement Concrete Pavement (300mm thk. - 5,150 sq.m.), including aggregate base course (1,030 cu.m.)
 6. Construction of catch drain manhole (10 sets), including reinforced concrete pipe 610mmØ - 136 l.m.), including gravel bedding (155 cu.m.)
 7. Supply and install 10m, ht. steel tapered lamp post (13 sets), with 120 watt LED lamp integrated solar street light (13 pcs) for lighting system
 - B. CONSTRUCTION OF ACCESS TRESTLE ON PILES (Area = 1,080.00 sq.m.)**
 1. Supply and drive A252 Grade 2, 500mmØ x 13mm thk. Steel Pipe Piles (426 m.t. equivalent to 2,724 l.m.), including application of polyurethane external coating (1,637 sq.m.), supply and place concrete filler (221 cu.m.), installation of reinforcing steel cage bar (352,437 kg of various sizes), extraction of clogged materials (97 cu.m), cutting of piles up to cut-off elevation and installation of reinforcing band tip (106 sets)
 2. Supply and place 3,500 PSI concrete (714 cu.m.) and reinforcing steel bars (119,797 kg of various sizes for superstructure, including construction joint (36 l.m.)
 3. Supply and installation of Rubber Dock Fender (V-400H x 200L - 4 sets) including accessories.

**C. CONSTRUCTION OF RC WHARF
(Area = 2,385.00 sq.m.)**

1. Supply and drive A252 Grade 2, 700mmØ x 13mm thk. Steel Pipe Piles (1,728 m.t. equivalent to 7,844 l.m.), including application of polyurethane external coating (8,585 sq.m.), supply and place concrete filler (1,588 cu.m.), installation of reinforcing steel cage bar (352,437 kg of various sizes), extraction of clogged materials (651 cu.m.) splicing, cutting of piles up to cut-off elevation and installation of reinforcing band tip (212 sets)
2. Supply and place 3,500 PSI concrete (1,585 cu.m.) and reinforcing steel bars (240,511 kg of various sizes of superstructure, including construction joint (57 l.m.)
3. Supply and installation of Rubber Dock Fender (V-400H x 2000L - 26 sets and Hyper Omega Fender, HOM-1000H x 100 - 14 sets) including accessories
4. Supply and installation of mooring bollard (100T, T-head - 14 sets and 50T, T-head - 12 sets) including accessories

| | |
|--|--|
| DATE OF BIDDING | : 02 June 2023 |
| DATE OF AWARD | : 04 July 2023 |
| DATE OF NOTICE TO PROCEED | : 26 July 2023 |
| CONTRACT DURATION | : 660 calendar days |
| APPROVED BUDGET AMOUNT | : ₱629,123,914.25 |
| SOURCE OF FUNDS | : PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : ₱627,596,517.01 |
| EFFECTIVITY DATE | : 26 July 2023 |
| ORIGINAL EXPIRY DATE | : 15 May 2025 |
| PROJECT STATUS (As of 25 September 2023) | : The project is 28.368% complete and progressing ahead of 23.139%. |
| REMARKS | : Ongoing. |
| OFFICER-IN-CHARGE | : EMIL JOSE GARCIA (Project Manager) |
| CONTACT NUMBER | : 8-527-4435 |
| EMAIL ADDRESS | : |

PROJECT BRIEF

- PROJECT TITLE** : **CAPINPIN PORT EXPANSION PROJECT**
- LOCATION** : **PORT OF CAPINPIN, ORION, BATAAN**
- CONTRACTOR** : **GOLDRIDGE CONSTRUCTION & DEV'T. CORP.**
- SCOPE OF WORK** :
- A. R.C. TRESTLE (9.00m x 252.00m)**
 1. Removal, disposal and excavation works
 2. Supply & delivery of PSC square piles
 3. Handling, pitching & driving of PSC square piles
 4. Chipping/cutting & disposal of newly driven PSC square piles
 5. Supply & installation of reinforcing steel bars for the superstructure
 6. Supply & placing concrete for the superstructure
 7. Supply & installation of construction joint
 8. Supply & installation of Rubber Fenders and mooring bollards
 9. Portlighting System
 - B. R.C. WHARF (211.00m x 15.00m)**
 1. Supply & delivery of Steel Pipe Piles
 2. Handling, pitching & driving of Steel Pipe Piles
 3. Supply, fabricate band tip for the Steel Pipe Piles
 4. Cutting & disposal of newly driven Steel Pipe Piles
 5. Extraction of clogged materials inside the SPP
 6. Supply & placing of concrete filler for SPP
 7. Supply & installation of reinforcing steel cage for SPP
 8. Supply & installation of reinforcing steel bars for the superstructure
 9. Supply & placing of concrete for the superstructure
 10. Supply & installation of construction joints
 11. Supply & installation of Rubber Fenders and mooring bollards
 - C. R.C. BREAKWATER PIER (6.00m x 240.00m)**
 1. Excavation of existing seabed
 2. Supply & delivery of PSC square piles
 3. Handling, pitching & driving of PSC sheet piles & corner piles
 4. Chipping/cutting & disposal of newly driven PSC sheet piles
 5. Supply & installation of reinforcing steel bars for the superstructure
 6. Supply & placing of concrete for the superstructure
 7. Supply & placing of rock boulders
 8. Construct concrete pavement
- DATE OF BIDDING** : **01 June 2023**
- DATE OF AWARD** : **04 July 2023**
- DATE OF NOTICE TO PROCEED** : **26 July 2023**
- CONTRACT DURATION** : **750 calendar days**

APPROVED BUDGET AMOUNT : **₱820,170,498.72**

SOURCE OF FUNDS : **PPA CORPORATE BUDGET**

IMPLEMENTING OFFICE : **PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)**

ORIGINAL CONTRACT AMOUNT : **₱818,588,478.00**

EFFECTIVITY DATE : **31 July 2023**

ORIGINAL EXPIRY DATE : **18 August 2025**

PROJECT STATUS : - The project is 11.136% completed and progressing ahead of
(As of 25 September 2023) 6.448%.

REMARKS : - Ongoing.

OFFICER-IN-CHARGE : **ARLINA G. MAGPALE**
(Project Manager)

CONTACT NUMBER : **8-527-4435**

EMAIL ADDRESS : **agmagpale@gmail.com.ph**

PROJECT BRIEF

- PROJECT TITLE** : **CURRIMAO PORT EXPANSION AND RESTORATION PROJECT**
- LOCATION** : **PORT OF CURRIMAO, CURRIMAO, ILOCOS NORTE**
- CONTRACTOR** : **MRBII CONSTRUCTION CORPORATION/ KXBG CONSTRUCTION & DEVELOPMNET CORPORATION/JV**
- SCOPE OF WORK** : **A. EXPANSION AND IMPROVEMENT OF PORT OPERATIONAL AREA (AREA = 30,850.38 SQ.M)**
1. Removal and disposal or turn-over of various items affected by the project, namely; retaining wall (84 cu.m.), mooring bollard (2 sets), CHB fence (525 sq.m.), RC curb (4 l.m.), interlocking concrete block pavement (372 sq.m.) and concrete pavement (233 s
 2. Remove and re-install existing, electrical high mast tower including provisions of new accessories (bolts, nuts, washers, etc.) - 2 sets
 3. Cutting of existing concrete piles up to elevation mean lower water (MLLW) including disposal of debris (76 sets)
 4. Excavate existing seabed up to required elevation prior to laying of rock materials (2,664 cu.m.)
 5. Supply and drive of concrete piles (0.35m x 0.525m x 19m PSC sheet piles - 2,869 l.m., RC corner sheet piles - 76 l.m. and 0.45m x 0.45m x 18 PSC piles - 54 l.m.), including chipping and cutting of newly driven piles up to required elevation (158 pcs)
 6. Construction of rock bulkhead (26,707 cu.m.) including geotextile fabric (9,198 sq.m.), fill materials (156,029 cu.m.), reinforced concrete for retaining walls, wing wall, RC curb, anchor wall, floodlight foundation, lamp post foundation, CHB fence column
 7. Construction of interlocking concrete block pavement (1,160 sq.m.) and PCCP (300mm thk. - 30,233 sq.m.), including aggregate base course (6,267 cu.m.), cement treated base course (174 cu.m.), sand cushion (58 cu.m.) and concrete edging (120 sq.m.)
 8. Construction of catch drain manhole (40 sets) and reinforced concrete pipe of various sizes (610mm-304 l.m., 760mm-142 l.m.), including gravel bedding (204 cu.m.) and excavation/backfilling works (1,112 cu.m.)
 9. Construction of CHb wall fence (1,238 sq.m.), including plastering and painting (2,995 sq.m.) and installation of various materials for cyclone wire mesh (1,685 sq.m.)
 10. Supply and installation of Rubber Dock Fender (V-500H x 1500L-5 sets) including accessories
 11. Supply and installation of mooring bollard (35T, T-head - 2 sets) including accessories
 12. Supply and installation of tie-rod (60mmØ x 18m - 40 pcs) including accessories
 13. Supply and installation of various materials for port lighting (1 lot)

**B. RECONSTRUCTION OF EXISTING RC PIER
(AREA = 4,693.84 SQ.M.)**

1. Removal and disposal or turn-over of various items affected by the project, namely; RC deck (4,324 cu.m.), breasting dolphins (18 sets), existing fender (40 sets), existing bollard and cleat (40 sets) and existing lamp post (3 sets)
2. Cutting of existing concrete piles up to seabed elevation including disposal of debris (739 pcs)
3. Supply and drive 450mm x 450mm PSC piles (18,808 l.m.), including chipping/cutting to required elevation (684 pcs)
4. Supply and place 3,500 PSI concrete (2,555 cu.m.) and reinforcing steel bars (391,825 kg of various sizes) for superstructure, including construction joint 1 and 2 (90 l.m. and 18 l.m., respectively)
5. Supply and installation of Rubber Dock Fender (V-500H x 2500L - 86 sets) including accessories
6. Supply and installation of mooring bollard (50T, T-head - 44 sets) including accessories

C. WIDENING OF ACCESS TRESTLE (AREA = 889.87 SQ.M.)


1. Supply and drive 450mm x 450mm PSC piles (3,913 l.m.), including chipping/cutting to required elevation (148 pcs)
2. Supply and place 3,500 PSI concrete (414 cu.m.) and reinforcing steel bars (69,901 kg of various sizes) for superstructure, including construction joint 1 and 2 (27 l.m. and 107 l.m., respectively)

| | |
|--|--|
| DATE OF BIDDING | : 12 July 2023 |
| DATE OF AWARD | : 02 August 2023 |
| DATE OF NOTICE TO PROCEED | : 06 September 2023 |
| CONTRACT DURATION | : 840 calendar days |
| APPROVED BUDGET AMOUNT | : ₱906,832,815.57 |
| SOURCE OF FUNDS | : PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : ₱886,698,449.52 |
| EFFECTIVITY DATE | : 06 September 2023 |
| ORIGINAL EXPIRY DATE | : 23 December 2025 |
| PROJECT STATUS (As of 25 September 2023) | : - The project is 26.676% complete and progressing ahead of 26.331%. |
| REMARKS | : - Ongoing. |
| OFFICER-IN-CHARGE | : |
| CONTACT NUMBER | : |
| EMAIL ADDRESS | : |


PROJECT BRIEF

| | |
|----------------------------------|---|
| PROJECT TITLE | : LUBANG PORT EXPANSION AND IMPROVEMENT PROJECT |
| LOCATION | : PORT OF LUBANG, BRGY. TILIK, LUBANG, OCCIDENTAL MINDORO |
| CONTRACTOR | : D.K. JOCSON CONSTRUCTION/ADVANCE TECH CONSTRUCTION AND TRADING CORP. /JV |
| SCOPE OF WORK | : A. PORT OPERATIONAL AREA <ol style="list-style-type: none">1. Excavation of existing sea bed (1,016 cu.m.)2. Demolition of existing CHB fence and turn over to PPA existing gate (33 l.m.)3. Remove existing solar powered lamp post and turn over to PPA (3 no.)4. Supply and place 3,500 PSI concrete (203 cu.m.)5. Supply and installation of steel reinforcement (16,823 kg.)6. Supply and place of 1000 kg armour rocks (1,097 cu.m.)7. Supply and place of 50-100 kg core rocks (1,533 cu.m.)8. Supply and installation of geotextile fabric (571 sq.m.)9. Supply, spread and compact fill materials (3,284 cu.m.)10. Supply and place gravel bedding (10 cu.m.)11. Construction of shear keys including steel reinforcement (127 sq.m.)12. Construction of PCCP including aggregate base course (92 sq.m.)13. Supply, deliver & install ICBP incl. 10% CTB and leveling sand (1,220 sq.m.)14. Construction of CHB fence with concrete baluster (75 l.m.)15. Supply, deliver and install electrical works and its accessories (1 lot) B. R.C. WHARF WITH RORO RAMP ON FILL <ol style="list-style-type: none">1. Supply, deliver and drive 450mm x 450mm PSC test piles (2 no.)2. Supply and drive 450mm x 450mm PSC piles (2,155 l.m.)3. Supply and place 3,500 PSI concrete for the superstructure (218 cu.m.)4. Supply and installation of steel reinforced for the superstructure (51,210 kg.)5. Supply and installation of construction joint (84 l.m.)6. Supply and installation of mooring bollard (35T) (3 set)7. Supply and installation of RDF (V400H x 1500L) (9 set) |
| DATE OF BIDDING | : 29 August 2023 |
| DATE OF AWARD | : 12 September 2023 |
| DATE OF NOTICE TO PROCEED | : 06 October 2023 |
| CONTRACT DURATION | : 360 calendar days |
| APPROVED BUDGET AMOUNT | : ₱74,214,949.61 |
| SOURCE OF FUNDS | : PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : ₱73,188,888.88 |
| EFFECTIVITY DATE | : 09 October 2023 |
| ORIGINAL EXPIRY DATE | : 02 October 2024 |
| PROJECT STATUS | : |
| (As of 25 September 2023) | |
| REMARKS | : |

LUBANG PORT EXPANSION AND IMPROVEMENT PROJECT PORT OF LUBANG, BRGY. TILIK, LUBANG, OCCIDENTAL MINDORO

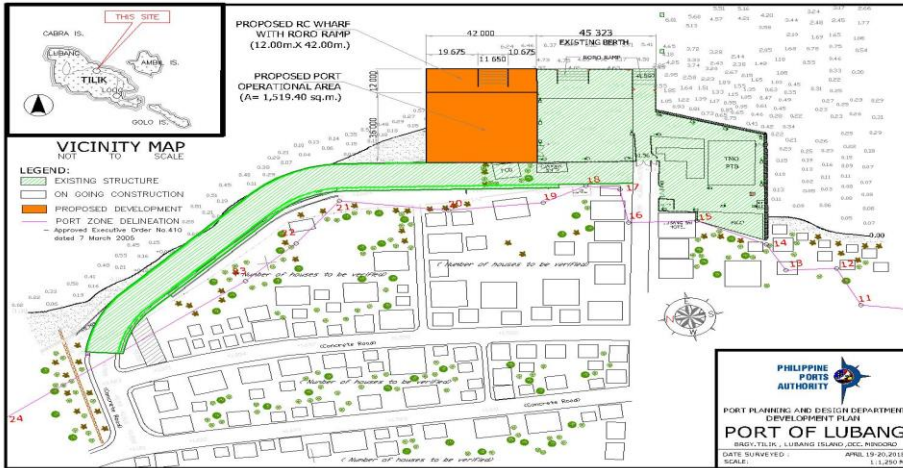

DEVELOPMENT PLAN



AFTER CONSTRUCTION

PROJECT BRIEF

PROJECT TITLE : **MAUBAN PORT IMPROVEMENT PROJECT**

LOCATION : **PORT OF MAUBAN, MAUBAN, QUEZON**

CONTRACTOR : **J.C. PINON CONSTRUCTION INC.**

SCOPE OF WORK : **A. PORT OPERATIONAL AREA & ACCESS ROAD**

1. Chipping & disposal of existing RC curb (234 l.m.)
2. Removal & disposal of existing concrete pavement (20 sq.m.)
3. Excavation and backfilling works (8 cu.m.)
4. Removal of existing mooring and fenders (13 sets)
5. Supply & driving of PSC anchor piles (999 l.m.)
6. Supply & driving of PSC shete piles & R.C corner piles (4,023 l.m.)
7. Supply & placing of 3,500 PSI concrete (677 cu.m.)
8. Supply & installation of reinforcing steel bars (55,064 kg.)
9. Supply & placing of gravel bedding (4 cu.m.)
10. Supply & placing of 50 to 3,000 kg. Rocks (19,537 cu.m.)
11. Supply & installation of concrete blocks of various sizes (15 sets)
12. Supply & installation of tie-rod (38 sets)
13. Supply & placing of fill materials (28,514 cu.m.)
14. Supply & placing of sub-base/base course (10,350 cu.m.)
15. Construction of Portland Cement Concrete Pavement (9,121 sq.m.)
16. Drainage system (139 l.m.)
17. Portlighting system (1 lot)
18. Supply & installation of mooring cleats (8 sets)
19. Construction of cyclone wire fence (1 lot)

DATE OF BIDDING : **12 July 2023**

DATE OF AWARD : **02 August 2023**

DATE OF NOTICE TO PROCEED : **04 September 2023**

CONTRACT DURATION : **450 calendar days**

APPROVED BUDGET AMOUNT : **₱277,419,881.74**

SOURCE OF FUNDS : **PPA CORPORATE BUDGET**

IMPLEMENTING OFFICE : **PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD)**

ORIGINAL CONTRACT AMOUNT : **₱275,155,175.53**

EFFECTIVITY DATE : **05 September 2023**

ORIGINAL EXPIRY DATE : **27 November 2024**

PROJECT STATUS : - Mobilization and sourcing of materials on-going.
(As of 25 September 2023)

REMARKS :

OFFICER-IN-CHARGE :

CONTACT NUMBER :

EMAIL ADDRESS :

PROJECT BRIEF

- PROJECT TITLE** : **CONSTRUCTION OF PORT OPERATIONAL AREA**
- LOCATION** : **PORT OF SAN AGUSTIN, SAN AGUSTIN, TABLAS ISLAND, ROMBLON**
- CONTRACTOR** : **D.K. JOCSON CONSTRUCTION/ S2A BUILDERS CORPORATION /JV**
- SCOPE OF WORK** : **A. DEMOLITION, REMOVAL AND EXCAVATION WORKS**
1. Cut existing trees affected by the constructions works (3 no.)
 2. remove and turn-over to PPA existing lamp post (3 no.)
 3. Demolish and dispose existing pavement (92 sq.m.)
 4. Scrape existing fill materials (62 cu.m.)
 5. Remove and dispose portion of existing revetment/curb (54 cu.m.)
 6. Excavation of existing fill materials for gate and fence (23 cu.m.)
 7. Excavation of existing seabed up to required elevation prior to placing of rocks (1,217 cu.m.)
- B. PORT OPERATIONAL AREA**
1. Supply, deliver and drive 350mm x 600mm PSC sheet piles and RC corner piles (1,224 l.m.)
 2. Supply and placing of 3,500 PSI concrete (271 cu.m.)
 3. Supply and installation of steel reinforcement (24,969 kg.)
 4. Supply and place 3,000 PSI pre-cast concrete blocks (3 set)
 5. Supply and place 3,000 PSI pre-cast concrete blocks (3 set)
 6. Supply and placing of 50 to 1,000 kg/pc rocks (3,808 cu.m.)
 7. Supply and installation of tie-rods (24 sets)
 8. Supply and placing of geotextile fabric filler (1,418 sq.m.)
 9. Supply and placing of fill materials (7,054 cu.m.)
 10. Supply, place and compact gravel bedding (2 cu.m.)
 11. Construct Portland cement Concrete Pavement, 300mm thk. (2,155 sq.m.)
 12. Construct catch drain manhole including installation of hot-dipped galv. Angle bar 200mm x 200mm x 9mm (3 set)
 13. Supply and install reinforced concrete pipe culvert (RCP) Ø 600mm (38 l.m.)
 14. Construct security fence on CHB with cyclone wire and barbed wire (85 l.m.)
 15. Supply, fabricate and install steel gate and including accessories (1 lot)
 16. Supply, fabricate and install PPA logo including accessories (1 lot)
 17. Supply and install 4mm thk. Aluminum composite panel (18 sq.m.)
 18. Construct Port Lighting System including appurtenances (1 lot)
 19. Supply, deliver and install mooring cleat including accessories (4 set)
- DATE OF BIDDING** :

DATE OF AWARD : 03 October 2023

DATE OF NOTICE TO PROCEED :

CONTRACT DURATION : *360 calendar days*

APPROVED BUDGET AMOUNT : ***₱75,864,320.97***

SOURCE OF FUNDS :

IMPLEMENTING OFFICE :

ORIGINAL CONTRACT AMOUNT : ***₱75,352,777.77***

EFFECTIVITY DATE :

ORIGINAL EXPIRY DATE :

PROJECT STATUS :

(As of 25 September 2023)

REMARKS : - Bidding was conducted on 13 September 2023.
- For post qualification of the lowest bidder.

OFFICER-IN-CHARGE :

CONTACT NUMBER :

EMAIL ADDRESS :

PROJECT BRIEF

| | | |
|----------------------------------|----------|---|
| PROJECT TITLE | : | LOOC PORT (MALBOG) IMPROVEMENT PROJECT |
| LOCATION | : | PORT OF LOOC, BRGY. MALBOG, LOOC, ROMBLON |
| CONTRACTOR | : | VESA ENGINEERING AND CONSTRUCTION/ S2A BUILDERS CORPORATION/JV |
| SCOPE OF WORK | : | A. PASSENGER TERMINAL BUILDING, GUARDHOUSE, FENCE AND GATE <ol style="list-style-type: none">1. Removal, disposal and excavation/backfilling works2. Construction of 1-storey Passenger Terminal Building, complete with architectural finishes, electro/mechanical, water/sewerage system, painting, etc. (439.44 sq.m., 50 pax)3. Supply, delivery & installation of distribution transformer & accessories4. Portlighting System5. Construction of security fence6. Supply & installation of solar panel & accessories |
| DATE OF BIDDING | : | |
| DATE OF AWARD | : | 20 September 2023 |
| DATE OF NOTICE TO PROCEED | : | |
| CONTRACT DURATION | : | 300 calendar days |
| APPROVED BUDGET AMOUNT | : | ₱35,784,363.43 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : | PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : | ₱35,405,565.01 |
| EFFECTIVITY DATE | : | |
| ORIGINAL EXPIRY DATE | : | |
| PROJECT STATUS | : | <ul style="list-style-type: none">- Bidding was conducted on 30 August 2023.- Notice of Award was issued to the contractor on 20 September 2023. |
| REMARKS | : | |
| OFFICER-IN-CHARGE | : | |
| CONTACT NUMBER | : | |
| EMAIL ADDRESS | : | |

PROJECT BRIEF

| | | |
|----------------------------------|----------|--|
| PROJECT TITLE | : | SALOMAGUE PORT EXPANSION PROJECT |
| LOCATION | : | PORT OF SALOMAGUE, BRGY. SALOMAGUE, CABUGAO, ILOCOS SUR |
| CONTRACTOR | : | |
| SCOPE OF WORK | : | A. CONSTRUCTION OF PORT OPERATIONAL AREA (AREA = 14,149.56 SQ.M.) <ol style="list-style-type: none">1. Removal and disposal or turn-over of various items affected by the project, namely; coping wall (65 cu.m.), mooring bollard (14 sets), mooring fender (28 sets), CHB fence2. Cutting of existing concrete piles up to elevation mean lower low water (MLLW) including disposal of debris (140 sets)3. Excavate existing seabed up to required elevation prior to laying of rock materials (6,403 cu.m.)4. Supply and drive of concrete piles (0.35m x 0.525m x 21m PSC sheet piles - 12,705 l.m., RC corner sheet piles - 105 l.m. and 0.45 m x 0.45m x 21m PSC anchor piles - 1,575 l.m.)5. Construction of rock bulkhead (11,099 cu.m.), including geotextile fabric (6,713 sq.m.), fill materials (73,411 cu.m.) reinforced concrete for retaining wall, wing wall, RC curb, anchor wall, anchor pile block, anchor block, tie-beam, lamp post, RC ditch, lamp post, ductbank, pedestal post and mooring block (1,073 cu.m. and 125,376 kg of reinforcing steel bars of various sizes)6. Construction of interlocking concrete block pavement (3,006 sq.m.) and PCCP (300mm thk.-10,769 sq.m.), including aggregate base course (2,647 cu.m.), cement treated base course (457 cu.m.), sand cushion (152 cu.m.) and concrete edging (110 sq.m.)7. Constructoin of catch drain manhole (10 sets) and reinforced concrete pipe (610mm-126 l.m.), including gravel bedding (25 cu.m.) and excavation/backfilling works (1,382 cu.m.)8. Supply and installation of Rubber Dock Fender (V-500H x 1500L - 30 sets) including accessories9. Supply and installation of mooring bollard (35T, T-head - 10 sets) including accessories10. Supply and installation of tie-rod of various sizes (60mmØ x 14m - 98 pcs, 60mmØ x 2.0m, 32mmØ 15.00m) including accessories11. Supply and installation of various materials for Port Lighting (1 lot) |
| DATE OF BIDDING | : | |
| DATE OF AWARD | : | |
| DATE OF NOTICE TO PROCEED | : | |
| CONTRACT DURATION | : | 600 calendar days |

APPROVED BUDGET AMOUNT : ***₱428,117,962.04***

SOURCE OF FUNDS :

IMPLEMENTING OFFICE :

ORIGINAL CONTRACT AMOUNT :

EFFECTIVITY DATE :

ORIGINAL EXPIRY DATE :

PROJECT STATUS :

REMARKS : - Bidding on 23 August 2023 was postponed.
- Bidding to be re-scheduled.

OFFICER-IN-CHARGE :

CONTACT NUMBER :

EMAIL ADDRESS :

PROJECT BRIEF

| | | |
|----------------------------------|----------|--|
| PROJECT TITLE | : | ROMBLON PORT EXPANSION PROJECT |
| LOCATION | : | PORT OF ROMBLON, ROMBLON |
| CONTRACTOR | : | MRBII CONSTRUCTION CORPORATION |
| SCOPE OF WORK | : | A. EXCAVATION AND REMOVAL WORKS <ol style="list-style-type: none">1. Removal & disposal of existing RC curb (127 l.m.)2. Chipping of existing mooring bollard base (8 no.)3. Removal & turn-over existing mooring bollard (6 set)4. Removal & turn-over existing mooring bitt (2 set)5. Removal & turn-over existing Rubber Dock Fender (17 set)6. Removal & turn-over existing lamp post (1 set)7. Removal & restoration of existing concrete pavement (33 sq.m.)8. Excavation and backfilling works (16 cu.m.) B. CONSTRUCTION OF RC WHARF <ol style="list-style-type: none">1. Supply & driving of PSC test pile (2 units)2. Supply & driving of PSC square pile (8,194 l.m.)3. Supply & placing of 3,500 PSI concrete (929 cu.m.)4. Supply & installation of reinforcing steel bar (162,064 kg)5. Supply & installation of construction joints (157 l.m.)6. Supply & install of Rubber Dock Fender (16 sets)7. Supply & installation of mooring bollards (8 sets)8. Construction of cyclone wire fence (27 l.m.)9. Reinstallation of the newly removed solar lamp post (1 set)10. Portlighting System (1 lot) |
| DATE OF BIDDING | : | 31 August 2023 |
| DATE OF AWARD | : | 12 September 2023 |
| DATE OF NOTICE TO PROCEED | : | 27 September 2023 |
| CONTRACT DURATION | : | 360 calendar days |
| APPROVED BUDGET AMOUNT | : | ₱167,628,028.96 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : | PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : | ₱166,124,479.61 |
| EFFECTIVITY DATE | : | 29 September 2023 |
| ORIGINAL EXPIRY DATE | : | 22 September 2024 |
| PROJECT STATUS | : | |
| (As of 25 September 2023) | | |
| REMARKS | : | <ul style="list-style-type: none">- Bidding was conducted on 25 August 2023.- Notice of Award was issued to the contractor on 12 September 2023. |
| OFFICER-IN-CHARGE | : | |
| CONTACT NUMBER | : | |
| EMAIL ADDRESS | : | |

PROJECT BRIEF

| | | |
|----------------------------------|----------|---|
| PROJECT TITLE | : | SAN ANDRES PORT IMPROVEMENT AND EXPANSION PROJECT |
| LOCATION | : | PORT OF SAN ANDRES, CATANDUANES |
| CONTRACTOR | : | BEMKAR CONSTRUCTION AND SUPPLY |
| SCOPE OF WORK | : | A. DEMOLITION & REMOVAL WORKS <ol style="list-style-type: none">Demolish and dispose existing structure (RoRo Ramp) for build up (77 sq.m.)Chip-off portion of existing RC curb (34 l.m.)Chip-off portion of existing mooring block to be aligned to pier (15 cu.m.)Removed and turn over to PPA existing mooring bits, mooring cleats and Rubber Dock Fenders affected by demolition (12 no.)Chip-off existing concrete piles for build-up (12 no.) B. RC PLATFORM, RORO RAMP AND RC PIER <ol style="list-style-type: none">Supply and drive A252 Grade 2, 500mm Ø Steel Pipe Piles test pile, 3 nos. (15.06 m.t. - 132 l.m.) including application of polyurethane external coating (43 sq.m.), installation of reinforcing band tip (3 pcs), splicing (3 pcs)Supply and drive A252 Grade 2, 500mm Ø Steel Pipe Piles test pile, 3 nos. (15.06 m.t. - 132 l.m.) including application of polyurethane external coating (43 sq.m.), installation of reinforcing band tip (3 pcs), splicing (3 pcs)Supply and place 3,500 psi concrete filler (274 cu.m.) and reinforcing steel cage (75,276 kgs of various sizes) for steel pipe piles including extraction of clogged materials (132 pcs)Supply and place 3,500 psi concrete (663 cu.m.) and reinforcing steel bars (109,182 kg of various sizes) for superstructureSupply and install Rubber Dock Fenders (V500 x 1500L - 16 sets) and mooring bollard, (35 - Tons, T-head - 8 sets) |
| DATE OF BIDDING | : | 14 September 2023 |
| DATE OF AWARD | : | 03 October 2023 |
| DATE OF NOTICE TO PROCEED | : | |
| CONTRACT DURATION | : | 450 calendar days |
| APPROVED BUDGET AMOUNT | : | ₱156,980,885.59 |
| SOURCE OF FUNDS | : | PPA CORPORATE BUDGET |
| IMPLEMENTING OFFICE | : | PPA - PORT CONSTRUCTION AND MAINTENANCE DEPARTMENT (PCMD) |
| ORIGINAL CONTRACT AMOUNT | : | ₱155,964,073.50 |
| EFFECTIVITY DATE | : | |
| ORIGINAL EXPIRY DATE | : | |


PROJECT STATUS :
(As of 25 September 2023)

REMARKS : - Bidding was conducted on 14 September
- 2023.
For post qualification of the lowest bidder.


OFFICER-IN-CHARGE :

CONTACT NUMBER :

EMAIL ADDRESS :



DEVELOPMENT PLAN





AFTER CONSTRUCTION
